

Manchester Memorial Elementary School Manchester-by-the-Sea, MA

MONTHLY CONSTRUCTION REPORT



Owner:

Manchester Essex Regional School
District
Manchester-by-the-Sea, MA

Owner's Project Manager:
Dore & Whittier Management Partners

Designer: JCJ Architecture Boston, MA

Construction Manager:

W. T. RICH COMPANY, INC.

29 Crafts Street, Suite 300

Newton, MA 02458

617-467-6010

December 2019

Manchester Memorial Elementary School Monthly Construction Report Summary – December 2019

TABLE OF CONTENTS

Section 1 - Project Schedule Update

- Project Schedule Update Summary
- Important Upcoming Milestones

Section 2 – Progress Photos

Section 3 – Attachments / Logs

- Project Schedule December Update
- 4 Week Look Ahead

Manchester Memorial Elementary School Monthly Construction Report Summary – December 2019

SECTION 2 - PROJECT SCHEDULE UPDATE

Summary:

Our attached schedule update has a data date of 12/31/19, so is inclusive of all progress through this date. Below are several notes in summary of progress and anticipated schedule, shown in our schedule update.

Permitting:

NGrid Easement Authorization signed by Board of Selectmen. Released into scheduling.

Phase 1 – Upcoming Critical Path Milestones (per Updated P6 Schedule):

MILESTONE ACTIVITY	TARGET COMPLETION	ACTUAL COMPLETION DATE
Slab-on Deck Pours Complete	11/27/19	11/26/19
Slab-on Grade Pours Complete	1/7/20	
Roof Complete (weather tight)/	1/20/20	12/30/19
AVB Complete	2/3/20	
2 nd Floor Rough-in	3/18/20	
1 st Floor Rough-in	4/7/20	

December Summary of Progress:


- Exterior Roof Edge Framing complete.
- Started Layout and Exterior Wall Framing.
- Main Roof Complete. Roofer to complete lower roof, blocking and curbs.
- Roof curbs, roof drains, sleeve penetrations, etc. to be completed prior to roof install.
- Roof Slabs poured.
- CMU Elevator shaft complete.

December Look Ahead:


- CMU Stair Shafts to be installed, followed by Stair #1 Erection.
- SOG to be poured.
- Exterior Framing and Sheathing to progress for start of AVB.
- Ready to start AVB.
- Mockup Schedule anticipated.
- Scheduling NGrid permanent power work order.
- Interior Rough-in to begin and proceed, starting with ductwork, interior wall framing, layout, etc.


Manchester Memorial Elementary School Monthly Construction Report Summary – December 2019

SECTION 2 - PROGRESS PHOTOS





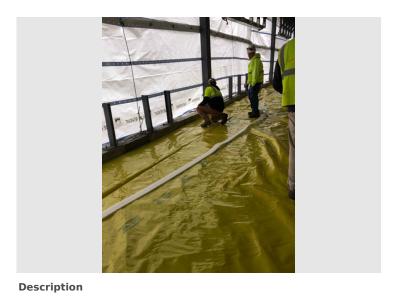

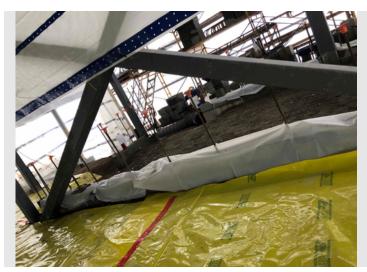

Description

Taken Date 2019/12/31 12:38:52

Upload Date 2019/12/31 12:38:55

Uploaded By Trishya Patel


File Name 635B2BB6-2CAE-4B1E-90A0-B0B... **Taken Date** 2019/12/31 12:38:47


Upload Date 2019/12/31 12:38:50 **Uploaded By** Trishya Patel

File Name

50A08990-6D37-41A7-AEF0-69FF...



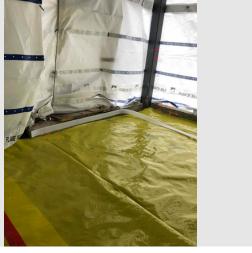

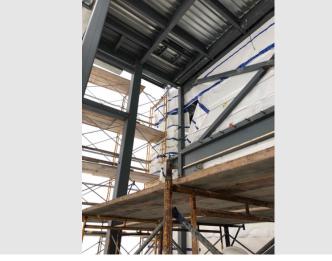

Description

Taken Date 2019/12/31 12:38:37

Description

2019/12/31 12:38:41

Upload Date

Uploaded By Trishya Patel

File Name 5C020BA0-6C83-4748-8420-F34... **Taken Date** 2019/12/31 10:24:20

Upload Date 2019/12/31 10:24:28 **Uploaded By** Trishya Patel

File Name

D0B91C22-CD6F-4F12-8700-1DD...



					MON TU	ES WED THUR FRI	AT SUN MON TUES WED THUR FRI SAT S 11 1/12 1/13 1/14 1/15 1/16 1/17 1/18	SUN MON TUES W	VED THUR FRI SAT SUN	MON TUES WED THUR FF	RI SAT SUN	MON TUES WEI	D THUR FRI 5	SAT SUN MON 2/8 2/9 2/10	TUES WED THUR 2/11 2/12 2/13	FRI SAT SUN
Milestone/Activity Description	Responsibility	First Delivery Initial Inspection	Start Date	End Date	1/0 1/	7 1/0 1/7 1/10		1/20 1/21 1	1/22 1/23 1/24 1/23 1/20	1/21 1/20 1/27 1/30 1/3		2/3 2/4 2/3	2/0 2/1	2/0 2/10	2/11 2/12 2/13	2/14 2/19 2/10
Building Interior - FIRST FLOOR																
Anneese Electric							w w	W	WW		ww			w		ww
Complete temp electric lights + power (roof tight)	SB		11/18/19	01/30/20	Х	X X X	w X X X X w	w X X	X X X w w	X X X X	w			w		w
Install UG pipe + inspection	SK		Complete	Complete			w w	w	w		w			w		w
E. Amanti & Sons Plumbing							w w	w	w		w			w		w
Complete UG + water service tie in+ inspected . DPW notified	SK	Completed	Complete	Complete			w w	W	w		w			w		w
JL Marshall							w w	w	www		w			w		w
Form column caps	SB	Not Required Completed	12/05/19	12/26/19			w w	W	www		w			w		w
Pour Stair 1 * maybe sooner	SB		01/27/20	01/27/20			w w	W	www	X	w			w		w
Install and inspect SOG vapor barrier + rebr and mesh	TP		12/26/19	01/07/20	X		w w	W	w		w			w		w
Hang angles at Curtain Wall , enbeds	TP		12/26/19	01/06/20	Х		w w	w	w		w			w		w
Boiler Room housekeeping pads * ck submittal/Boiler/ Hot water	SK		01/16/20	01/20/20			w w X X w	w X	w		w			w		w
Place SOG	TP		01/08/20	01/08/20		Х	w w	w	w		w			w		w
Water Cure slab	TP		01/08/20	01/14/20		X X X	w X X	w	w		w			w		w
Manganaro							w w	w	w		ww			w		ww
Framing Layout	SB	Not Required	01/16/20	01/15/20			w w	W	w		w			w		w
Marmelo							w w	w	www		W			w		w w
Stair CMU + Staging	JDB		01/13/20	01/22/20			w W X X X X W	w X X	X w w		w			w		w
United Civil							w w	w	www		W			w		w w
Prep area for SOG placement	SB		Complete	Complete			w w	W	w		w			w		w
Stellar Steel							w w	W	www		w			w		www
Weld cross braces, punch items, lintel adjustment. Latest punchlist?	JDB		01/08/20	01/15/20		x x x	w W X X X	W	www		w			w		w
Decking at eye brow windows			01/16/20	01/24/20												
CW support set and epoxy			Complete	Complete												
Elevator sizmic connection			01/16/20	01/24/20												
weld galvi angles at CW enbeds			01/16/20	01/24/20												
Stair #1 Steel - Lintels * after slab	JDB		01/08/20	01/24/20		X X X	w X X X W	w X X	X X w w		w			w		w
Misc Items																
Set Control first floor			01/15/20	01/15/20			w w	w	w		w			w		w
Building Interior - SECOND FLOOR																
Anneese Electric							w w	w	w		ww			w		ww
Temp power	SK		12/30/19	01/06/20	X		w w	w	w		w			w		w
Install main electricial conduit + tel Com	SK		12/23/19	12/27/19				w	w		w			w		w
Install switchgear(pending building tight) * pushed untill building tight	SK		TBD	TBD				W	w		w			w		w
E. Amanti & Sons Plumbing							w w	w	www		W			w		W
Beam penetrations for drains, stair #1 and overhang tie in	SK		TBD	TBD												
Roof drain piping	SK		12/11/19	12/24/19			w w	w	w		w			w		w
	1	J I		<u> </u>												



Milestone/Activity Description	Romansibility	First Dolivory	Initial Inspection	Start Data	M. Frid Data	ION TUES WEI 1/6 1/7 1/8	D THUR FRI 1/9 1/10	SAT SUN MON 7 1/11 1/12 1/13	TUES WED THUR 1/14 1/15 1/16	FRI SAT SUN 1/17 1/18 1/19	MON TUE 0 1/20 1/23	S WED THUR 1 1/22 1/23	FRI SAT SUN 1/24 1/25 1/26	MON TUES WED T 1/27 1/28 1/29	HUR FRI 1/30 1/31	SAT SU 2/1 2/	N MON 7 2 2/3	TUES WED 2/4 2/5	THUR FRI SA 2/6 2/7 2/	T SUN MON T 8 2/9 2/10 2	JES WED THUR F /11 2/12 2/13 2/	RI SAT SI /14 2/15 2
Pipe hangers	SK	<u>Pitst Denvery</u>	mitial inspection		01/15/20	x x x	ХХ	w w X	х х	ww			w			W	7			w		W
E. Amanti & Sons HVAC								ww		ww			w			W	7		V	w		w
Duct work Delivery 1/6	SK			01/06/20	02/20/20	x x x	х х	w w X	х х х	Xww	х х	х х	X w w	х х х	х х	W	X	х	X X	w X	х х х	X
Manganaro								w		ww			ww			w	7		, ,	w		w
LGMF Framing layout	JDB			Complete	Complete			ww		ww			ww			W	7			w		W
Exterior wall framing	SB			12/23/19	01/17/20	x x x	ХХ	w w X	х х х	X w w			w			W	7			W		W
Interior partitions	SB			01/02/20	1/124/2020	x x x	X X	w w X	x x x	X w w	Х Х	х х	X w w	x x x	X X	W	X	Х	XX	w X	х х х	X w
Safety, toe kick, 2nd floor egress	SB	Not Required	Completed	Complete	Complete			w		ww			w			W	7			W		W
Stellar								w		ww			w			W	7		V	w		w
Detailing	JDB			12/18/19	01/03/20			w		ww			w			W	7		, I	w		W
Weld brick lentals + inspection + repair of lintels	JDB			12/12/19	12/27/19			w		w			w			W				W		W
Elevator sizemic * Observation / RFI																						
Cogswell Sprinkler								w		w			w			W			V	W		W
Start 2nd floor rough Start Date. Duration?				01/27/20	01/27/20																	
Building EXTERIOR																						
Anneese Electric								w		w			w			W	7			w		W
Install Verizon conduit and electric ductbank Tied to UC digging	SB			TBD	TBD			w		w			w			W	7			w		W
Install Seconderies into building + inspection	SB			01/13/20	01/15/20			w w X	Х	W			w			W	7			w		W
E. Amanti & Sons								W		W			w			W	7			W		W
Install water service + test	TP	Completed	Completed	Complete	Complete			w		www			w			W	7			W		w
Cogswell Sprinkler								ww		ww			www			W	7		V	W		w
Install FP service + test ?	SK	Completed	Completed	12/19/19	12/20/19			ww		ww			w			W	7		V	W		w
Manganaro								w		w			w			W	7		V	W		w
Framing roof edge / Lower Roof at Stair 1	SB			12/24/19	01/10/20	x x x	X X	w		w			w			W	7			W		w
Frame Mockup	SB			TBD	TBD			w		ww			w			W	7			w		W
Frame Soffit	SB			12/18/19	01/10/20	X X X	X X	ww		WW			w			W				w		W
JL Marshall								w		WW			ww			W				w		w
Place oil containment ? On hodl	SB			TBD	TBD			w		WW			w			W	7			W		W
2nd placement of transformer pad Date guess with SOG	SB			TBD	TBD			w		WW			w			W				w		W
W.T. Rich								W		WW			WW			W	/			W		W
Clean site + maintain Enclosure	JDB			12/10/19	02/13/20	X X X	X X	w w X	X X X	X w w	X X	X X	X w w	X X X	Х Х	W	X	X X	X	w X	X X X	w
Temp drain overhang? + stair 1	SK			TBD	TBD			w		W			w			W				W		W
United Civil								WW		WW			ww			W			V	W		W
E&B for Verizon line	JDB			TBD	TBD			w		W			w			W	7			W		W
Flush + test Water main * date from UC	SK			TBD	TBD			www		WW			w			W	7			W		w
Prep transformer * after oil containment	SB			12/30/19	12/31/19			W		W			w			W				W		W
Prep Mockup	JDB			Omplete	Complete			w		w			w			W	7			w		W




						MON TU	ES WED THUR F 7 1/8 1/9 1/	RI SAT SUN M	MON TUES V	WED THUR F	RI SAT SU	N MON T	TUES WED	THUR FRI	SAT SUN	MON TUES WE	D THUR F	RI SAT	SUN N	MON TUES W	ED THUR F	RI SAT SUN MO	N TUES WED TH	UR FRI SAT
Milestone/Activity Description	Responsibility	<u>First Delivery</u>	Initial Inspection	Start Date		1/0 1/	7 1/8 1/9 1/	10 1/11 1/12 1/	1/13 1/14 .	1/15 1/16 1/	17 1/18 1/1	9 1/20	1/21 1/22	1/23 1/24	1/25 1/26	1/27 1/28 1/2	9 1/30 1/	51 2/1	2/2	2/3 2/4 2	5 2/6 2	7 2/8 2/9 2/	0 2/11 2/12 2/3	2/14 2/15
Maintain SWWP	TP			TBD	TBD			w			W				W W			W	W			ww		W
Helical																								
Install ground improvements + ramp	BP			TBD	TBD			W			ww				w w			W	W			ww		w
ROOF																								
W.T. Rich								ww			ww				W W			W	W			w w		N.
Clean snow	JDB							ww			ww				WW			W	W			ww		W
Spray spot welds with galvi spray PCO 8021	JDB			Complete	Complete										W W			150	****					
	JDB			Complete	Complete			W			W W				W			W	· · ·			W W		
Stanley Roofing								W			WW				W			W	W			WW		- W
Stair 1 roof	TP	Completed	Completed	01/22/20	01/22/20			W			W		X		W			W	W			W		W
Scuppers / Metal	TP	Completed	Completed	TBD	TBD			W			W				W			W	W			w		W
Upcomming Tasks																								
American Environmental				TBD	TBD			ww			ww				w w			W	W			ww		w
Clean out existing basement	SB/JDB			02/14/20	02/20/20			w			W				w w			W	w			w		X
Anneese Electric								ww			W				W			W	w			ww		W
Verizon Conduit to Manhole in the Street	SK			TBD	TBD			ww			ww				w w			W	W			ww		W
Survey & Layout existing building/all subs	SK			12/23/19	01/01/20			W			www				W W			W	W			NY NY		
				12, 23, 17	01/01/20										***				· · ·					
Install Temp Raceways * existing Building ?	SK																							
Install Tranformer, Generator Pad, Oil Containment (need Generator)	SK			12/02/19	12/27/19			W			W				W			W	W			W		W.
Helical																								
Install ground improvements west elevation	JDB			01/06/20	01/10/20	Х	X X	K w w			w				W			W	W			ww		w
Permanent Power	SK			02/01/20	02/15/20			w			w				W			W	W	X X		X w w X	x x x	Xw
Install New Gas Service (TBC - NGrid)	SK			Spring	Spring			w			w				W			W	W			ww		w
Permits / Sign-offs / C of Os/ Inspections		•																						
Foundation Permit				Complete	Complete			w			W				W W			W	W			w		w
Building Permit				Complete	Complete			ww			ww				W W			W	W			ww		W
Holiday's - NO WORK - 12/25, 1/1								ww			ww				W W			W	W			w		W
No school - WORK but NO KIDS, 12/23-1/3, 1/17, 2/27-2/21								w			ww				W			W	W			w		W
1/2 day - WORK but HALF DAY FOR KIDS, 12/4								W			W				W			W	W			W		W
Quality Control						<u> </u>																		
Preinstallation Meetings	ITTO							W			W				W			W	W			W		W
Steel	JTC			Complete	Complete			W			W				W			W	W			W		W
Decking	JTC			Complete	Complete			W			W				W			W	W			W W		
Welds	JTC			Complete	Complete			W			W				W			W	W			W		
Shear Studs Ethal Study	JTC			Complete	Complete			W			W				W			W	W			W		
Final inspection welds after SOD & SOR All SS	JTC			12/13/19	12/26/19			W			W				W			W	W			W		
First Delivery Inspections	<u> </u>							W			W				W			W	W			W		
Initial and Follow-Up Inspections (Review of Workmanship and Procedures)								W			W				W			Ŵ	W			W		W
Concrete D. L								W			W				W			W	W			W		
Rebar								W			W				W			W	W			W		
Subcontractor Meetings - Every Thursday AM @ 8:00AM								W			W				W			W	W			W		
								W			W				W			W	W			W		W

W.T. Rich Company - Look Ahead Schedule


			5
		1	
9			
		9	

						MON TUES	WED THUR FRI S	AT SUN	MON TUES WED THUR FI	RI SAT SUN	MON TUES	WED	THUR FRI	SAT	SUN MON	TUES WE	D THUR I			N TUES WE	D THUR F	RI SAT SU	JN MON TUI	ES WED 7	THUR FRI S	SAT SUN
Milestone/Activity Description	Rosponsibility	First Daliyary	<u>Initial Inspection</u>	Start Data	End Data	1/6 1/7	1/8 1/9 1/10 1	/11 1/12	1/13 1/14 1/15 1/16 1/	17 1/18 1/19	1/20 1/21	1/22	1/23 1/24	1/25	1/26 1/27	1/28 1/2	9 1/30 1	/31 2/1	2/2 2/3	2/4 2/5	5 2/6 2	7 2/8 2	/9 2/10 2/1	1 2/12	2/13 2/14 2	/15 2/16
Safety	Responsibility	rust Denvery	mitial Hispection	Start Date	<u>End Date</u>																					
Orientations - On Going as Needed with New Hires								w		w				W	W			w	W			W	W			w
CORI Check- On Going as Needed with New Hires								w		w				W	W			w	w			w	w			w
ConstructSecure Safety Inspections (min 1 per Week)								w		ww				W	W			W	W			W	w			W

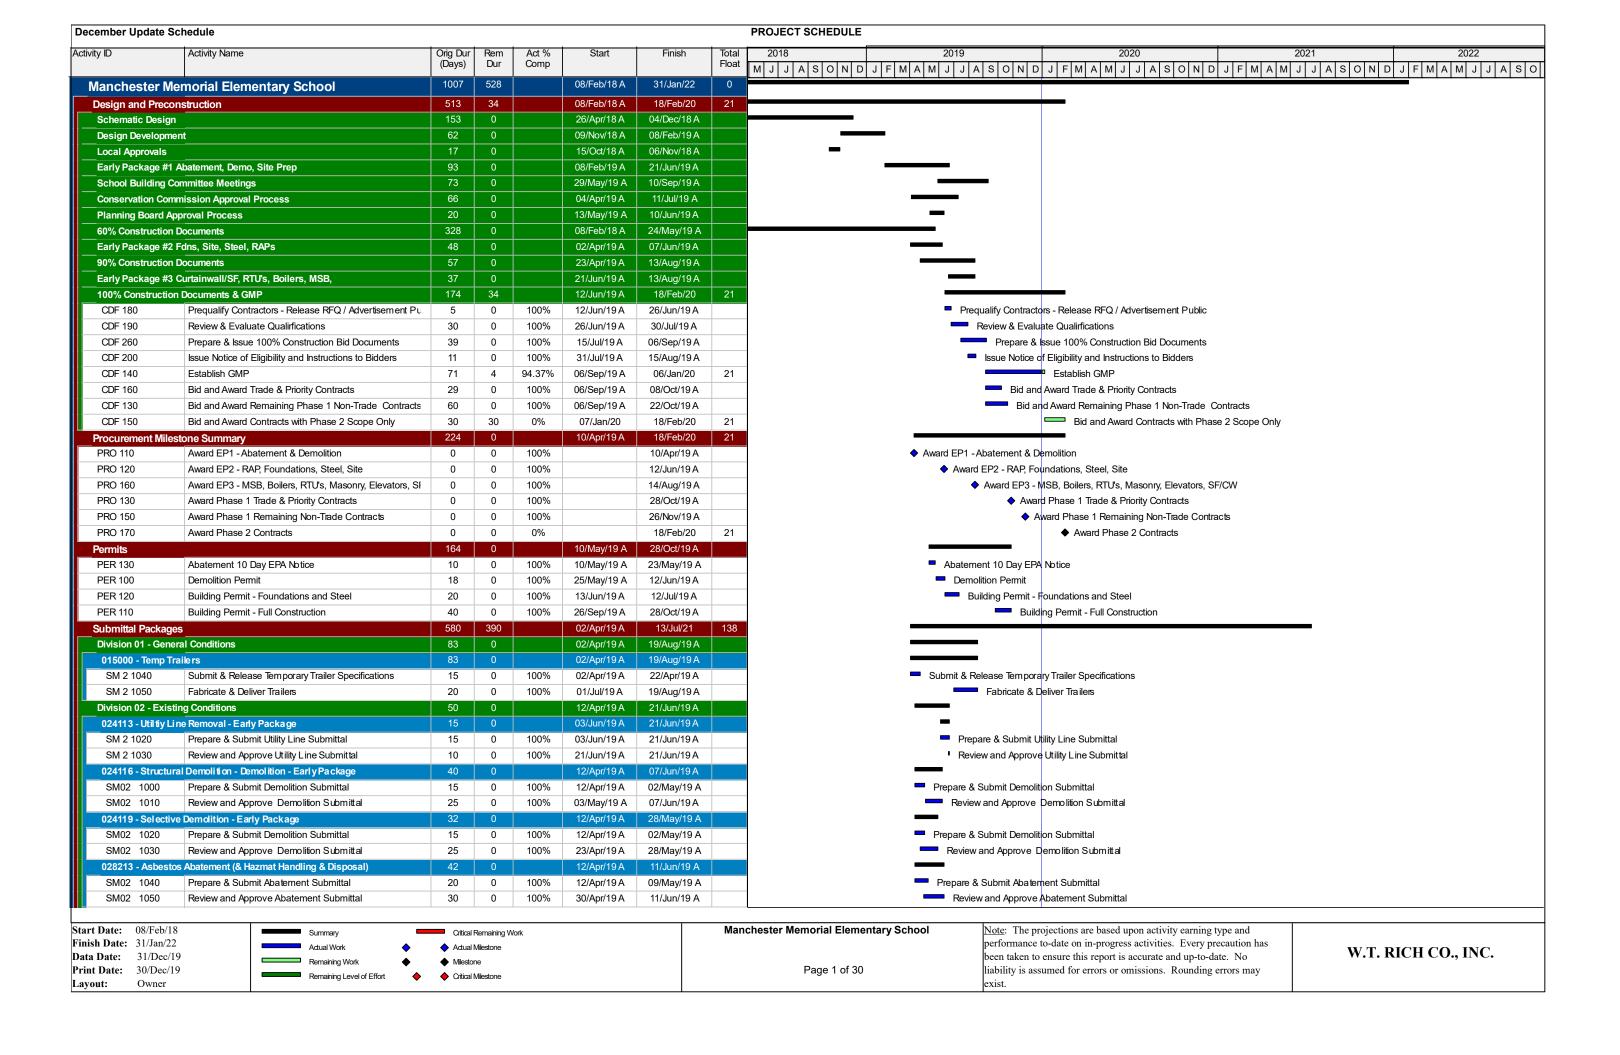

ember Update S	Activity Name	Orig Dur	Rem	Act %	Start	Finish	Total	PROJECT SCHEDULE 2018 2019 2020 2021 2022
	reducty reality	(Days)	Dur	Comp	Otart	Tillori	Float	M
Division 03 - Conc	rete & Reinforcement	216	45		18/Jun/19 A	21/Apr/20	84	
033000 Phase 1 -	- Cast-In-Place Concrete	49	0		18/Jun/19 A	30/Aug/19 A		
SM 3 1000	Prepare and Submit Concrete Package	15	0	100%	18/Jun/19 A	22/Jul/19 A		Prepare and Submit Concrete Package
SM 3 1010	Review and Approve Concrete Package	15	0	100%	18/Jul/19 A	02/Aug/19 A		Review and Approve Concrete Package
SM 3 1020	Fabricate & Deliver Steel Reinforcement	15	0	100%	05/Aug/19 A	30/Aug/19 A		Fabricate & Deliver Steel Reinforcement
_	- Cast-In-Place Concrete	45	45		19/Feb/20	21/Apr/20	84	
SM 3 1030	Prepare and Submit Concrete Package	15	15	0%	19/Feb/20	10/Mar/20	84	Prepare and Submit Concrete Package
SM 3 1040	Review and Approve Concrete Package	15	15	0%	11/Mar/20*	31/Mar/20	84	Review and Approve Concrete Package
SM 3 1050	Fabricate & Deliver Steel Reinforcement	15	15	0%	01/Apr/20	21/Apr/20	84	Fabricate & Deliver Steel Reinforcement
Division 04 - Maso	-	124	30		03/Sep/19 A	11/Feb/20	236	
_	1 CMU (Stair & Elevator Shaft)	63	0		03/Sep/19 A	29/Nov/19 A		
SM04 1060	Prepare and Submit Package CMU	20	0	100%	03/Sep/19 A	04/Nov/19 A		Prepare and Submit Package CMU
SM04 1070	Review and Approve Package CMU	19	0	100%	22/Oct/19 A	15/Nov/19 A		Review and Approve Package CMU
SM04 1080	Fabricate and Deliver CMU and Reinforcement	9	0	100%	18/Nov/19 A	29/Nov/19 A		Fabricate and Deliver CMU and Reinforcement
	2 CMU (Stair & Elevator Shaft)	113	30	1000/	03/Sep/19 A	11/Feb/20	236	
SM04 1090	Prepare and Submit Package CMU	20	0	100%	03/Sep/19 A	30/Sep/19 A		Prepare and Submit Package CMU
SM04 1100	Review and Approve Package CMU	20	0	100%	30/Sep/19 A	31/Dec/19	236	Review and Approve Package CMU
SM04 1110	Fabricate and Deliver CMU and Reinforcement	30	30	0%	31/Dec/19	11/Feb/20	236	Fabricate and Deliver CMU and Reinforcement
042613 - Masonr	•	88	24	4000	16/Sep/19 A	03/Feb/20	10	
SM04 1000	Prepare and Submit Package Masonry Veneer	20	0	100%	16/Sep/19 A	23/Sep/19 A		Prepare and Submit Package Masonry Veneer
SM04 1010	Review and Approve Package Masonry Veneer	15	0	100%	14/Oct/19 A	08/Nov/19 A		Review and Approve Package Masonry Veneer
SM04 1020	Fabricate and Deliver Masonry Veneer	55	24	56.36%	31/Oct/19 A	03/Feb/20	10	Fabricate and Deliver Masonry Veneer
042613 - Concre		72	0		03/Sep/19 A	03/Dec/19 A		
SM04 1030	Prepare and Submit Package Decorative CMU	20	0	100%	03/Sep/19 A	30/Sep/19 A		Prepare and Submit Package Decorative CMU
SM04 1040	Review and Approve Package Decorative CMU	20	0	100%	30/Sep/19 A	31/Oct/19 A		Review and Approve Package Decorative CMU
SM04 1050	Fabricate and Deliver CMU and Reinforcement	30	0	100%	31/Oct/19 A	03/Dec/19 A		Fabricate and Deliver CMU and Reinforcement
_047200 - Cast Sto		105	24		30/Sep/19 A	03/Feb/20	10	
SM 4 1000	Prepare and Submit Package Cast Stone Masonry	20	0	100%	30/Sep/19 A	18/Oct/19 A		Prepare and Submit Package Cast Stone Masonry
SM 4 1020	Review and Approve Package Cast Stone Masonry	20	0	100%	11/Nov/19 A	09/Dec/19 A		Review and Approve Package Cast Stone Masonry
SM 4 1040	Fabricate and Deliver Unit Masonry Cast Stone Masonry	60	24	60%	03/Dec/19 A	03/Feb/20	10	Fabricate and Deliver Unit Masonry Cast Stone Masonry
Division 05 - Metal	<u> </u>	242	192		10/Jun/19 A	30/Sep/20	336	
	I (Area A) Anchor Bolts	242	0	4000/	13/Jun/19 A	16/Aug/19 A		Province and Outlook Distance Analysis Distance
SM 5 1310	Prepare and Submit Package Anchor Bolts	9	0	100%	13/Jun/19 A	28/Jun/19 A		Prepare and Submit Package Anchor Bolts
SM 5 1320	Review and Approve Package Anchor Bolts	15	0	100%	01/Jul/19 A	22/Jul/19 A		Review and Approve Package Anchor Bolts
SM 5 1330	Fabricate and Deliver Structural Anchor Bolts	15	0	100%	01/Aug/19 A	16/Aug/19 A	400	Fabricate and Deliver Structural Anchor Bolts
_	2 (Area B&C) Anchor Bolts	172	30	4000/	28/Oct/19 A	11/Feb/20	132	Decrease and Order's Declarate Analysis Delta
SM 5 1420	Prepare and Submit Package Anchor Bolts	9	0	100%	28/Oct/19 A	31/Dec/19	132	Prepare and Submit Package Anchor Bolts
SM 5 1430	Review and Approve Package Anchor Bolts	15	15	0%	31/Dec/19	21/Jan/20	132	Review and Approve Package Anchor Bolts
SM 5 1440	Fabricate and Deliver Structural Anchor Bolts	15	15	0%	22/Jan/20	11/Feb/20	132	Fabricate and Deliver Structural Anchor Bolts
_	Structural Steel Framing	98	0	1000/	10/Jun/19 A	28/Oct/19 A		Droppers and Cultural Designational Charles
SM 5 1000	Prepare and Submit Package Structural Steel	30	0	100%	10/Jun/19 A	01/Aug/19 A		Prepare and Submit Package Structural Steel
SM 5 1060	Review and Approve Package Structural Steel	24	0	100%	01/Aug/19 A	30/Sep/19 A		Review and Approve Package Structural Steel
SM 5 1160	Fabricate and Deliver Structural Steel Framing	35	172	100%	09/Sep/19 A	28/Oct/19 A	20	Fabricate and Deliver Structural Steel Framing
_	2 (Area B&C) Structural Steel Framing	98	172	40001	10/Jun/19 A	01/Sep/20	26	Decree and Other to Decree
SM 5 1450	Prepare and Submit Package Structural Steel	30	0	100%	10/Jun/19 A	01/Aug/19 A		Prepare and Submit Package Structural Steel
SM 5 1460	Review and Approve Package Structural Steel	24	172	100%	01/Aug/19 A	30/Sep/19 A	200	Review and Approve Package Structural Steel
SM 5 1470	Fabricate and Deliver Structural Steel Framing	35	172	0%	09/Sep/19 A	01/Sep/20	26	Fabricate and Deliver Structural Steel Framing
051500 - Stud Sh		110	0	40001	13/Jun/19 A	31/Oct/19 A		Design of Access Design of Access of Design of
SM 5 1080	Review and Approve Package Steel Joists	20	0	100%	13/Jun/19 A	06/Sep/19 A		Review and Approve Package Steel Joists
SM 5 1020	Prepare and Submit Package Steel Joists	20	0	100%	01/Jul/19 A	19/Aug/19 A		Prepare and Submit Package Steel Joists
SM 5 1170	Fabricate and Deliver Stud Shear Connectors	50	0	100%	09/Sep/19 A	31/Oct/19 A		Fabricate and Deliver Stud Shear Connectors
	I (Area A) Steel Decking	110	0	4000	13/Jun/19 A	28/Oct/19 A		
_	Prepare and Submit Package Steel Decking	20	0	100%	13/Jun/19 A	09/Aug/19 A		Prepare and Submit Package Steel Decking
053100 - Phase 1 SM 5 1040							Man	chester Memorial Elementary School Note: The projections are based upon activity earning type and
SM 5 1040 Date: 08/Feb/18	Currinary	Critical	Remaining W	/ork				
SM 5 1040 Date: 08/Feb/18 h Date: 31/Jan/22	2 Adual Work	Critical	-	/ork			ar	performance to-date on in-progress activities. Every precaution has
_	Actual Work		Milestone one	/ork				

rity ID	Activity Name	Orig Dur	Rem	Act %	Start	Finish	Total	2018 2019 2020 2021 2022
ity iD	Activity Name	(Days)	Dur	Comp	Otart	I IIIIoii	Float	
SM 5 1100	Review and Approve Package Steel Decking	20	0	100%	12/Aug/19 A	09/Sep/19 A		Review and Approve Package Steel Decking
SM 5 1180	Fabricate and Deliver Steel Decking	49	0	100%	10/Sep/19 A	28/Oct/19 A		Fabricate and Deliver Steel Decking
053100 - Phase	2 (Area B&C) Steel Decking	110	192		13/Jun/19 A	30/Sep/20	21	
SM 5 1480	Prepare and Submit Package Steel Decking	20	0	100%	13/Jun/19 A	09/Aug/19 A		Prepare and Submit Package Steel Decking
SM 5 1490	Review and Approve Package Steel Decking	20	0	100%	12/Aug/19 A	09/Sep/19 A		Review and Approve Package Steel Decking
SM 5 1500	Fabricate and Deliver Steel Decking	49	192	0%	10/Sep/19 A	30/Sep/20	21	Fabricate and Deliver Steel Decking
<u> </u>	ormed Metal Framing	35	0		22/Oct/19 A	05/Dec/19 A		
SM 5 1140	Prepare and Submit Package Metal Framing	25	0	100%	22/Oct/19 A	15/Nov/19 A		Prepare and Submit Package Metal Framing
SM 5 1210	Review and Approve Package Metal Framing	5	0	100%	15/Nov/19 A	29/Nov/19 A		Review and Approve Package Metal Framing
SM 5 1250	Fabricate and Deliver Cold Formed Metal Framing	4	0	100%	29/Nov/19 A	05/Dec/19 A		Fabricate and Deliver Cold Formed Metal Framing
_	1 (Area A) Metal Fabrications	79	31	050/	22/Oct/19 A	12/Feb/20	3	Province and October 1 Produces Make I False
SM 5 1130	Prepare and Submit Package Metal Fabs	20	1	95%	22/Oct/19 A	31/Dec/19	3	Prepare and Submit Package Metal Fabs
SM 5 1220	Review and Approve Package Metal Fabs	10	10	0%	02/Jan/20	15/Jan/20	3	Review and Approve Package Metal Fabs
SM 5 1260	Fabricate and Deliver Metal Fabrications	20	20	0%	16/Jan/20	12/Feb/20	3	Fabricate and Deliver Metal Fabrications
_	2 (Area B&C) Metal Fabrications	113	65	00/	22/Oct/19 A	01/Apr/20	463	Province and October Produces Make Follows
SM 5 1510	Prepare and Submit Package Metal Fabs	20	20	0%	22/Oct/19 A	28/Jan/20	463	Prepare and Submit Package Metal Fabs
SM 5 1520 SM 5 1530	Review and Approve Package Metal Fabs Fabricate and Deliver Metal Fabrications	20 25	20 25	0% 0%	29/Jan/20 27/Feb/20	26/Feb/20 01/Apr/20	463 463	Review and Approve Package Metal Fabs Fabricate and Deliver Metal Fabrications
	1 Metal Pan Stairs		25	U 70		07/Nov/19 A	400	Fabilicate aliu Delivei ivietai Fabilications
SM 5 1150	Prepare and Submit Package Metal Stairs & Railings	29	0	100%	23/Sep/19 A 23/Sep/19 A	27/Sep/19 A		Prepare and Submit Package Metal Stairs & Railings
SM 5 1190	Review and Approve Package Metal Stairs & Pailings	10	0	100%	01/Oct/19 A	14/Oct/19 A		Review and Approve Package Metal Stairs & Railings
SM 5 1300	Fabricate and Deliver Metal Stairs	10	0	100%	22/Oct/19 A	07/Nov/19 A		Fabricate and Deliver Metal Stairs
055113 - Phase		107	53	10070	10/Oct/19 A	16/Mar/20	41	Tabilitate and Deliver Wetai Stails
SM 5 1540	Prepare and Submit Package Metal Railings	60	28	53.33%	10/Oct/19 A	07/Feb/20	41	Prepare and Submit Package Metal Railings
SM 5 1550	Review and Approve Package Metal Railings	10	10	0%	10/Feb/20	24/Feb/20	41	Review and Approve Package Metal Railings
SM 5 1560	Field Measure and Release	5	5	0%	25/Feb/20	02/Mar/20	41	Field Measure and Release
SM 5 1570	Fabricate and Deliver Metal Railings	10	10	0%	03/Mar/20	16/Mar/20	41	□ Fabricate and Deliver Metal Railings
	2 Metal Pan Stairs	104	50	070	14/Oct/19 A	11/Mar/20	478	Tublicate and Bollyof Motal Fallings
SM 5 1370	Prepare and Submit Package Metal Stairs & Railings	20	10	50%	14/Oct/19 A	14/Jan/20	478	Prepare and Submit Package Metal Stairs & Railings
SM 5 1400	Field Meassure Floor Heights	3	3	0%	31/Dec/19	03/Jan/20	515	Field Meassure Floor Heights
SM 5 1410	Fabricate Field Measured Items and Deliver Metal Stairs	10	10	0%	06/Jan/20	17/Jan/20	515	□ Fabricate Field Measured Items and Deliver Metal Stairs & Railings
SM 5 1380	Review and Approve Package Metal Stairs & Railings	25	25	0%	15/Jan/20	19/Feb/20	478	Review and Approve Package Metal Stairs & Railings
SM 5 1390	Fabricate Stock Sized Items and Deliver	15	15	0%	20/Feb/20	11/Mar/20	478	□ Fabricate Stock Sized Items and Deliver
	nd Tube Railings	108	60		22/Oct/19 A	25/Mar/20	468	
SM 5 1270	Prepare and Submit Package Metal Stairs & Railings	20	20	0%	22/Oct/19 A	28/Jan/20	125	Prepare and Submit Package Metal Stairs & Railings
SM 5 1280	Review and Approve Package Metal Stairs & Railings	15	15	0%	29/Jan/20	19/Feb/20	468	Review and Approve Package Metal Stairs & Railings
SM 5 1290	Fabricate and Deliver Metal Stairs & Railings	25	25	0%	20/Feb/20	25/Mar/20	468	Fabricate and Deliver Metal Stairs & Railings
Division 06 - Woo	d, Plastics and Composites	447	390		09/Oct/19 A	13/Jul/21	138	
061053 - Misc C	arpentry	59	10		09/Oct/19 A	14/Jan/20	518	
SM 6 1000	Prepare and Submit Package Rough Carpentry	15	0	100%	09/Oct/19 A	12/Nov/19 A		Prepare and Submit Package Rough Carpentry
SM 6 1010	Review and Approve Package Rough Carpentry	15	0	100%	12/Nov/19 A	03/Dec/19 A		Review and Approve Package Rough Carpentry
SM 6 1070	Fabricate and Deliver Rough Carpentry	20	10	50%	04/Dec/19 A	14/Jan/20	518	Fabricate and Deliver Rough Carpentry
061533 - Wood F	Patio Decking	296	296		31/Dec/19	01/Mar/21	30	
SM 6 1220	Prepare and Submit Package Wood Patio Decking	20	20	0%	31/Dec/19	28/Jan/20	30	Prepare and Submit Package Wood Patio Decking
SM 6 1230	Review and Approve Package Wood Patio Decking	40	40	0%	29/Jan/20	25/Mar/20	30	Review and Approve Package Wood Patio Decking
SM 6 1240	Fabricate and Deliver Wood Patio Decking	236	236	0%	26/Mar/20	01/Mar/21	30	Fabricate and Deliver Wood Patio Decking
061600 - Sheath	ing	29	0		22/Oct/19 A	20/Dec/19 A		
SM 6 1020	Prepare and Submit Package Sheathing	15	0	100%	22/Oct/19 A	12/Nov/19 A		Prepare and Submit Package Sheathing
SM 6 1060	Review and Approve Package Sheathing	9	0	100%	12/Nov/19 A	22/Nov/19 A		Review and Approve Package Sheathing
SM 6 1080	Fabricate and Deliver Sheathing	5	0	100%	25/Nov/19 A	20/Dec/19 A		Fabricate and Deliver Sheathing
061850 - Glue La	aminated Timber Beams	356	356		19/Feb/20	13/Jul/21	66	
SM 6 1030	Prepare and Submit Package Glue Laminated Timber Be	306	306	0%	19/Feb/20	30/Apr/21	66	Prepare and Submit Package Glue Laminated Timber
SM 6 1100	Review and Approve Package Glue Laminated Timber B	20	20	0%	03/May/21	28/May/21	66	Review and Approve Package Glue Laminated Tim
Date: 08/Feb/1	8 Summary	(ritical	Remaining W	fork			Man	chester Memorial Elementary School Note: The projections are based upon activity earning type and
sh Date: 31/Jan/2	Carrinary	Adual	-	o.n				performance to-date on in-progress activities. Every precaution has
Date: 31/Dec/	19 Remaining Work	◆ Milesto						been taken to ensure this report is accurate and up-to-date. No W.T. RICH CO., INC.
t Date: 30/Dec/	10 ¥	-						Page 3 of 30 liability is assumed for errors or omissions. Rounding errors may

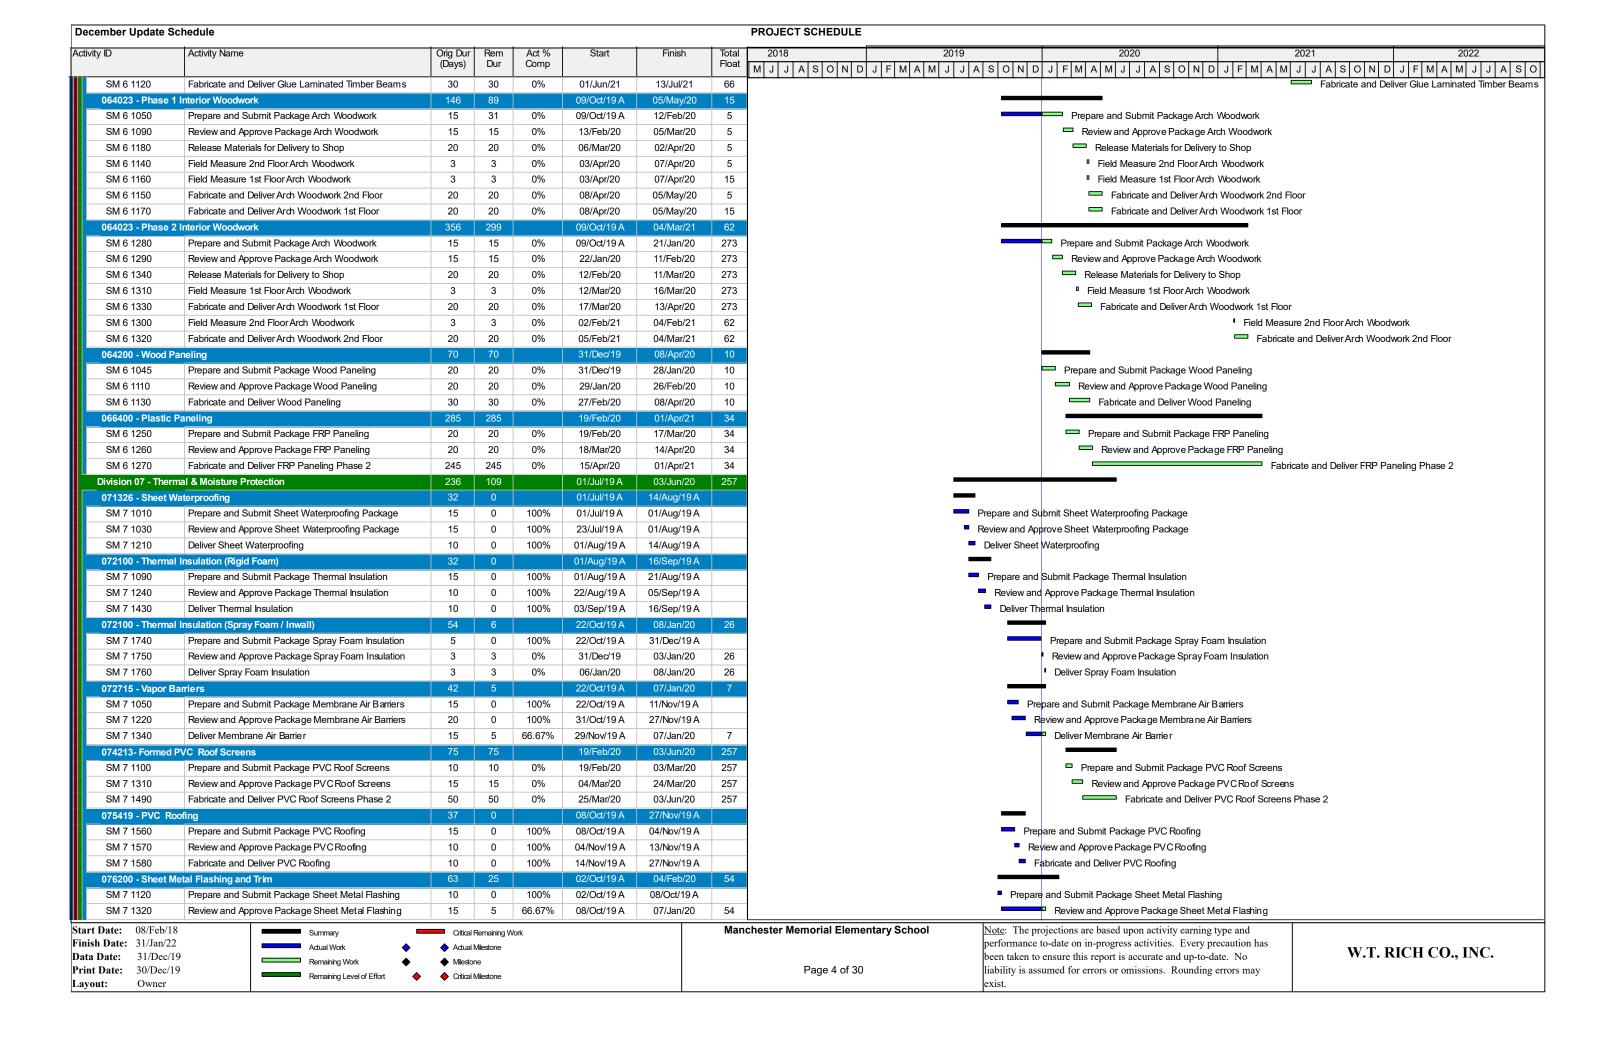

ity ID	Activity Name	Oria Dur	Dom	Act 0/	Stort	Einich	Total	2019 2010 2020 2021
IJ	Activity Name	Orig Dur (Days)	Rem Dur	Act % Comp	Start	Finish	Total Float	2018 2019 2020 2021 2022 MJJJASONDJFMAMJJJASONDJFMAMJJJASONDJFMAMJJJ
SM 7 1500	Fabricate and Deliver Sheet Metal Flashing & Trim	20	20	0%	08/Jan/20	04/Feb/20	54	☐ Fabricate and Deliver Sheet Metal Flashing & Trim
77100 - Roof Sp	pecialties	114	60		14/Oct/19 A	25/Mar/20	14	
SM 7 1150	Prepare and Submit Package Roof Specialties	20	20	0%	14/Oct/19 A	28/Jan/20	14	Prepare and Submit Package Roof Specialties
SM 7 1350	Review and Approve Package Roof Specialties	20	20	0%	29/Jan/20	26/Feb/20	14	Review and Approve Package Roof Specialties
SM 7 1510	Fabricate and Deliver Roof Specialties	20	20	0%	27/Feb/20	25/Mar/20	14	Fabricate and Deliver Roof Specialties
77129 - Manufa	cturered Roof Expansion Joints	42	0		01/Oct/19 A	27/Nov/19 A		
SM 7 1770	Prepare and Submit Package Roof Expansion Joints	15	0	100%	01/Oct/19 A	21/Oct/19 A		Prepare and Submit Package Roof Expansion Joints
SM 7 1780	Review and Approve Package Roof Expansion Joints	15	0	100%	08/Oct/19 A	31/Oct/19 A		Review and Approve Package Roof Expansion Joints
SM 7 1790	Fabricate and Deliver Roof Expansion Joints	20	0	100%	31/Oct/19 A	27/Nov/19 A		Fabricate and Deliver Roof Expansion Joints
77200 - Roof Ad	ccessories	85	44		31/Oct/19 A	03/Mar/20	35	
SM 7 1160	Prepare and Submit Package Roof Accessories	14	14	0%	31/Oct/19 A	20/Jan/20	35	Prepare and Submit Package Roof Accessories
SM 7 1360	Review and Approve Package Roof Accessories	10	10	0%	21/Jan/20	03/Feb/20	35	Review and Approve Package Roof Accessories
SM 7 1520	Fabricate and Deliver Roof Accessories	20	20	0%	04/Feb/20	03/Mar/20	35	Fabricate and Deliver Roof Accessories
78413 - Penetra	ation Firestopping	76	35		31/Oct/19 A	19/Feb/20	3	
SM 7 1620	Prepare and Submit Package Penetration Firestopping	10	10	0%	31/Oct/19 A	14/Jan/20	3	Prepare and Submit Package Penetration Firestopping
SM 7 1630	Review and Approve Package Penetration Firestopping	15	15	0%	15/Jan/20	04/Feb/20	3	Review and Approve Package Penetration Firestopping
SM 7 1640	Fabricate and Deliver Penetration Firestopping	10	10	0%	05/Feb/20	19/Feb/20	3	□ Fabricate and Deliver Penetration Firestopping
78446 - Fire Re	sistive Joints	76	35		31/Oct/19 A	19/Feb/20	3	
SM 7 1650	Prepare and Submit Package Fire Resistant Joints	10	10	0%	31/Oct/19 A	14/Jan/20	3	Prepare and Submit Package Fire Resistant Joints
SM 7 1660	Review and Approve Package Fire Resistant Joints	15	15	0%	15/Jan/20	04/Feb/20	3	Review and Approve Package Fire Resistant Joints
SM 7 1670	Fabricate and Deliver Fire Resistant Joints	10	10	0%	05/Feb/20	19/Feb/20	3	□ Fabricate and Deliver Fire Resistant Joints
79200 - Joint S	ealants	40	40		31/Dec/19	26/Feb/20	54	
SM 7 1680	Prepare and Submit Package Joint Sealants	10	10	0%	31/Dec/19	14/Jan/20	54	Prepare and Submit Package Joint Sealants
SM 7 1690	Review and Approve Package Joint Sealants	15	15	0%	15/Jan/20	04/Feb/20	54	Review and Approve Package Joint Sealants
SM 7 1700	Fabricate and Deliver Joint Sealants	15	15	0%	05/Feb/20	26/Feb/20	54	Fabricate and Deliver Joint Sealants
79500 - Expans	sion Control	40	40		31/Dec/19	26/Feb/20	200	
SM 7 1710	Prepare and Submit Package Expansion Control	10	10	0%	31/Dec/19	14/Jan/20	200	Prepare and Submit Package Expansion Control
SM 7 1720	Review and Approve Package Expansion Control	15	15	0%	15/Jan/20	04/Feb/20	200	Review and Approve Package Expansion Control
SM 7 1730	Fabricate and Deliver Expansion Control Phase 2	15	15	0%	05/Feb/20	26/Feb/20	200	Fabricate and Deliver Expansion Control Phase 2
ivision 08 - Oper	nings	423	340		15/Aug/19 A	30/Apr/21	188	
81113 - Hollow	Metal Doors & Frames	114	60		14/Oct/19 A	25/Mar/20	468	
SM 8 1110	Prepare and Submit Package HM Doors & Frames	20	0	100%	14/Oct/19 A	01/Nov/19 A		Prepare and Submit Package HM Doors & Frames
SM 8 1210	Review and Approve Package HM Doors & Frames	30	0	100%	04/Nov/19 A	22/Nov/19 A		Review and Approve Package HM Doors & Frames
SM 8 1230	Fabricate and Delivery Masonry HM Door Frames	20	0	100%	04/Nov/19 A	05/Dec/19 A		Fabricate and Delivery Masonry HM Door Frames
SM 8 1270	Fabricate and Deliver HM Door Frames	20	0	100%	25/Nov/19 A	31/Dec/19	528	Fabricate and Deliver HM Door Frames
SM 8 1280	Fabricate and Deliver HM Doors	60	60	0%	31/Dec/19	25/Mar/20	41	Fabricate and Deliver HM Doors
)81416 - Flush V	Vood Doors	85	85		31/Dec/19	29/Apr/20	16	
SM 8 1120	Prepare and Submit Package Flush Wood Doors	5	5	0%	31/Dec/19	07/Jan/20	16	Prepare and Submit Package Flush Wood Doors
SM 8 1220	Review and Approve Package Flush Wood Doors	20	20	0%	08/Jan/20	04/Feb/20	16	Review and Approve Package Flush Wood Doors
SM 8 1290	Fabricate and Deliver Flush Wood Doors	60	60	0%	05/Feb/20	29/Apr/20	16	Fabricate and Deliver Flush Wood Doors
83323 - Access	Doors & Frames	45	45		31/Dec/19	04/Mar/20	3	
SM8 1090	Prepare and Submit Package Access Doors	5	5	0%	31/Dec/19	07/Jan/20	3	 Prepare and Submit Package Access Doors
SM8 1100	Review and Approve Package Access Doors	10	10	0%	08/Jan/20	21/Jan/20	3	Review and Approve Package Access Doors
SM8 1110	Fabricate and Deliver Access Doors	30	30	0%	22/Jan/20	04/Mar/20	3	Fabricate and DeliverAcœss Doors
)83323 - Coiling	Doors	306	306		19/Feb/20	30/Apr/21	26	
SM8 1000	Prepare and Submit Package Overhead Coiling Doors	15	15	0%	19/Feb/20	10/Mar/20	26	Prepare and Submit Package Overhead Coiling Doors
SM8 1010	Review and Approve Package Overhead Coiling Doors	15	15	0%	11/Mar/20	31/Mar/20	26	Review and Approve Package Overhead Coiling Doors
SM8 1020	Fabricate and Deliver Coiling Doors Phase 2	276	276	0%	01/Apr/20	30/Apr/21	26	Fabricate and Deliver Coiling Doors Phase 2
84113 Aluminur	m Entrances	132	50		19/Aug/19 A	11/Mar/20	24	
SM 8 1020	Prepare and Submit Package Storefronts	25	0	100%	19/Aug/19 A	25/Sep/19 A		Prepare and Submit Package Storefronts
SM 8 1080	Review and Approve Package Storefronts	25	0	100%	26/Sep/19 A	31/Oct/19 A		Review and Approve Package Storefronts
SM 8 1180	Fabricate and Deliver Storefront & Entrance Frames	90	50	44.44%	31/Oct/19 A	11/Mar/20	24	Fabricate and Deliver Storefront & Entrance Frames
84113 Phase 1	Storefront Windows	122	40		03/Sep/19 A	26/Feb/20	34	
ate: 08/Feb/1	8 Summary	Critical	Remaining \\	ork		I	Man	nester Memorial Elementary School Note: The projections are based upon activity earning type and
Date: 31/Jan/22	Currinary	Actual	-	OI N				performance to-date on in-progress activities. Every precaution has
ate: 31/Dec/1	19 Remaining Work	Milesto						been taken to ensure this report is accurate and up-to-date. No W.T. RICH CO., INC.
Date: 30/Dec/1	19 Remaining Level of Effort	•	Milestone					Page 5 of 30 liability is assumed for errors or omissions. Rounding errors may
: Owner	Nemainid Level of Lifott	VIII(dai						exist.

ivity ID	Activity Name	Orig Dur		Act %	Start	Finish	Total	2018 2019 2020 2021 2022
		(Days)	Dur	Comp			Float	M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A
SM 8 1330	Prepare and Submit Package Storefront Windows	25	0	100%	03/Sep/19 A	18/Sep/19 A		Prepare and Submit Package Storefront Windows
SM 8 1340	Review and Approve Package Storefront Windows	25	0	100%	19/Sep/19 A	02/Oct/19 A		Review and Approve Package Storefront Windows
SM 8 1350	Fabricate and Deliver Storefront Windows Frames	80	40	50%	31/Oct/19 A	26/Feb/20	34	Fabricate and Deliver Storefront Windows Frames
084113 Phase 2	Storefront Windows	114	40		03/Sep/19 A	26/Feb/20	34	
SM 8 1390	Prepare and Submit Package Storefront Windows	25	0	100%	03/Sep/19 A	18/Sep/19 A		Prepare and Submit Package Storefront Windows
SM 8 1400	Review and Approve Package Storefront Windows	25	0	100%	19/Sep/19 A	02/Oct/19 A		Review and Approve Package Storefront Windows
SM 8 1410	Fabricate and Deliver Storefront Windows Frames	80	40	50%	21/Oct/19 A	26/Feb/20	34	Fabricate and Deliver Storefront Windows Frames
084113 Phase 1	Interior Storefront	102	80		01/Oct/19 A	22/Apr/20	21	
SM 8 1300	Prepare and Submit Package Interior Storefronts	25	0	100%	01/Oct/19 A	11/Oct/19 A		Prepare and Submit Package Interior Storefronts
SM 8 1310	Review and Approve Package Interior Storefronts	5	0	100%	14/Oct/19 A	18/Oct/19 A		 Review and Approve Package Interior Storefronts
SM 8 1320	Fabricate and Deliver Interior Storefront Frames	80	80	0%	31/Oct/19 A	22/Apr/20	21	Fabricate and Deliver Interior Storefront Frames
084113 Phase 2	Interior Storefront	295	295		31/Dec/19	26/Feb/21	33	
SM 8 1360	Prepare and Submit Package Interior Storefronts	25	25	0%	31/Dec/19*	04/Feb/20	33	Prepare and Submit Package Interior Storefronts
SM 8 1370	Review and Approve Package Interior Storefronts	25	25	0%	05/Feb/20	11/Mar/20	33	Review and Approve Package Interior Storef ronts
SM 8 1380	Fabricate and Deliver Interior Storefront Frames Phase 2	245	245	0%	12/Mar/20	26/Feb/21	33	Fabricate and Deliver Interior Storefront Frames Phase 2
084413 Glazed	Aluminum Curtain Walls	132	50		15/Aug/19 A	11/Mar/20	24	
SM 8 1030	Prepare and Submit Aluminum Curtain Wall Package	25	0	100%	15/Aug/19 A	25/Sep/19 A		Prepare and Submit Aluminum Curtain Wall Package
SM 8 1090	Review and Approve Curtain Wall Package	20	0	100%	08/Oct/19 A	06/Nov/19 A		Review and Approve Curtain Wall Package
SM 8 1190	Fabricate and Deliver Curtain Wall	85	50	41.18%	07/Nov/19 A	11/Mar/20	24	Fabricate and Deliver Curtain Wall
084413 Phase 2	! Glazed Aluminum Curtain Walls	379	296		15/Aug/19 A	01/Mar/21	32	
SM 8 1420	Prepare and Submit Aluminum Curtain Wall Package	25	0	100%	15/Aug/19 A	25/Sep/19 A		Prepare and Submit Aluminum Curtain Wall Package
SM 8 1430	Review and Approve Curtain Wall Package	20	5	75%	08/Oct/19 A	07/Jan/20	32	Review and Approve Curtain Wall Package
SM 8 1440	Fabricate and Deliver Curtain Wall	291	291	0%	08/Jan/20	01/Mar/21	32	Fabricate and Deliver Curtain Wall
087000 - Door H		111	63		22/Oct/19 A	30/Mar/20	48	
SM8 1120	Prepare and Submit Package Door Hardware	10	0	100%	22/Oct/19 A	27/Nov/19 A		Prepare and Submit Package Door Hardware
SM8 1130	Review and Approve Package Door Hardware	20	30	0%	29/Nov/19 A	11/Feb/20	48	Review and Approve Package Door Hardware
SM8 1140	Fabricate and Deliver Door Hardware	33	33	0%	12/Feb/20	30/Mar/20	48	Fabricate and Deliver Door Hardware
	atic Door Operators	128	80	070	22/Oct/19 A	22/Apr/20	21	Tableate and Bellion Beet Halaware
SM8 1180	Prepare and Submit Package Automatic Doors Operator	15	15	0%	22/Oct/19 A	21/Jan/20	21	Prepare and Submit Package Automatic Doors Operator
SM8 1190	Review and Approve Package Automatic Doors Operato	15	15	0%	22/Jan/20	11/Feb/20	21	Review and Approve Package Automatic Doors Operator
SM8 1200	Fabricate and Deliver Automatic Doors Operator	50	50	0%	12/Feb/20	22/Apr/20	21	Fabricate and Deliver Automatic Doors Operator
	·	113		076	22/Oct/19 A		0	Pablicate and Deliver Automatic Doors Operator
088000 Exterio SM8 1210	Prepare and Submit Package Exterior Glazing	25	65	100%	22/Oct/19 A	01/Apr/20 05/Dec/19 A	9	Prepare and Submit Package Exterior Glazing
			0		06/Dec/19 A	28/Jan/20	9	· · · · · · · · · · · · · · · · · · ·
SM8 1220	Review and Approve Package Exterior Glazing	25	20	20%			-	Review and Approve Package Exterior Glazing
SM8 1230	Fabricate and Deliver Exterior Glazing	45	45	0%	29/Jan/20	01/Apr/20	9	Fabricate and Deliver Exterior Glazing
<u> </u>	tive Glass Glazing	143	95	00/	22/Oct/19 A	13/May/20	6	
SM8 1060	Prepare and Submit Package Interior Glazing	25	25	0%	22/Oct/19 A	04/Feb/20	6	Prepare and Submit Package Interior Glazing
SM8 1070	Review and Approve Package Interior Glazing	25	25	0%	05/Feb/20	11/Mar/20	6	Review and Approve Package Interior Glazing
SM8 1080	Fabricate and Deliver Interior Glazing	45	45	0%	12/Mar/20	13/May/20	6	Fabricate and Deliver Interior Glazing
088700 Windov		113	65		22/Oct/19 A	01/Apr/20	39	
SM 8 1050	Prepare and Submit Package Exterior Glazing	25	0	100%	22/Oct/19 A	05/Dec/19 A		Prepare and Submit Package Exterior Glazing
SM 8 1150	Review and Approve Package Exterior Glazing	25	20	20%	06/Dec/19 A	28/Jan/20	39	Review and Approve Package Exterior Glazing
SM 8 1260	Fabricate and Deliver Exterior Glazing	45	45	0%	29/Jan/20	01/Apr/20	39	Fabricate and Deliver Exterior Glazing
089119 Fixed Lo	ouvers	96	55		31/Oct/19 A	18/Mar/20	3	
SM 8 1100	Prepare and Submit Package Louvers	15	0	100%	31/Oct/19 A	20/Nov/19 A		Prepare and Submit Package Louvers
SM 8 1200	Review and Approve Package Louvers	15	15	0%	21/Nov/19 A	21/Jan/20	3	Review and Approve Package Louvers
SM 8 1250	Fabricate and Deliver Fixed Louvers & Vents	40	40	0%	22/Jan/20	18/Mar/20	3	Fabricate and Deliver Fixed Louvers & Vents
Division 09 - Fini	shes	397	349		22/Oct/19 A	13/May/21	37	
092116 Gypsum	Board Assemblies	90	42		22/Oct/19 A	28/Feb/20	6	
SM 9 1040	Prepare and Submit Package Gboard Assembles	20	0	100%	22/Oct/19 A	27/Nov/19 A		Prepare and Submit Package Gboard Assemblies
SM 9 1140	Review and Approve Package Gboard Assemblies	15	15	0%	29/Nov/19 A	21/Jan/20	6	Review and Approve Package Gboard Assemblies
SM 9 1240	Fabricate and Deliver GBoard Assemblies	27	27	0%	22/Jan/20	28/Feb/20	6	Fabricate and Deliver GBoard Assemblies
	uctural Metal framing	73			22/Oct/19 A	04/Feb/20	8	
t Date: 08/Feb/1							Mar	chester Memorial Elementary School Note: The projections are based upon activity earning type and
sh Date: 08/Feb/1	2	Critical	-	ork			Widi	performance to-date on in-progress activities. Every precaution has
Date: 31/Dec/	19 Adda Work	Actual Milosto						been taken to ensure this report is accurate and up-to-date. No W.T. RICH CO., INC.
t Date: 30/Dec/	19 Remaining work	◆ Milesto						Page 6 of 30 liability is assumed for errors or omissions. Rounding errors may
out: Owner	Remaining Level of Effort	Critical	ivillesione			1		i :


cember Update Schedule	lama	Oria Du	Dor-	Λ ~+ 0/	Ctout	Finial	Tot-!	PROJECT SCHEDULE
y ID Activity N	varne	Orig Dur (Days)	Rem Dur	Act % Comp	Start	Finish	Total Float	2018 2019 2020 2021 2022 M
SM 9 1330 Prepare	and Submit Package Non Structural Metal Fram	20	0	100%	22/Oct/19 A	27/Nov/19 A		Prepare and Submit Package Non Structural Metal Framing
SM 9 1340 Review a	and Approve Package Non Structural Metal Fram	15	5	66.67%	29/Nov/19 A	07/Jan/20	8	Review and Approve Package Non Structural Metal Framing
SM 9 1350 Fabricate	e and Deliver Non Structural Metal Framing	20	20	0%	08/Jan/20	04/Feb/20	8	Fabricate and Deliver Non Structural Metal Framing
092900 Gypsum Board		83	35		22/Oct/19 A	19/Feb/20	13	
SM 9 1100 Prepare	and Submit Package Shaft Wall Assemblies	20	0	100%	22/Oct/19 A	27/Nov/19 A		Prepare and Submit Package Shaft Wall Assemblies
SM 9 1170 Review a	and Approve Package Shaft Wall Assemblies	15	15	0%	29/Nov/19 A	21/Jan/20	13	Review and Approve Package Shaft Wall Assemblies
SM 9 1270 Fabricate	e and Deliver Shaft Wall Assemblies	20	20	0%	22/Jan/20	19/Feb/20	13	Fabricate and Deliver Shaft Wall Assemblies
093000 Tiling		123	75		22/Oct/19 A	15/Apr/20	3	
SM 9 1080 Prepare	and Submit Package Tiling	20	0	100%	22/Oct/19 A	27/Nov/19 A		Prepare and Submit Package Tiling
	and Approve Package Tiling	15	15	0%	31/Dec/19	21/Jan/20	3	Review and Approve Package Tiling
SM 9 1250 Fabricate	e and Deliver Tiling	60	60	0%	22/Jan/20	15/Apr/20	3	Fabricate and Deliver Tiling
095113 Acoustical Ceiling P	anels	113	65		22/Oct/19 A	01/Apr/20	15	
SM 9 1010 Prepare	and Submit Package Acoustical Ceilings	15	15	0%	22/Oct/19 A	21/Jan/20	15	Prepare and Submit Package Acoustical Ceilings
	and Approve Package Acoustical Ceilings	15	15	0%	22/Jan/20	11/Feb/20	15	Review and Approve Package Acoustical Ceilings
SM 9 1220 Fabricate	e and Deliver Acoustical Ceilings	35	35	0%	12/Feb/20	01/Apr/20	15	Fabricate and Deliver Acoustical Ceilings
095123 Wood Ceiling Panels		118	70		22/Oct/19 A	08/Apr/20	10	
•	and Submit Package Wood Ceilings	15	15	0%	22/Oct/19 A	21/Jan/20	10	Prepare and Submit Package Wood Ceilings
	and Approve Package Wood Ceilings	15	15	0%	22/Jan/20	11/Feb/20	10	Review and Approve Package Wood Ceilings
	e and Deliver Wood Ceilings	40	40	0%	12/Feb/20	08/Apr/20	10	Fabricate and Deliver Wood Ceilings
096466 Wood Athletic Floori	ng	321	321		31/Dec/19	05/Apr/21	40	
·	and Submit Wood Athletic Floor Package	25	25	0%	31/Dec/19	04/Feb/20	40	Prepare and Submit Wood Athletic Floor Package
	and Approve Wood Athletic Floor Package	25	25	0%	05/Feb/20	11/Mar/20	40	Review and Approve Wood Athletic Floor Package
SM9 1080 Fabricate	e and Deliver Wood Athletic Floor Phase 2	271	271	0%	12/Mar/20	05/Apr/21	40	Fabricate and Deliver Wood Athletic Floor Phase 2
096513 Resilient Base & Ac		133	85		22/Oct/19 A	29/Apr/20	8	
SM 9 1060 Prepare	and Submit Package	25	0	100%	22/Oct/19 A	08/Nov/19 A		Prepare and Submit Package
SM 9 1200 Review a	and Approve Package	25	25	0%	08/Nov/19 A	04/Feb/20	8	Review and Approve Package
SM 9 1310 Fabricate	e and Deliver Resilient Base & Acœssories	60	60	0%	05/Feb/20	29/Apr/20	8	Fabricate and Deliver Resilient Base & Accessories
096519 Resilient Tile Flooring		133	85		22/Oct/19 A	29/Apr/20	8	
·	and Submit Package	25	0	100%	22/Oct/19 A	08/Nov/19 A		Prepare and Submit Package
	and Approve Package	25	25	0%	31/Dec/19	04/Feb/20	8	Review and Approve Package
	e and Deliver Tile Flooring	60	60	0%	05/Feb/20	29/Apr/20	8	Fabricate and Deliver Tile Flooring
096566 Resilient Athletic Flo		363	315		22/Oct/19 A	26/Mar/21	39	
· ·	and Submit Resilient Athletic Floor Package	25	25	0%	22/Oct/19 A	04/Feb/20	39	Prepare and Submit Resilient Athletic Floor Package
	and Approve Resilient Athletic Package	25	25	0%	05/Feb/20	11/Mar/20	39	Review and Approve Resilient Athletic Package
	e and Deliver Resilient Athletic Phase 2	265	265	0%	12/Mar/20	26/Mar/21	39	Fabricate and Deliver Resilient Athletic Phase 2
096723 Resinous Flooring		98	50		22/Oct/19 A	11/Mar/20	23	
· ·	and Submit Resinous Floor Package	15	5	66.67%	22/Oct/19 A	07/Jan/20	23	Prepare and Submit Resinous Floor Package
	and Approve Resinous Floor Package	15	15	0%	08/Jan/20	28/Jan/20	23	Review and Approve Resinous Floor Package
	e and Deliver Resinous Flooring	30	30	0%	29/Jan/20	11/Mar/20	23	Fabricate and Deliver Resinous Flooring
096813 Tile Carpeting	and Only if Darlows Over the	90	90	00/	31/Dec/19	06/May/20	3	Down and Order to Down the se
	and Submit Package Carpeting	15	15	0%	31/Dec/19	21/Jan/20	3	Prepare and Submit Package Carpeting
	and Approve Package Carpeting	15	15	0%	22/Jan/20	11/Feb/20	3	Review and Approve Package Carpeting
	e and Deliver Carpeting	60 215	60	0%	12/Feb/20	06/May/20	3	Fabricate and Deliver Carpeting
097200 Wall Coverings	and Submit Dadkage Well Covering	315	315	00/	19/Feb/20	13/May/21	37	Dranger and Culturit Dealeges Well Courtiers
	and Submit Package Wall Coverings	15	15	0%	19/Feb/20	10/Mar/20	37	Prepare and Submit Package Wall Coverings
	and Approve Package Wall Coverings e and Deliver Wall Coverings Phase 2	15	15	0%	11/Mar/20	31/Mar/20	37 37	Review and Approve Package Wall Coverings
	<u> </u>	285	285	0%	01/Apr/20	13/May/21	11	Fabricate and Deliver Wall Coverings Phase 2
D97723 Fabric Wrapped Par SM 9 1480 Prepare		90	90	00/	31/Dec/19	06/May/20		Propage and Submit Poolsage Eabite Wronned Penals
	and Submit Package Fabric Wrapped Panels and Approve Package Fabric Wrapped Panels	15 15	15 15	0%	31/Dec/19 22/Jan/20	21/Jan/20 11/Feb/20	11	 Prepare and Submit Package Fabric Wrapped Panels Review and Approve Package Fabric Wrapped Panels
	and Approve Package Fabric Wrapped Panels e and Deliver Fabric Wrapped Panels	15 60	15 60	0%	12/Feb/20	06/May/20	11	Fabricate and Deliver Fabric Wrapped Panels
	**			U70		-		rabilicate and Deliver rability Wilapped Pariets
098433 Sound Absorbing Was SM9 1090 Prepare	and Submit Package Sound Absorbing Panels	309	309	0%	31/Dec/19	18/Mar/21	39	Prepare and Submit Package Sound Absorbing Panels
	and Submit Package Sound Absorbing Panels	20	20	U%	31/Dec/19	28/Jan/20	39	
Date: 08/Feb/18 Date: 31/Jan/22	Summary Actual Work	Critical Actual	Remaining W Milestone	ork			Man	Note: The projections are based upon activity earning type and performance to-date on in-progress activities. Every precaution has
Date: 31/Dec/19	Remaining Work	Milesto						been taken to ensure this report is accurate and up-to-date. No W.T. RICH CO., INC.
Date: 30/Dec/19	Remaining Level of Effort	Critical						Page 7 of 30 liability is assumed for errors or omissions. Rounding errors may
t: Owner	· ·							exist.

ty ID	Activity Name	Orig Dur	Rem	Act %	Start	Finish	Total	2018 2019 2020 2021 2022
y ID	Activity marrie	(Days)	Dur	Comp	Start	Tillisit	Float	2019 2020
SM9 1100	Review and Approve Package Sound Absorbing Panels	15	15	0%	29/Jan/20	19/Feb/20	39	Review and Approve Package Sound Absorbing Panels
SM9 1110	Fabricate and Deliver Sound Absorbing Panels Phase 2	274	274	0%	20/Feb/20	18/Mar/21	39	Fabricate and Deliver Sound Absorbing Panels Phase 2
098436 Sound A	bsorbing Ceiling Units	309	309		31/Dec/19	18/Mar/21	39	
SM9 1150	Prepare and Submit Package Sound Absorbing Panels	20	20	0%	31/Dec/19	28/Jan/20	39	Prepare and Submit Package Sound Absorbing Panels
SM9 1160	Review and Approve Package Sound Absorbing Panels	15	15	0%	29/Jan/20	19/Feb/20	39	Review and Approve Package Sound Absorbing Panels
SM9 1170	Fabricate and Deliver Sound Absorbing Panels Phase 2	274	274	0%	20/Feb/20	18/Mar/21	39	Fabricate and Deliver Sound Absorbing Panels Phase 2
099113 Exterior		107	107	20/	31/Dec/19	01/Jun/20	38	
SM 9 1090	Prepare and Submit Package Paint & Coating	20	20	0%	31/Dec/19	28/Jan/20	38	Prepare and Submit Package Paint & Coating
SM 9 1160	Review and Approve Package Paint & Coating	15	15	0%	29/Jan/20	19/Feb/20	38	Review and Approve Package Paint & Coating
SM 9 1260	Order and Deliver Paint & Coating	72	72	0%	20/Feb/20	01/Jun/20	38	Order and Deliver Paint & Coating
099123 Interior I SM 9 1510	Prepare and Submit Package Paint & Coating	55	55	00/	31/Dec/19	18/Mar/20 28/Jan/20	2	Prepare and Submit Package Paint & Coating
SM 9 1510	Review and Approve Package Paint & Coating	20	20	0%	31/Dec/19 29/Jan/20	19/Feb/20	2	Review and Approve Package Paint & Coating
SM 9 1530	Order and Deliver Paint & Coating	15 20	15 20	0%	29/Jan/20 20/Feb/20	19/Feb/20 18/Mar/20	2	— Review and Approve Package Paint & Coating □ Order and Deliver Paint & Coating
	and Transparent Finishing	35	35	070	31/Dec/19	20/Feb/20	22	— Order and Deliver Paint & Coating
SM 9 1540	Prepare and Submit Package Paint & Coating	20	20	0%	31/Dec/19	28/Jan/20	22	Prepare and Submit Package Paint & Coating
SM 9 1550	Review and Approve Package Paint & Coating	15	15	0%	29/Jan/20	19/Feb/20	22	Review and Approve Package Paint & Coating
SM 9 1560	Fabricate and Deliver Paint & Coating	0	0	0%	29/Jan/20 20/Feb/20	20/Feb/20	22	Fabricate and Deliver Paint & Coating
	formance Coating	55	55	0 70	31/Dec/19	18/Mar/20	2	Tabilitate and politor Fairt & coating
99600 High Fel SM 9 1570	Prepare and Submit Package Paint & Coating	20	20	0%	31/Dec/19	28/Jan/20	2	Prepare and Submit Package Paint & Coating
SM 9 1580	Review and Approve Package Paint & Coating	15	15	0%	29/Jan/20	19/Feb/20	2	Review and Approve Package Paint & Coating
SM 9 1590	Fabricate and Deliver Paint & Coating	20	20	0%	20/Feb/20	18/Mar/20	2	Fabricate and Deliver Paint & Coating
vision 10 - Spec		286	286	0,0	31/Dec/19	15/Feb/21	52	- assisted and Bonson Caming
	isplay Surfaces	90	90		31/Dec/19	06/May/20	11	
SM 10 100	Prepare and Submit Package Display Units	15	15	0%	31/Dec/19	21/Jan/20	11	Prepare and Submit Package Display Units
SM 10 200	Review and Approve Package Display Units	15	15	0%	22/Jan/20	11/Feb/20	11	Review and Approve Package Display Units
SM 10 280	Fabricate and Deliver Visual Display Unit	60	60	0%	12/Feb/20	06/May/20	11	Fabricate and Deliver Visual Display Unit
01400 Signage		80	80		31/Dec/19	22/Apr/20	21	
SM 10 110	Prepare and Submit Package Signage	15	15	0%	31/Dec/19	21/Jan/20	21	□ Prepare and Submit Package Signage
SM 10 190	Review and Approve Package Signage	15	15	0%	22/Jan/20	11/Feb/20	21	Review and Approve Package Signage
SM 10 270	Fabricate and Deliver Signage	50	50	0%	12/Feb/20	22/Apr/20	21	Fabricate and Deliver Signage
01453 Traffic S	ignage	70	70		19/Feb/20	27/May/20	21	
SM10 1000	Prepare and Submit Package Traffic Signage	10	10	0%	19/Feb/20	03/Mar/20	21	□ Prepare and Submit Package Traffic Signage
SM10 1010	Review and Approve Package Traffic Signage	10	10	0%	04/Mar/20	17/Mar/20	21	□ Review and Approve Package Traffic Signage
SM10 1020	Fabricate and Deliver Traffic Signage	50	50	0%	18/Mar/20	27/May/20	21	Fabricate and Deliver Traffic Signage
02113 Phenolic	:Core Toil et Compartments	70	70		31/Dec/19	08/Apr/20	31	
SM 10 120	Prepare and Submit Package Toilet Partitions	15	15	0%	31/Dec/19	21/Jan/20	31	Prepare and Submit Package Toilet Partitions
SM 10 210	Review and Approve Package Partitions	15	15	0%	22/Jan/20	11/Feb/20	31	Review and Approve Package Partitions
SM 10 290	Fabricate and Deliver Toilet Partitions	40	40	0%	12/Feb/20	08/Apr/20	31	Fabricate and Deliver Toilet Partitions
02123 Cubicles	•	70	70		31/Dec/19	08/Apr/20	31	
SM10 1030	Prepare and Submit Package Cubicle Curtains	25	25	0%	31/Dec/19	04/Feb/20	31	Prepare and Submit Package Cubicle Curtains
SM10 1040	Review and Approve Package Cubicle Curtains	25	25	0%	05/Feb/20	11/Mar/20	31	Review and Approve Package Cubicle Curtains
SM10 1050	Fabricate and Deliver Cubicle Curtains	20	20	0%	12/Mar/20	08/Apr/20	31	Fabricate and Deliver Cubicle Curtains
02239 Folding	Panel Partitions	286	286		31/Dec/19	15/Feb/21	52	
SM10 1090	Prepare and Submit Package Folding Panel Partitions	25	25	0%	31/Dec/19	04/Feb/20	238	Prepare and Submit Package Folding Panel Partitions
SM10 1100	Review and Approve Package Folding Panel Partitions	25	25	0%	05/Feb/20	11/Mar/20	238	Review and Approve Package Folding Panel Partitions
SM10 1120	Field Measure for Folding Panel Paritition	3	3	0%	01/Dec/20	03/Dec/20	52	 Field Measure for Folding Panel Paritition
SM10 1110	Fabricate and Deliver Folding Panel Partitions	50	50	0%	04/Dec/20	15/Feb/21	52	Fabricate and Deliver Folding Panel Partitions
02600 Wall & D	Door Protection	70	70		31/Dec/19	08/Apr/20	31	
SM 10 140	Prepare and Submit Package Wall Protection	25	25	0%	31/Dec/19	04/Feb/20	31	Prepare and Submit Package Wall Protection
SM 10 230	Review and Approve Package Wall Protection	25	25	0%	05/Feb/20	11/Mar/20	31	Review and Approve Package Wall Protection
SM 10 310	Fabricate and Deliver Wall & Door Protection	20	20	0%	12/Mar/20	08/Apr/20	31	Fabricate and Deliver Wall & Door Protection
02800 Toilet Ac	ccessories	80	80		31/Dec/19	22/Apr/20	21	
ate: 08/Feb/1	8 Summary	Critical	l Remaining W	/ork			Man	ester Memorial Elementary School Note: The projections are based upon activity earning type and
Date: 31/Jan/2	2 Actual Work	Actual	-					performance to-date on in-progress activities. Every precaution has
ate: 31/Dec/		Milesto						been taken to ensure this report is accurate and up-to-date. No Page 8 of 30 W.T. RICH CO., INC.
Date: 30/Dec/	1 Containing 11 Containing							


December Update Se	cember Update Schedule PROJECT SCHEDULE PROJECT SCHEDULE										
Activity ID	Activity Name	Orig Dur	Rem	Act %	Start	Finish	Total	2018 2019 2020 2021 2022			
,		(Days)	Dur	Comp			Float				
SM 10 150	Prepare and Submit Package Toilet Accessories	25	25	0%	31/Dec/19	04/Feb/20	21	Prepare and Submit Package Toilet Accessories			
SM 10 240	Review and Approve Package Toilet Accessories	25	25	0%	05/Feb/20	11/Mar/20	21	Review and Approve Package Toilet Accessories			
SM 10 320	Fabricate and Deliver Bath Accessories	30	30	0%	12/Mar/20	22/Apr/20	21	Fabricate and Deliver Bath Accessories			
104413 Fire Extin		80	80	5 .5	31/Dec/19	22/Apr/20	21				
SM 10 340	Prepare and Submit Package Fire Cabinets	25	25	0%	31/Dec/19	04/Feb/20	21	Prepare and Submit Package Fire Cabinets			
SM 10 350		25	25	0%	05/Feb/20	11/Mar/20	21	Review and Approve Package Fire Cablinets			
SM 10 350 SM 10 360	Review and Approve Package Fire Cabinets Fabricate and Deliver Fire Protection Cabinets	30	30	0%	12/Mar/20	22/Apr/20	21	Review and Approve Package Fire Cabinets Fabricate and Deliver Fire Protection Cabinets			
				076							
104416 Fire Extin	Prepare and Submit Package Fire Extinguishers	80	80	0%	31/Dec/19	22/Apr/20 04/Feb/20	21	Prepare and Submit Package Fire Extinguishers			
		25	25		31/Dec/19		21				
SM 10 250	Review and Approve Package Fire Extinguishers	25	25	0%	05/Feb/20	11/Mar/20	21	Review and Approve Package Fire Extinguishers			
SM 10 330	Fabricate and Deliver Fire Protection Extinguishers	30	30	0%	12/Mar/20	22/Apr/20	21	Fabricate and Deliver Fire Protection Extinguishers			
105113 Lockers	Draw and Cultural Designation Land	90	90	00/	31/Dec/19	06/May/20	11	Province and Outcome Province			
SM 10 170	Prepare and Submit Package Lockers	15	15	0%	31/Dec/19	21/Jan/20	11	Prepare and Submit Package Lockers			
SM 10 180	Review and Approve Package Lockers	15	15	0%	22/Jan/20	11/Feb/20	11	Review and Approve Package Lockers			
SM 10 260	Fabricate and Deliver Metal Lockers	60	60	0%	12/Feb/20	06/May/20	11	Fabricate and Deliver Metal Lockers			
Division 11 - Equip		346	346		31/Dec/19	10/May/21	90				
113100 - Resider		80	80		31/Dec/19	22/Apr/20	21				
SM11 1030	Prepare and Submit Package Appliances	15	15	0%	31/Dec/19	21/Jan/20	21	Prepare and Submit Package Appliances			
SM11 1040	Review and Approve Package Appliances	15	15	0%	22/Jan/20	11/Feb/20	21	Review and Approve Package Appliances			
SM11 1050	Fabricate and Deliver Appliances	50	50	0%	12/Feb/20	22/Apr/20	21	Fabricate and Deliver Appliances			
114000 - Food Se	ervice Equipment	302	302		19/Feb/20	26/Apr/21	25				
SM11 1000	Prepare and Submit Package Food Service Equipment	25	25	0%	19/Feb/20	24/Mar/20	25	Prepare and Submit Package Food Service Equipment			
SM11 1010	Review and Approve Package Food Service Equipment	25	25	0%	25/Mar/20	28/Apr/20	25	Review and Approve Package Food Service Equipment			
SM11 1020	Fabricate and Deliver Food Service Equipment Phase 2	252	252	0%	29/Apr/20	26/Apr/21	25	Fabricate and Deliver Food Service Equipment Phase 2			
115213 Projection	Screens	70	70		31/Dec/19	08/Apr/20	31				
SM 11 100	Prepare and Submit Package Proj Screens	25	25	0%	31/Dec/19	04/Feb/20	31	Prepare and Submit Package Proj Screens			
SM 11 110	Review and Approve Package Proj Screens	25	25	0%	05/Feb/20	11/Mar/20	31	Review and Approve Package Proj Screens			
SM 11 120	Fabricate and Deliver Projection Screens	20	20	0%	12/Mar/20	08/Apr/20	31	Fabricate and Deliver Projection Screens			
115700 - Misc E	·	71	71		31/Dec/19	09/Apr/20	30				
SM11 1060	Prepare and Submit Package Misc Equipment	15	15	0%	31/Dec/19	21/Jan/20	30	□ Prepare and Submit Package Misc Equipment			
SM11 1070	Review and Approve Package Misc Equipment	16	16	0%	22/Jan/20	12/Feb/20	30	Review and Approve Package Misc Equipment			
SM11 1080	Fabricate and Deliver Misc Equipment	40	40	0%	13/Feb/20	09/Apr/20	30	Fabricate and Deliver Misc Equipment			
116143 - Platform	• •	285	285		19/Feb/20	01/Apr/21	27				
SM11 1090	Prepare and Submit Package Platform Curtains	25	25	0%	19/Feb/20	24/Mar/20	27	Prepare and Submit Package Platform Curtains			
SM11 1100	Review and Approve Package Platform Curtains	25	25	0%	25/Mar/20	28/Apr/20	27	Review and Approve Package Platform Curtains			
SM11 1100	Fabricate and Deliver Platform Curtains Phase 2	235	235	0%	29/Apr/20	01/Apr/21	27	Fabricate and Deliver Platform Curtains Phase 2			
116310 - Scoring		227	227	0 /0	19/Feb/20	11/Jan/21	41	i abilicate and Deliver Flationin Cultains Fridse Z			
SM11 1120	Prepare and Submit Package Scoreboard Equipment		25	0%	19/Feb/20	24/Mar/20	41	Prepare and Submit Package Scoreboard Equipment			
	Review and Approve Package Scoreboard Equipment	25				-	-	Review and Approve Package Scorebo and Equipment			
SM11 1130	0	25	25	0%	25/Mar/20	28/Apr/20	41				
SM11 1140	Fabricate and Deliver Scoreboard Equipment - Phase 2	177	177	0%	29/Apr/20	11/Jan/21	41	Fabricate and Deliver Scoreboard Equipment - Phase 2			
116623 - Gymnas		286	286	00/	19/Feb/20	02/Apr/21	33				
SM11 1150	Prepare and Submit Package Gym Equipment	25	25	0%	19/Feb/20	24/Mar/20	33	Prepare and Submit Package Gym Equipment			
SM11 1160	Review and Approve Package Gym Equipment	25	25	0%	25/Mar/20	28/Apr/20	33	Review and Approve Package Gym Equipment			
SM11 1170	Fabricate and Deliver Gym Equipment	236	236	0%	29/Apr/20	02/Apr/21	33	Fabricate and Deliver Gym Equipment			
116653 - Gymnas		285	285		19/Feb/20	01/Apr/21	34				
SM11 1180	Prepare and Submit Package Gym Dividers	25	25	0%	19/Feb/20	24/Mar/20	34	Prepare and Submit Package Gym Dividers			
SM11 1190	Review and Approve Package Gym Dividers	25	25	0%	25/Mar/20	28/Apr/20	34	Review and Approve Package Gym Dividers			
SM11 1200	Fabricate and Deliver Gym Dividers	235	235	0%	29/Apr/20	01/Apr/21	34	Fabricate and Deliver Gym Dividers			
116813 - Play Eq	uipment and Structures	312	312		19/Feb/20	10/May/21	90				
SM11 1210	Prepare and Submit Package Play Equipment and Struc	25	25	0%	19/Feb/20	24/Mar/20	90	Prepare and Submit Package Play Equipment and Structures			
SM11 1220	Review and Approve Package Play Equipment and Struc	25	25	0%	25/Mar/20	28/Apr/20	90	Review and Approve Package Play Equipment and Structures			
SM11 1230	Fabricate and Deliver Play Equipment and Structures	262	262	0%	29/Apr/20	10/May/21	90	Fabricate and Deliver Play Equipment and Structures			
Division 12 - Furnis	shings	341	341		31/Dec/19	03/May/21	88				
Start Date: 08/Feb/18	Cumma-	استف	Pomoinir 144	ork			Man	chester Memorial Elementary School Note: The projections are based upon activity earning type and			
Finish Date: 31/Jan/22	Garrinary	Critical I	Remaining Wo Milestone	OIK.				performance to-date on in-progress activities. Every precaution has			
Data Date: 31/Dec/1		Milestor						been taken to ensure this report is accurate and up-to-date. No W.T. RICH CO., INC.			
Print Date: 30/Dec/19	Remaining Level of Effort	◆ Critical I						Page 9 of 30 liability is assumed for errors or omissions. Rounding errors may			
Layout: Owner		→ Jinnodi I						exist.			


PROJECT SCHEDULE


December Update Schedule

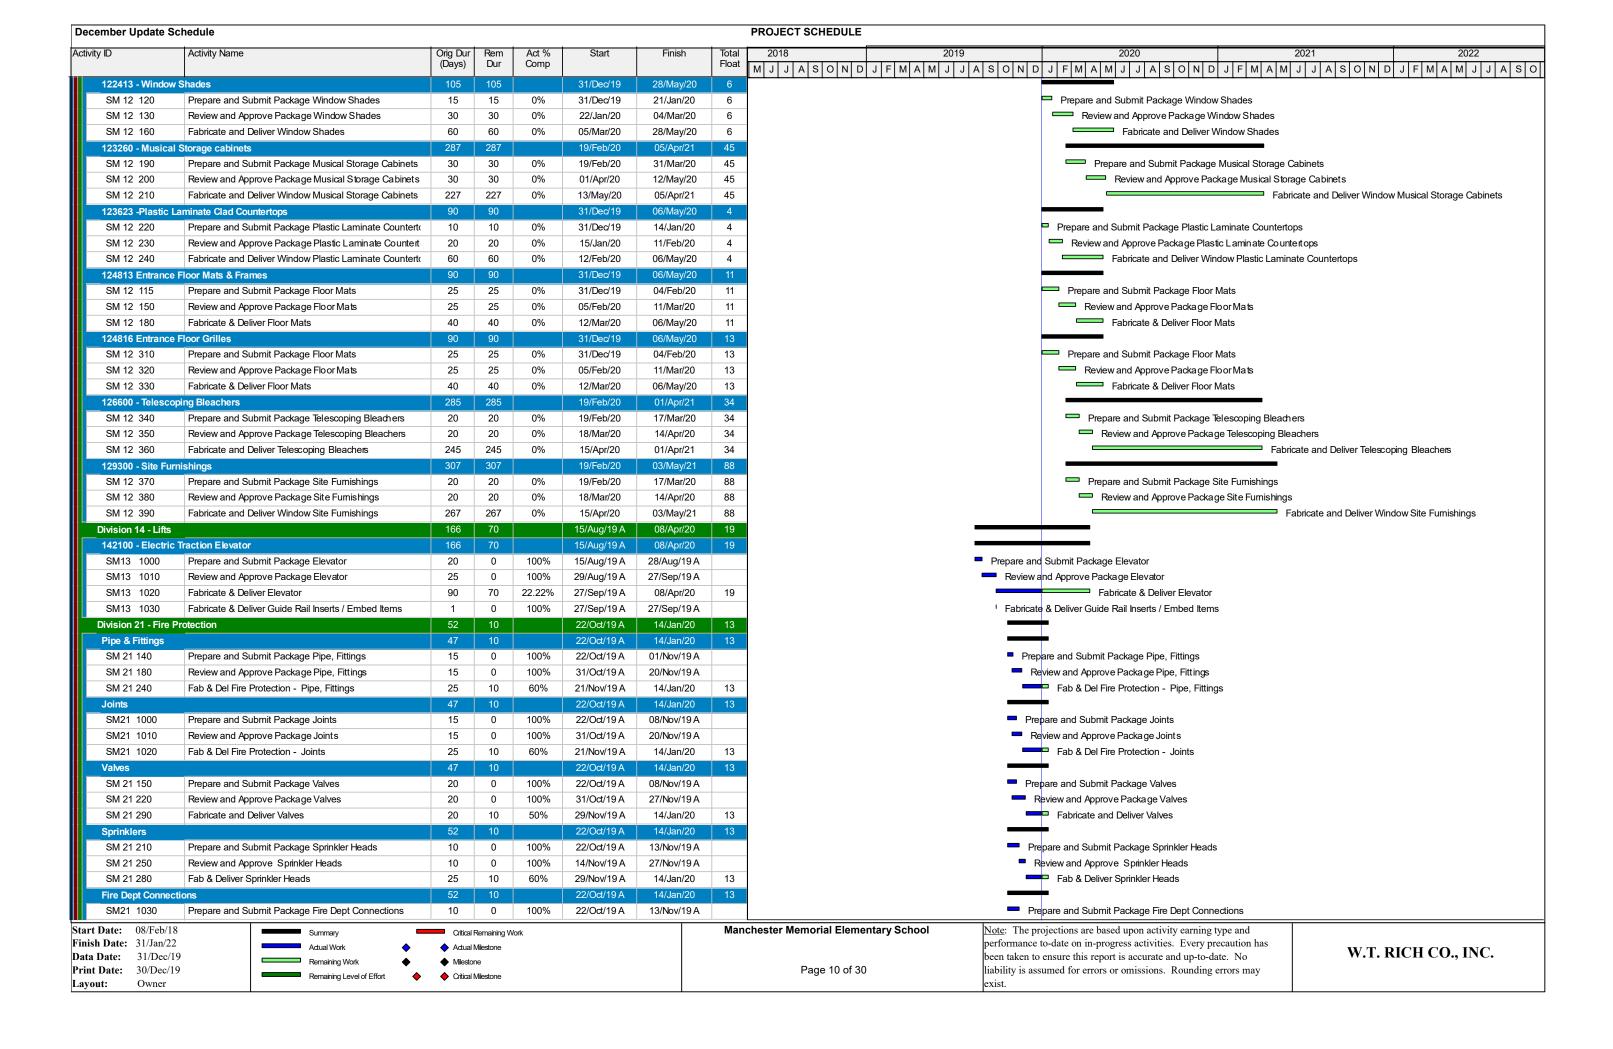


ity ID	Activity Name	Orig Dur	Rem	Act %	Start	Finish	Total	2018 2019 2020 2021 2022
.,	roung Hallo	(Days)	Dur	Comp	Glait	I II IIIII	Float	
SM21 1040	Review and Approve Fire Dept Connections	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Fire Dept Connections
SM21 1050	Fab & Deliver Fire Dept Connections	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Fire Dept Connections
Fire Standpipe Equi	pment	52	10		22/Oct/19 A	14/Jan/20	13	
SM21 1060	Prepare and Submit Package Fire Standpipe Equip	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Fire Standpipe Equip
SM21 1070	Review and Approve Fire Standpipe Equip	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Fire Standpipe Equip
	Fab & Deliver Fire Standpipe Equip	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Fire Standpipe Equip
Roof Manifold		52	10		22/Oct/19 A	14/Jan/20	13	
	Prepare and Submit Package Roof Manifold	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Roof Manifold
	Review and Approve Roof Manifold	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Roof Manifold
	Fab & Deliver Roof Manifold	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Roof Manifold
		52	10	0070	22/Oct/19 A	14/Jan/20	13	T ab & Beliver Floor Warniold
Fire Dept Hydrant Co				1000/			13	Drange and Submit Dackage Fire Dept Hydrant Connection
	Prepare and Submit Package Fire Dept Hydrant Connect	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Fire Dept Hydrant Connection
	Review and Approve Fire Dept Hydrant Connection	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Fire Dept Hydrant Connection
	Fab & Deliver Fire Dept Hydrant Connection	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Fire Dept Hydrant Connection
	l Channels & Supports	52	10		22/Oct/19 A	14/Jan/20	13	
SM21 1150	Prepare and Submit Package Steel Channels & Supports	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Steel Channels & Supports
SM21 1160	Review and Approve Steel Channels & Supports	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Steel Channels & Supports
SM21 1170	Fab & Deliver Steel Channels & Supports	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Steel Channels & Supports
Hangers & Seismic	Restraints	42	10		22/Oct/19 A	14/Jan/20	13	
	Prepare and Submit Package Hangers	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Hangers
SM 21 190	Review and Approve Package Hangers	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Package Hangers
	Fabricate and Deliver Fire Protection Hangers & Seismic	15	10	33.33%	29/Nov/19 A	14/Jan/20	13	Fabricate and Deliver Fire Protection Hangers & Seismic Restraints
Alarm Devices		52	10		22/Oct/19 A	14/Jan/20	13	
	Prepare and Submit Package Alarm Devices	10	0	100%	22/Oct/19 A	13/Nov/19 A	10	Prepare and Submit Package Alarm Devices
	Review and Approve Alarm Devices	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Alarm Devices
			-			-	40	
	Fab & Deliver Alarm Devices	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Alarm Devices
Double Check Valve		52	10	1000/	22/Oct/19 A	14/Jan/20	13	
	Prepare and Submit Package Double Check Valves	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Double Check Valves
SM21 1220	Review and Approve Double Check Valves	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Double Check Valves
SM21 1230	Fab & Deliver Double Check Valves	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Double Check Valves
Access Panels		52	10		22/Oct/19 A	14/Jan/20	13	
SM 21 100	Prepare and Submit Package Access Panels	15	0	100%	22/Oct/19 A	20/Nov/19 A		Prepare and Submit Package Access Panels
SM 21 170	Review and Approve Access Panels	15	0	100%	21/Nov/19 A	12/Dec/19 A		Review and Approve Access Panels
SM 21 230	Fab & Deliver Access Panels	15	10	33.33%	13/Dec/19 A	14/Jan/20	13	Fab & Deliver Access Panels
Air Compressor		52	10		22/Oct/19 A	14/Jan/20	13	
SM21 1240	Prepare and Submit Package Air Compressor	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Air Compressor
	Review and Approve Air Compressor	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Air Compressor
	Fab & Deliver Air Compressor	25	10	60%	29/Nov/19 A	14/Jan/20	13	Fab & Deliver Air Compressor
Division 22 - Plumbin	•	97	49		22/Oct/19 A	01/Apr/20	9	
Pipe,Fittings	9	52	0		22/Oct/19 A	06/Jan/20 A		
	Prepare and Submit Package Pipe	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Pipe
	Review and Approve Package Pipe	10	0	100%	14/Nov/19 A	27/Nov/19 A	-	Review and Approve Package Pipe
	Fabricate and Deliver Plumbing Pipe	25	0	100%	29/Nov/19 A	06/Jan/20 A		Fabricate and Deliver Plumbing Pipe
Joints		52	0		22/Oct/19 A	06/Jan/20 A		
	Prepare and Submit Package Joints	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Joints
SM22 1010	Review and Approve Package Joints	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Package Joints
SM22 1020	Fabricate and Deliver Plumbing Joints	25	0	100%	29/Nov/19 A	06/Jan/20 A		Fabricate and Deliver Plumbing Joints
Valves		52	0		22/Oct/19 A	06/Jan/20 A		
SM22 1030	Prepare and Submit Package Valves	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Valves
	Review and Approve Package Valves	10	0	100%	14/Nov/19 A	27/Nov/19 A		Review and Approve Package Valves
	Fabricate and Deliver Plumbing Valves	25	0	100%	29/Nov/19 A	06/Jan/20 A		Fabricate and Deliver Plumbing Valves
Insulation		37	0		22/Oct/19 A	12/Dec/19 A		
	Prepare and Submit Package Insulation	15	0	100%	22/Oct/19 A	20/Nov/19 A		Prepare and Submit Package Insulation
	T TOPATO ATTA OADITIET AUNAYO IITSUIALIUTI	13		100 70	22/00/19 A	20/190V/19A		
Date: 08/Feb/18	Summary	Critical	Remaining W	/ork			Man	chester Memorial Elementary School Note: The projections are based upon activity earning type and
sh Date: 31/Jan/22	Actual Work	Actual	Milestone					performance to-date on in-progress activities. Every precaution has been taken to ensure this report is accurate and un-to-date. No W.T. RICH CO., INC.
Date: 31/Dec/19 t Date: 30/Dec/19	Remaining Work	Milesto	one					been taken to ensure this report is accurate and up-to-date. No Page 11 of 30 liability is assumed for errors or omissions. Rounding errors may
	Remaining Level of Effort	A 03111	Milestone					r age it of our phaomy is assumed for effors of offissions. Rounding effors may

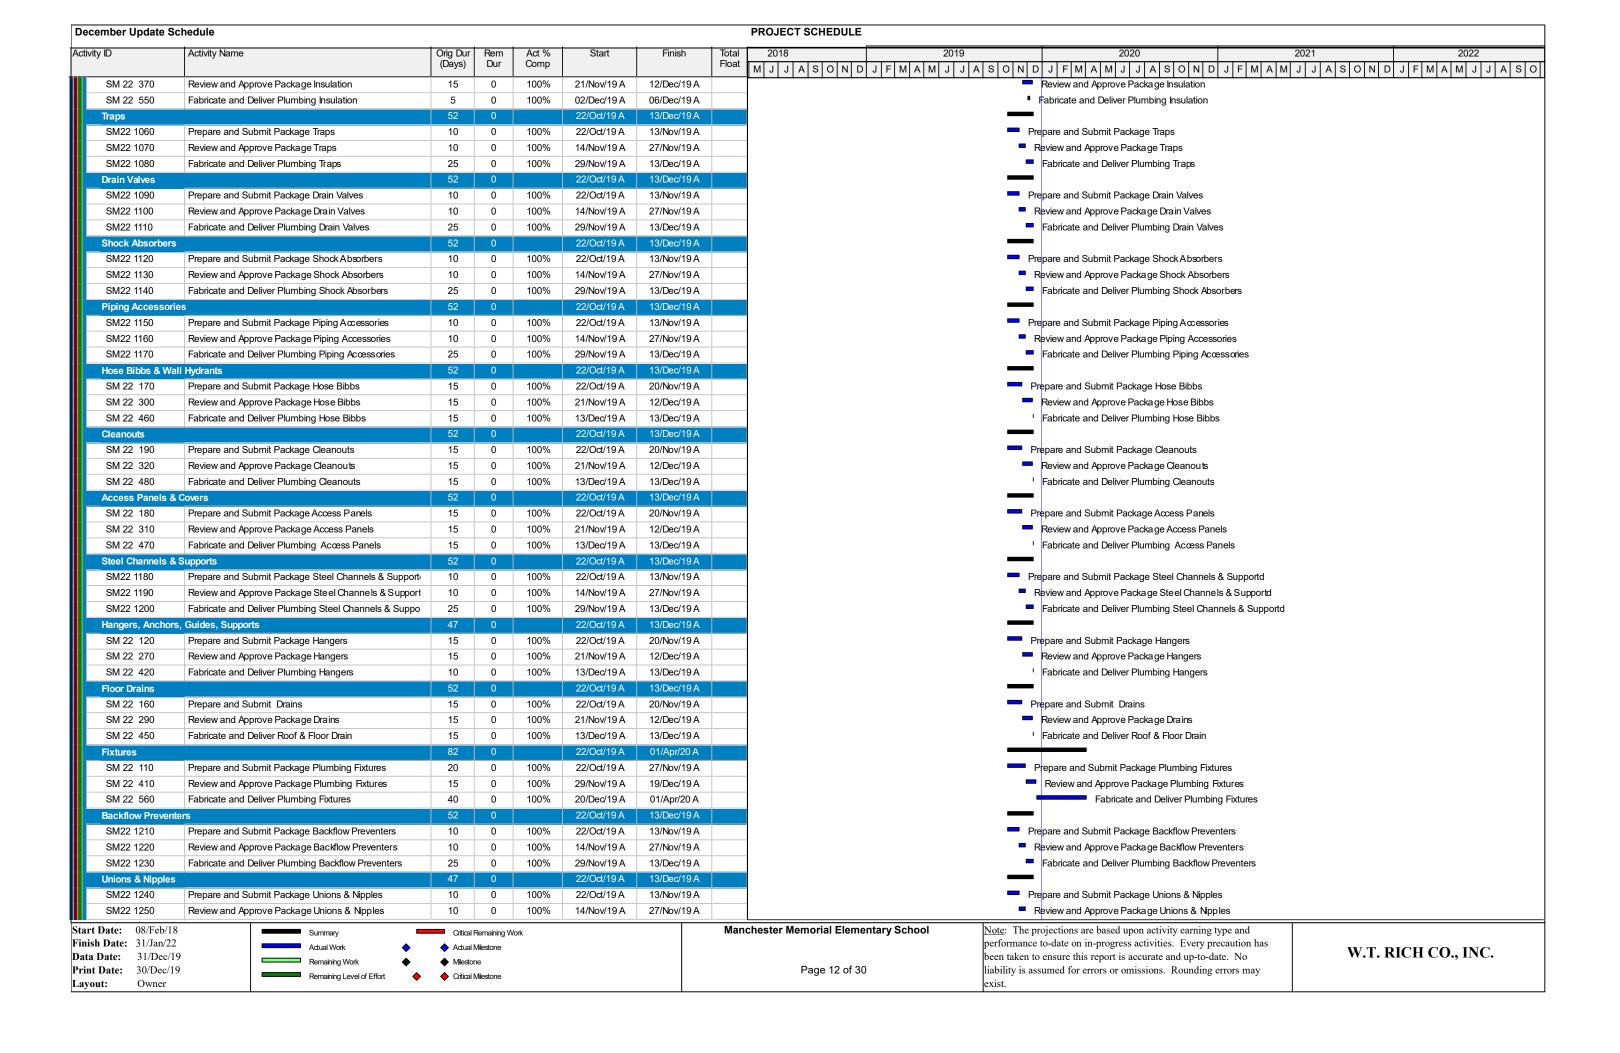

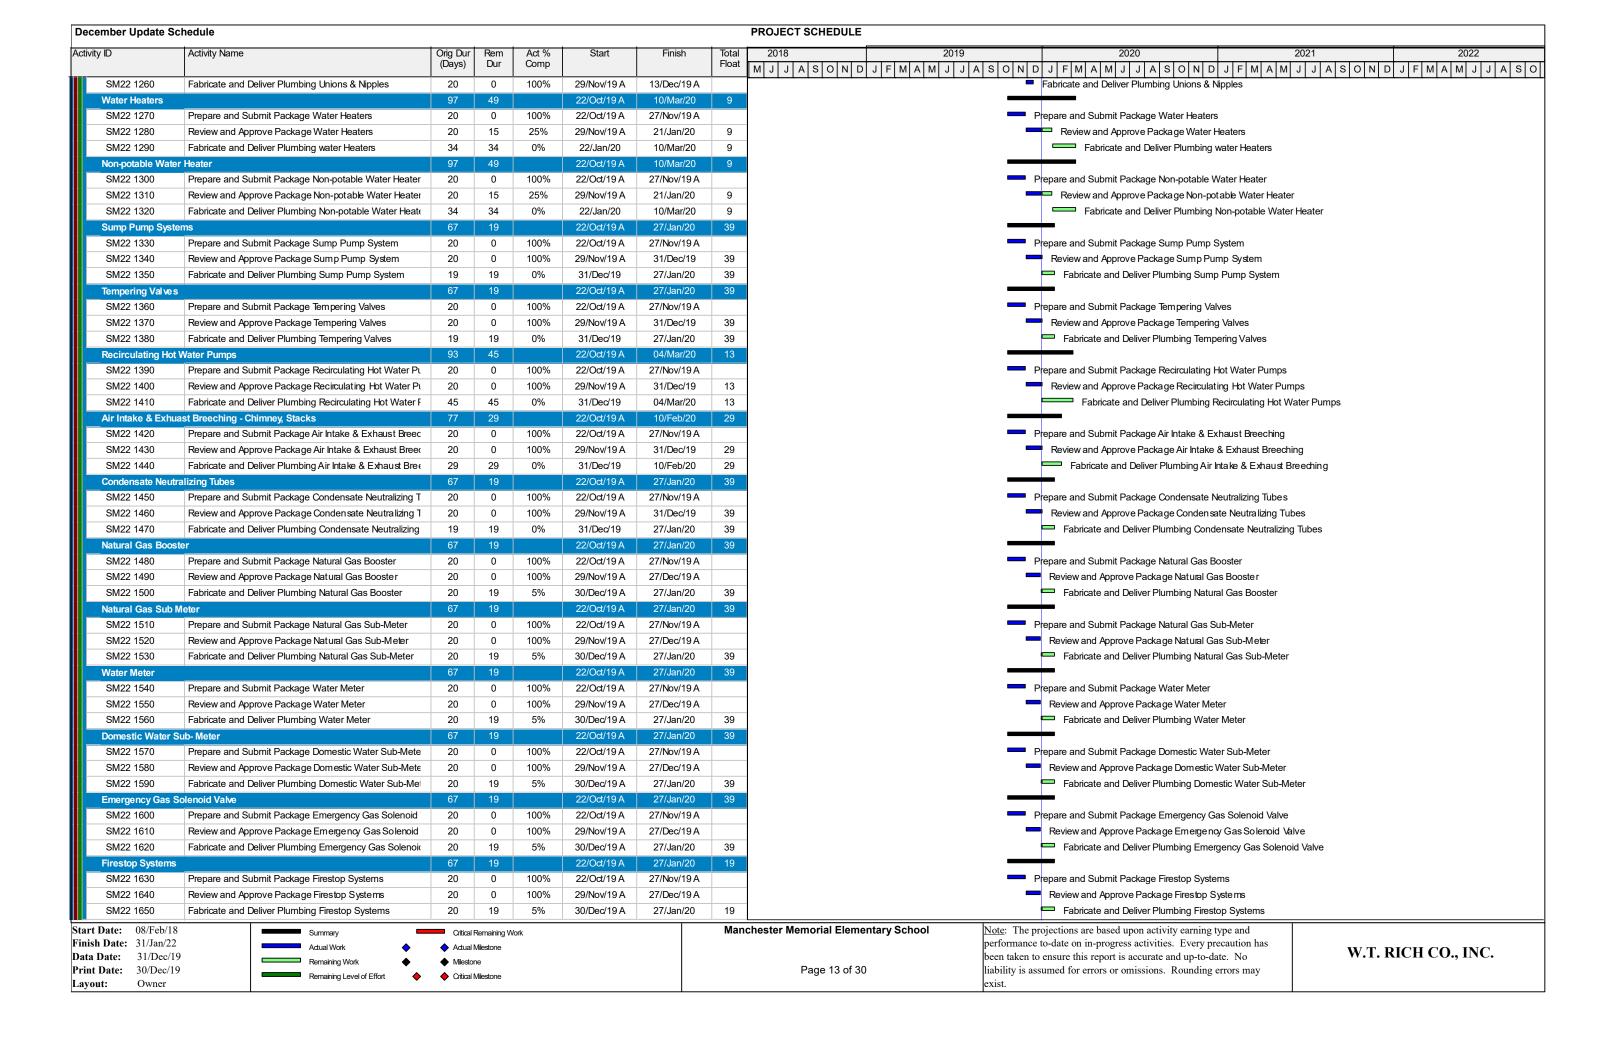

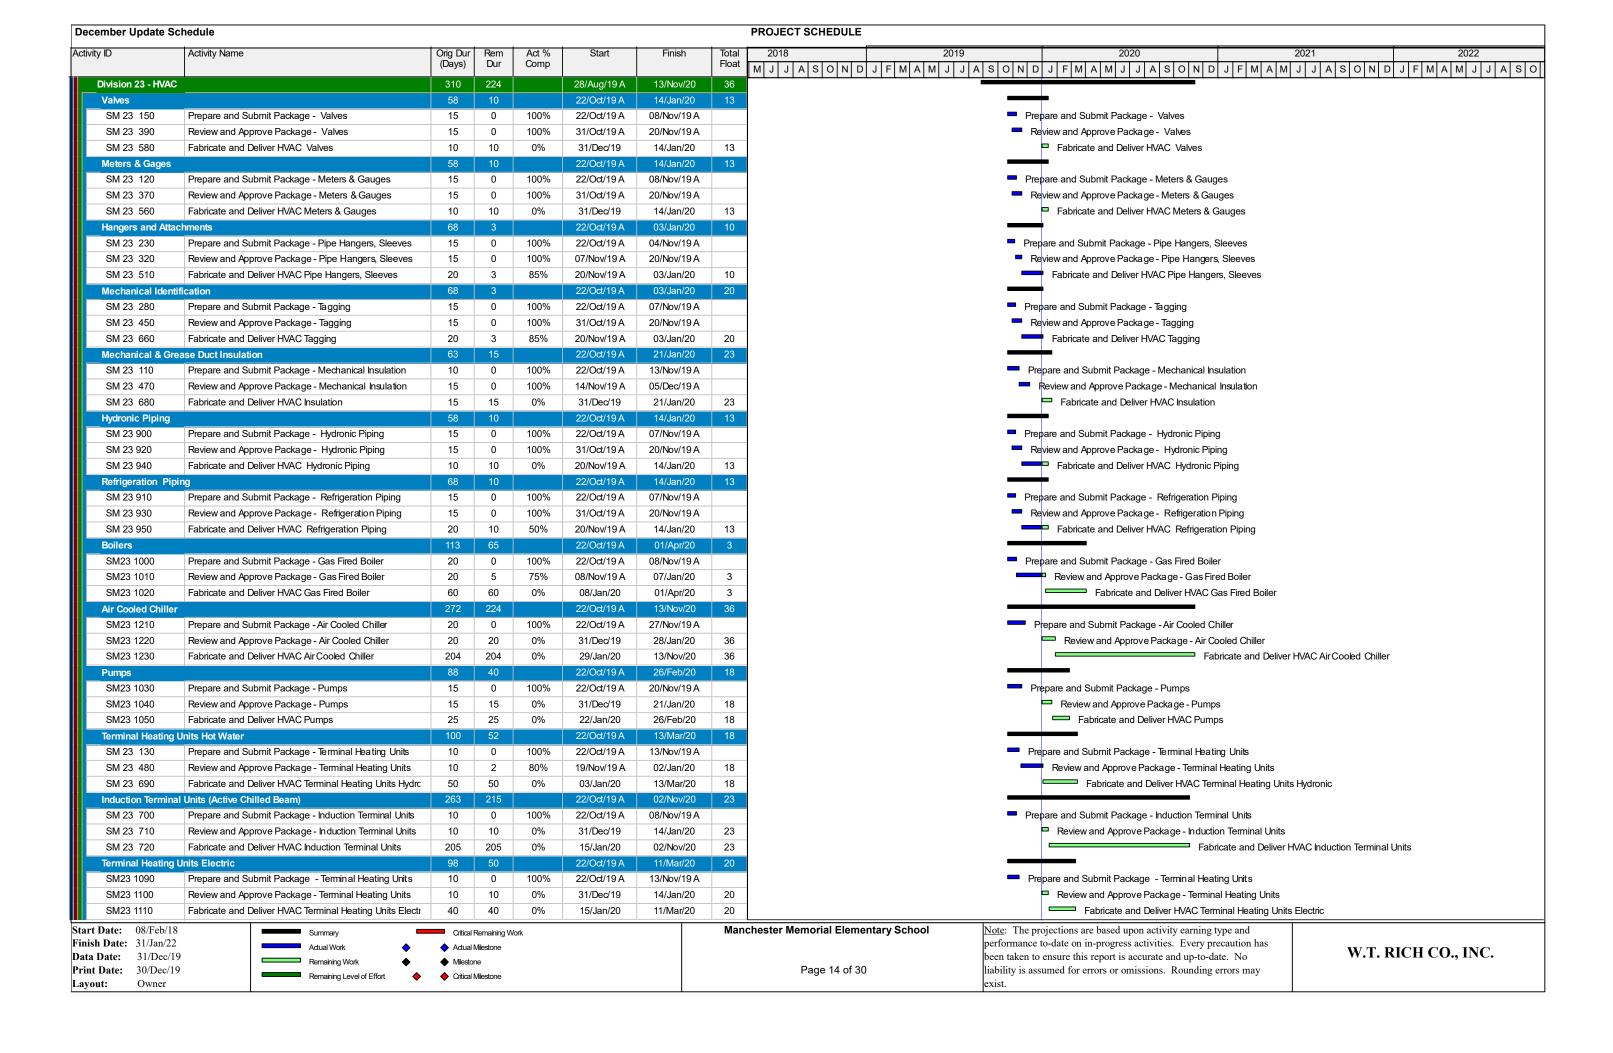

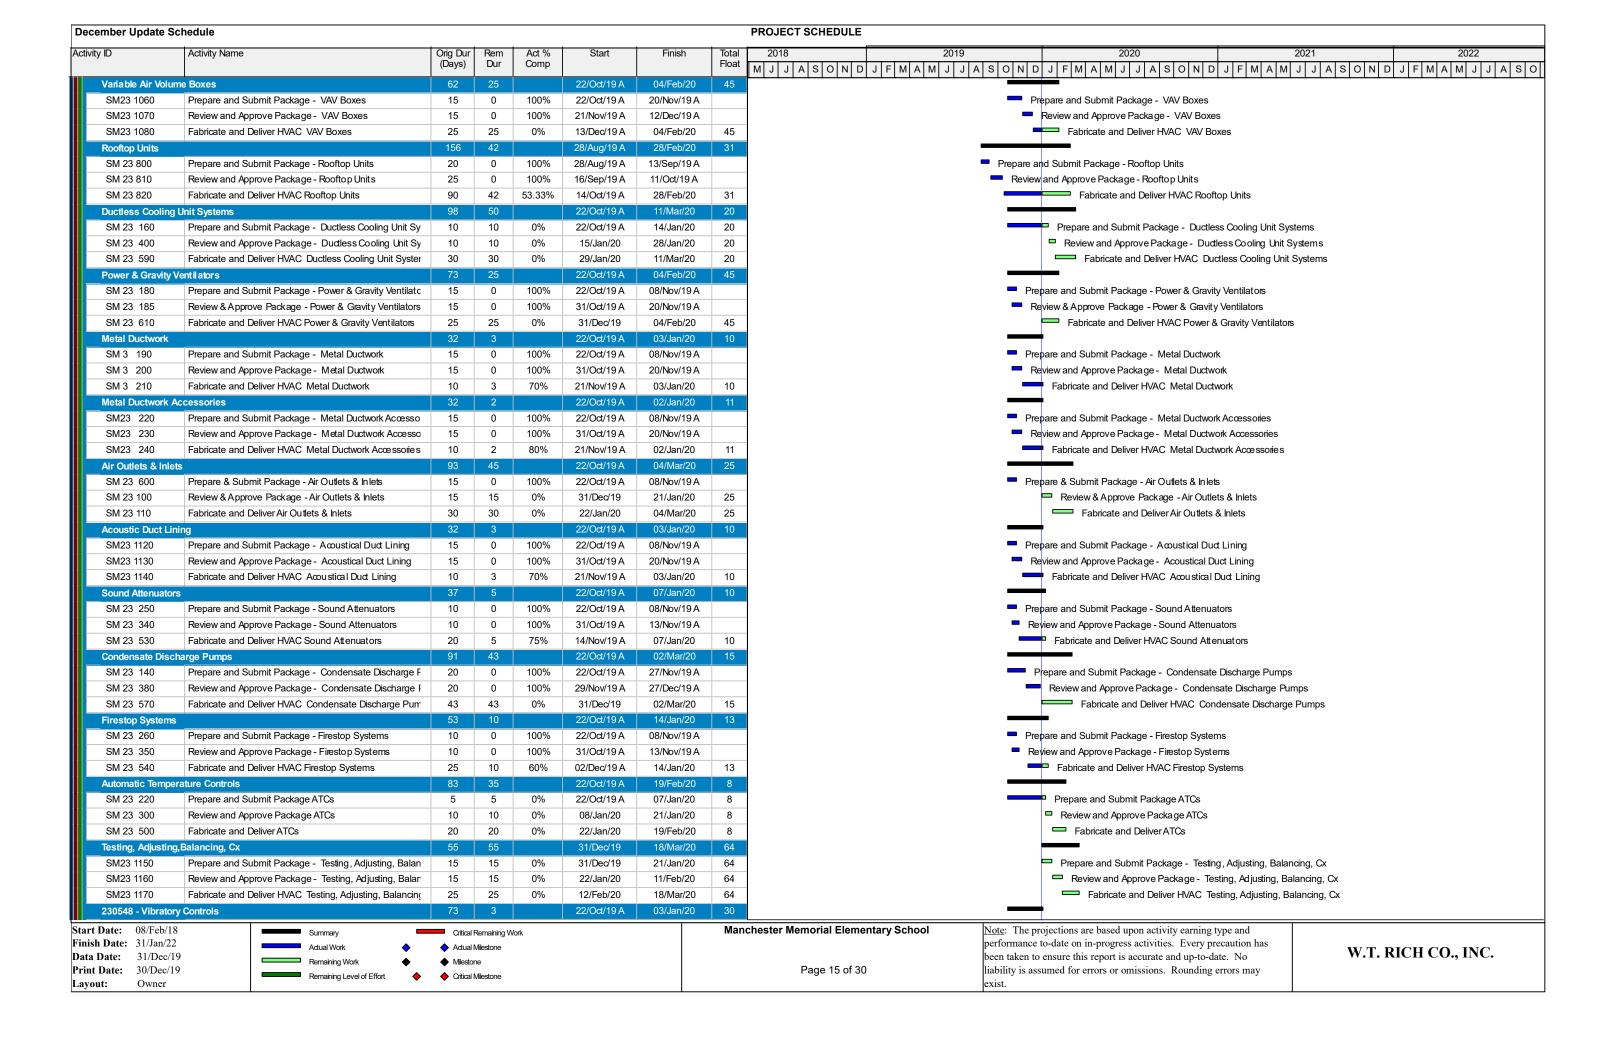

ty ID	hedule	Orio Dur	Pom	Δ at 0/.	Start	Einich	Total	2018	2020	2022
IJ.	Activity Name	Orig Dur (Days)	Rem Dur	Act % Comp	Start	Finish	Total Float	2018 2019 M J J A S O N D J F M A M J J A	2020 2021 N S O N D J F M A M J J A S O N D J F M A M J J A S O	2022 N D J F M A M J J
SM23 1180	Prepare and Submit Package - Vibratory & Seismic Con	15	0	100%	22/Oct/19 A	07/Nov/19 A			Prepare and Submit Package - Vibratory & Seismic Controls	1 1 1 1 1 1 1 1 1 1 1 1
SM23 1190	Review and Approve Package - Vibratory & Seismic Con	15	0	100%	31/Oct/19 A	20/Nov/19 A			Review and Approve Package - Vibratory & Seismic Controls	
SM23 1200	Fabricate and Deliver HVAC Vibratory & Seismic Controls	25	3	88%	20/Nov/19 A	03/Jan/20	30		Fabricate and Deliver HVAC Vibratory & Seismic Controls	
ivision 26 - Electri	cal	174	70		15/Aug/19 A	08/Apr/20	458	•		
Raceways & Fitting		43	15		22/Oct/19 A	21/Jan/20	8			
SM 26 900	Prepare and Submit Package Raceways & Fittings	20	0	100%	22/Oct/19 A	27/Nov/19 A			Prepare and Submit Package Raceways & Fittings	
SM 26 920	Review and Approve Package Raceways & Fittings	15	0	100%	29/Nov/19 A	19/Dec/19 A			Review and Approve Package Raceways & Fittings	
SM 26 940	Fabricate and Deliver Raceways & Fittings	15	15	0%	19/Dec/19 A	21/Jan/20	8		Fabricate and Deliver Raceways & Fittings	
Conductors		43	15		22/Oct/19 A	21/Jan/20	8			
SM26 1000	Prepare and Submit Package Conductors	20	0	100%	22/Oct/19 A	27/Nov/19 A			Prepare and Submit Package Conductors	
SM26 1010	Review and Approve Package Conductors	15	0	100%	29/Nov/19 A	19/Dec/19 A			Review and Approve Package Conductors	
SM26 1020	Fabricate and Deliver Conductors	15	15	0%	19/Dec/19 A	21/Jan/20	8		Fabricate and Deliver Conductors	
Access Panels	<u></u>	63	15		22/Oct/19 A	21/Jan/20	8			
SM 26 910	Prepare and Submit Package Access Panels	20	0	100%	22/Oct/19 A	27/Nov/19 A			Prepare and Submit Package Access Panels	
SM 26 930	Review and Approve Package Access Panels	15	0	100%	29/Nov/19 A	19/Dec/19 A			Review and Approve Package Access Panels	
SM 26 950	Fabricate and Deliver Access Panels	15	15	0%	31/Dec/19	21/Jan/20	8		Fabricate and Deliver Access Panels	
Sleeves, Inserts, C		23	3	070	22/Oct/19 A	03/Jan/20	525		. Salitation and Bollton / 10000 i Gilloto	
SM 26 100	Prepare and Submit Package Sleeves, Inserts	15	0	100%	22/Oct/19 A	11/Nov/19 A	020		Prepare and Submit Package Sleeves, Inserts	
SM 26 110	Review and Approve Package Sleeves, Inserts	5	0	100%	12/Nov/19 A	18/Nov/19 A			Review and Approve Package Sleeves, Inserts	
SM 26 120	Fabricate and Deliver Sleeves, Inserts	3	3	0%	12/Nov/19 A 19/Nov/19 A	03/Jan/20	525		Fabricate and Deliver Sleeves, Inserts	
	i abilicate and Deliver Sieeves, Hiserts			U 70			020		abilicate and Deliver Steeves, Insents	
Wiring Devices SM 26 190	Propage and Submit Package Wiring Parises	56	15	1000/	22/Oct/19 A	21/Jan/20 27/Nov/19 A	0		Prepare and Submit Package Wiring Devices	
SM 26 190 SM 26 240	Prepare and Submit Package Wiring Devices	20	0	100%	22/Oct/19 A 29/Nov/19 A	19/Dec/19 A				
	Review and Approve Package Wiring Devices	15	15	100%			0		Review and Approve Package Wiring Devices	
SM 26 360	Fabricate and Deliver Electrical Wiring Devices	15	15	0%	19/Dec/19 A	21/Jan/20	8		Fabricate and Deliver Electrical Wiring Devices	
Lighting Fixtures	Designation and Colombia Designation of Light 571	111	63	40001	22/Oct/19 A	30/Mar/20	15		Danage and Coherik Danks at 15th 4 February	
SM 26 130	Prepare and Submit Package Light Fixtures	20	0	100%	22/Oct/19 A	27/Nov/19 A	4.5		Prepare and Submit Package Light Fixtures	
SM 26 250	Review and Approve Package Light Fixtures	15	15	0%	29/Nov/19 A	21/Jan/20	15		Review and Approve Package Light Fixtures	
SM 26 370	Fabricate & Deliver Lighting Fixtures	48	48	0%	22/Jan/20	30/Mar/20	15		Fabricate & Deliver Lighting Fixtures	
Electric Power Equ		71	30	4225	22/Oct/19 A	11/Feb/20	25			
SM26 1030	Prepare and Submit Package Electrical Power Equipmen	15	0	100%	22/Oct/19 A	20/Nov/19 A			Prepare and Submit Package Electrical Power Equipment	
SM26 1040	Review and Approve Package Electrical Power Equipmer	15	0	100%	21/Nov/19 A	12/Dec/19 A			Review and Approve Package Electrical Power Equipment	
SM26 1050	Fabricate & Deliver Dry Type Electrical Power Equipment	30	30	0%	19/Dec/19 A	11/Feb/20	25		Fabricate & Deliver Dry Type Electrical Power Equipment	
Electrical Controls		83	35		22/Oct/19 A	19/Feb/20	59			
SM26 1060	Prepare and Submit Package Electrical Controls & Instru	20	0	100%	22/Oct/19 A	29/Nov/19 A			Prepare and Submit Package Electrical Controls & Instruments	
SM26 1070	Review and Approve Package Electrical Controls & Instru	15	15	0%	29/Nov/19 A	21/Jan/20	59		Review and Approve Package Electrical Controls & Instruments	
SM26 1080	Fabricate & Deliver Dry Type Electrical Controls & Instrum	20	20	0%	22/Jan/20	19/Feb/20	59		Fabricate & Deliver Dry Type Electrical Controls & Instruments	
Grounding		71	15		22/Oct/19 A	21/Jan/20	8			
SM 26 120	Prepare and Submit Package Grounding	20	0	100%	22/Oct/19 A	29/Nov/19 A			Prepare and Submit Package Grounding	
SM 26 290	Review and Approve Package Grounding	15	0	100%	29/Nov/19 A	10/Dec/19 A			Review and Approve Package Grounding	
SM 26 410	Fabricate & Deliver Grounding	15	15	0%	10/Dec/19 A	21/Jan/20	8		Fabricate & Deliver Grounding	
Distribution Switch		138	50		15/Aug/19 A	11/Mar/20	5	•		
SM 26 180	Prepare and Submit Package Switchboard	25	0	100%	15/Aug/19 A	20/Sep/19 A		•	Prepare and Submit Package Switchboard	
SM 26 230	Review and Approve Package Switchboard	15	0	100%	23/Sep/19 A	11/Oct/19 A			Review and Approve Package Switchboard	
SM 26 350	Fabricate and Deliver Switchboard	50	50	0%	19/Dec/19 A	11/Mar/20	5		Fabricate and Deliver Switchboard	
Panel Boards		103	55		22/Oct/19 A	18/Mar/20	0			
SM 26 170	Prepare and Submit Package Panel Boards	15	0	100%	22/Oct/19 A	04/Nov/19 A			Prepare and Submit Package Panel Boards	
SM 26 220	Review and Approve Package Panel Boards	15	5	66.67%	04/Nov/19 A	07/Jan/20	0		Review and Approve Package Panel Boards	
SM 26 340	Fabricate and Deliver Electrical Panel Boards	50	50	0%	08/Jan/20	18/Mar/20	0		Fabricate and Deliver Electrical Panel Boards	
Dry Type Transforn	ners	113	65		22/Oct/19 A	01/Apr/20	5		 	
SM 26 710	Prepare and Submit Package Dry Type Transformers	15	0	100%	22/Oct/19 A	20/Nov/19 A			Prepare and Submit Package Dry Type Transformers	
SM 26 790	Review and Approve Package Dry Type Transformers	15	5	66.67%	21/Nov/19 A	07/Jan/20	5		Review and Approve Package Dry Type Transformers	
SM 26 840	Fabricate & Deliver Dry Type Transformers	60	60	0%	08/Jan/20	01/Apr/20	5		Fabricate & Deliver Dry Type Transformers	
Fire Alarm System		73		070	22/Oct/19 A	04/Feb/20	13		. azaata a zantai zij ijpo nanalainia	
						04/1 05/20		charter Manuarial Et	by my to the state of the state	
Date: 08/Feb/18 Date: 31/Jan/22	Summary		Remaining W	ork (Man	chester Memorial Elementary School	Note: The projections are based upon activity earning type and performance to-date on in-progress activities. Every precaution has	
Date: 31/Jan/22 Date: 31/Dec/19	Actual Work	Actual							been taken to ensure this report is accurate and up-to-date. No	T. RICH CO., INC.
t Date: 31/Dec/19	Remaining Work	◆ Milesto						Page 16 of 30	liability is assumed for errors or omissions. Rounding errors may	2 = 2 3 ., 21 (0)
50, D00, 17	Remaining Level of Effort	Critical	Milestone			1		30 01 00		

December Update S	PROJECT SCHEDULE PROJECT SCHEDULE										
Activity ID	Activity Name	Orig Dur	Rem	Act %	Start	Finish	Total	2018 2019 2020 2021 2022			
,		(Days)	Dur	Comp			Float				
SM 26 130	Prepare and Submit Package Fire Alarm System	25	5	80%	22/Oct/19 A	07/Jan/20	13	Prepare and Submit Package Fire Alarm System			
SM 26 140	Review and Approve Package Fire Alarm System	10	10	0%	08/Jan/20	21/Jan/20	13	Review and Approve Package Fire Alarm System			
SM 26 150						04/Feb/20	_				
	Fabricate & Deliver Fire Alarm System	10	10	0%	22/Jan/20		13	Fabricate & Deliver Fire Alarm System			
Surge Protection		88	40		22/Oct/19 A	26/Feb/20	54				
SM 26 110	Prepare and Submit Package Surge Protection Devices	10	0	100%	22/Oct/19 A	08/Nov/19 A		Prepare and Submit Package Surge Protection Devices			
SM 26 270	Review and Approve Package Surge Protection Devices	15	15	0%	31/Dec/19	21/Jan/20	54	Review and Approve Package Surge Protection Devices			
SM 26 390	Fabricate & Deliver Dry Type Surge Protection Devices	25	25	0%	22/Jan/20	26/Feb/20	54	Fabricate & Deliver Dry Type Surge Protection Devices			
Lighting Control S	System	98	50		22/Oct/19 A	11/Mar/20	28				
SM 26 100	Prepare and Submit Package Lighting Control	20	0	100%	22/Oct/19 A	08/Nov/19 A		Prepare and Submit Package Lighting Control			
SM 26 280	Review and Approve Package Lighting Control	15	15	0%	31/Dec/19	21/Jan/20	28	Review and Approve Package Lighting Control			
SM 26 400	Fabricate & Deliver Lighting Control System	35	35	0%	22/Jan/20	11/Mar/20	28	Fabricate & Deliver Lighting Control System			
	Tablicate a Beliver Eighting Control Cystem	61	10	070	22/Oct/19 A	14/Jan/20	Q	Tublicate a beliver Eighting control bysterin			
Wireways	Draw and Cultural Daylong Wingsung			4000/			0	Description and Cultural Posterior Missource			
SM 26 700	Prepare and Submit Package Wireways	5	0	100%	22/Oct/19 A	26/Dec/19 A		Prepare and Submit Package Wireways			
SM 26 750	Review and Approve Package Wireways	15	5	66.67%	27/Dec/19 A	07/Jan/20	8	Review and Approve Package Wireways			
SM 26 800	Fabricate and Deliver Wireways	5	5	0%	08/Jan/20	14/Jan/20	8	□ Fabricate and Deliver Wireways			
Seals		61	5		22/Oct/19 A	07/Jan/20	13				
SM 26 720	Prepare and Submit Package Seals	5	0	100%	22/Oct/19 A	26/Dec/19 A		Prepare and Submit Package Seals			
SM 26 760	Review and Approve Package Seals	15	0	100%	27/Dec/19 A	27/Dec/19 A		Review and Approve Package Seals			
SM 26 810	Fabricate and Deliver Seals	5	5	0%	30/Dec/19 A	07/Jan/20	13	□ Fabricate and Deliver Seals			
	Standby Electrical System 127 40 22/Oct/19 A 26/Feb/20 30										
SM 26 740	Prepare and Submit Package Standby Electrical System	15	0	100%	22/Oct/19 A	06/Nov/19 A		Prepare and Submit Package Standby Electrical System			
SM 26 780	Review and Approve Package Standby Electrical System	15	0	100%	06/Nov/19 A	29/Nov/19 A	20	Review and Approve Package Standby Electrical System			
SM 26 830	Fabricate and Deliver Generator	80	40	50%	29/Nov/19 A	26/Feb/20	30	Fabricate and Deliver Generator			
Variable Frequer		73	25		22/Oct/19 A	04/Feb/20	33				
SM26 1090	Prepare and Submit Package Variable Frequency Drives	10	5	50%	22/Oct/19 A	07/Jan/20	33	Prepare and Submit Package Variable Frequency Drives			
SM26 1100	Review and Approve Package Variable Frequency Drives	10	10	0%	08/Jan/20	21/Jan/20	33	Review and Approve Package Variable Frequency Drives			
SM26 1110	Fabricate & Deliver Dry Type Variable Frquesncy Drives	10	10	0%	22/Jan/20	04/Feb/20	33	□ Fabricate & Deliver Dry Type Variable Frquesncy Drives			
Firestop		56	5		22/Oct/19 A	07/Jan/20	13				
SM 26 730	Prepare and Submit Package Firestop	5	0	100%	22/Oct/19 A	06/Nov/19 A		Prepare and Submit Package Firestop			
SM 26 770	Review and Approve Package Firestop	15	0	100%	07/Nov/19 A	27/Nov/19 A		Review and Approve Package Firestop			
SM 26 820	Fabricate and Deliver Firestop	15	5	66.67%	19/Dec/19 A	07/Jan/20	13	Fabricate and Deliver Firestop			
	1 dollade and believe 1 liestop	51	5	00.01 70	22/Oct/19 A	07/Jan/20	13	Tabilitate and Beliver Fliestop			
Cabling System	Duran and Cultural Dealers and Cultural		0	4000/			10	Decrees and Cultural Declarate Cable Customs			
SM 26 200	Prepare and Submit Package Cable System	10	0	100%	22/Oct/19 A	13/Nov/19 A		Prepare and Submit Package Cable System			
SM 26 260	Review and Approve Package Cable System	15	0	100%	14/Nov/19 A	05/Dec/19 A		Review and Approve Package Cable System			
SM 26 380	Fabricate & Deliver Cable System	10	5	50%	19/Dec/19 A	07/Jan/20	13	Fabricate & Deliver Cable System			
Bi-directional An		68	20		22/Oct/19 A	28/Jan/20	13				
SM26 1150	Prepare & Submit Package - Antenna System	15	0	100%	22/Oct/19 A	20/Nov/19 A		Prepare & Submit Package - Antenna System			
SM26 1160	Review & Approve Package - Antenna System	15	5	66.67%	21/Nov/19 A	07/Jan/20	13	Review & Approve Package - Antenna System			
SM26 1170	Fabricate & Deliver Antenna System	15	15	0%	08/Jan/20	28/Jan/20	13	□ Fabricate & Deliver Antenna System			
Lightning Protect	•	118	70		22/Oct/19 A	08/Apr/20	65				
SM26 1210	Prepare & Submit Package - Lightning Protection	15	0	100%	22/Oct/19 A	20/Nov/19 A		Prepare & Submit Package - Lightning Protection			
SM26 1220	Review & Approve Package - Lightning Protection	15	0	100%	21/Nov/19 A	12/Dec/19 A		Review & Approve Package - Lighthing Protection			
							CF				
SM26 1230	Fabricate & Deliver Lightning Protection	70	70	0%	31/Dec/19	08/Apr/20	65	Fabricate & Deliver Lightning Protection			
Floor Outlets		63	15		22/Oct/19 A	21/Jan/20	3				
SM 26 320	Prepare & Submit Package - Floor Outlets	15	0	100%	22/Oct/19 A	20/Nov/19 A		Prepare & Submit Package - Floor Outlets			
SM 26 160	Review & Approve Package - Floor Outlets	15	0	100%	21/Nov/19 A	12/Dec/19 A		Review & Approve Package - Floor Outlets			
SM 26 170	Fabricate & Deliver Floor Outlets	15	15	0%	31/Dec/19	21/Jan/20	3	Fabricate & Deliver Floor Outlets			
Division 27 & 28 -	Technology & Security	58	10		22/Oct/19 A	14/Jan/20	8				
Communications	Room Equipment	58	10		22/Oct/19 A	14/Jan/20	8				
SM27 1000	Prepare & Submit Package - Communications Room Eq	15	0	100%	22/Oct/19 A	20/Nov/19 A		Prepare & Submit Package - Communications Room Equip			
SM27 1010	Review & Approve Package - Communications Room Eq	15	5	66.67%	19/Dec/19 A	07/Jan/20	Д	Review & Approve Package - Communications Room Equip			
SM27 1010 SM27 1020	Fabricate & Deliver Communications Room Equip	5	5	0%	08/Jan/20	14/Jan/20	Ω	□ Fabricate & Deliver Communications Room Equip			
		-	-	U70			0	· Fabilitate α Deliver Continuintations Room Equip			
Fiber Optic Cable	95	58	10		22/Oct/19 A	14/Jan/20	8				
Start Date: 08/Feb/1	Cultifically	Critical F	Remaining W	Vork			Man	chester Memorial Elementary School Note: The projections are based upon activity earning type and			
Finish Date: 31/Jan/22	Addai Work	Actual N	Milestone					performance to-date on in-progress activities. Every precaution has been taken to ensure this report is accurate and up-to-date. No W.T. RICH CO., INC.			
Data Date: 31/Dec/1	Remaining work	♠ Milestor	ne					The same of the sa			
Print Date: 30/Dec/1	9 Remaining Level of Effort	Critical N	Milestone					Page 17 of 30 liability is assumed for errors or omissions. Rounding errors may			
Layout: Owner								exist.			


PROJECT SCHEDULE


December Update Schedule


cember Update So											
vity ID	Activity Name	Orig Dur (Days)	Rem	Act % Comp	Start	Finish	Total Float	2018 2019	2020		021 2022
				<u> </u>			1 loat	M J J A S O N D J F M A M J J A S O N			J A S O N D J F M A M J J A
SM27 1030	Prepare & Submit Package - Fiber Optic Cables	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Fiber Optic Cal		
SM27 1040	Review & Approve Package - Fiber Optic Cables	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Fiber Opti	ic Cables	
SM27 1050	Fabricate & Deliver Fiber Optic Cables	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Fiber Optic Cables		
UTP Cable		58	10		22/Oct/19 A	14/Jan/20	8				
SM27 1060	Prepare & Submit Package - UTP Cables	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - UTP Cables		
SM27 1070	Review & Approve Package - UTP Cables	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - UTP Cabl	es	
SM27 1080	Fabricate & Deliver UTP Cables	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver UTP Cables		
Fiber Innerduct		58	10		22/Oct/19 A	14/Jan/20	8				
SM27 1090	Prepare & Submit Package - Fiber Innerduct	15	0	100%	22/Oct/19 A	20/Nov/19 A			Prepare & Submit Package - Fiber Innerduct		
	•						0				
SM27 1100	Review & Approve Package - Fiber Innerduct	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Fiber Inne	elduct	
SM27 1110	Fabricate & Deliver Fiber Innerduct	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Fiber Innerduct		
Fiber Distribution		58	10		22/Oct/19 A	14/Jan/20	8				
SM27 1120	Prepare & Submit Package - Fiber Distribution	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Fiber Distribution	on	
SM27 1130	Review & Approve Package - Fiber Distribution	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Fiber Distr	ributio n	
SM27 1140	Fabricate & Deliver Fiber Distribution	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Fiber Distribution		
Work Station Cab	ole	56	5		22/Oct/19 A	07/Jan/20	13				
SM27 1150	Prepare & Submit Package - Work Station Cable	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Work Station C	able	
SM27 1160	Review & Approve Package - Work Station Cable	15	0	100%	21/Nov/19 A	12/Dec/19 A		_	Review & Approve Package - Work Station		
SM27 1170	Fabricate & Deliver Work Station Cable	15	5	66.67%	19/Dec/19 A	07/Jan/20	13		■ Fabricate & Deliver Work Station Cable		
				00.07 70			0		rabilicate & Beliver Work Station Cable	•	
Main Distribution	·	58	10	4000/	22/Oct/19 A	14/Jan/20	0		D		
SM27 1180	Prepare & Submit Package - Main Distribution Facility	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Main Distribution	•	
SM27 1190	Review & Approve Package - Main Distribution Facility	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Main Distr	•	
SM27 1200	Fabricate & Deliver Main Distribution Facility	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Main Distribution F	acility	
Intermediate Distr	ribution Facilities	58	10		22/Oct/19 A	14/Jan/20	8	_			
SM27 1210	Prepare & Submit Package - Intermediate Distribution Fa	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Intermediate Di	istribution Facility	
SM27 1220	Review & Approve Package - Intermediate Distribution Fa	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Intermedia	ate Distribution Facility	/
SM27 1230	Fabricate & Deliver Intermediate Distribution Facility	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Intermediate Distrit	oution Facility	
Public Address S	•	58	10		22/Oct/19 A	14/Jan/20	8			•	
SM27 1240	Prepare & Submit Package - Public Address System	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Public Address	System	
SM27 1240 SM27 1250	· · · · · · · · · · · · · · · · · · ·		-				-		Review & Approve Package - Public Ad		
	Review & Approve Package - Public Address System	15	5	66.67%	19/Dec/19 A	07/Jan/20	8			•	
SM27 1260	Fabricate & Deliver Public Address System	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Public Address Sys	stem	
Wireless Master (Clock System	58	10		22/Oct/19 A	14/Jan/20	8				
SM27 1270	Prepare & Submit Package - Wireless Clock System	15	0	100%	22/Oct/19 A	20/Nov/19 A			Prepare & Submit Package - Wireless Clock	System	
SM27 1280	Review & Approve Package - Wireless Gock System	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Wireless	Oock System	
SM27 1290	Fabricate & Deliver Wireless Clock System	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Wireless Clock Sys	stem	
Two Way Commur	nications Call Boxes	58	10		22/Oct/19 A	14/Jan/20	8				
SM27 1300	Prepare & Submit Package - Two Way Call Box	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Two Way Call E	Box	
SM27 1310	Review & Approve Package - Two Way Call Box	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Two Way	Call Box	
SM27 1320	Fabricate & Deliver Two Way Call Box	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Two Way Call Box		
Local Sound Syste	-		-	0 /0		14/Jan/20	0		Tablicate & Deliver IWO Way Call Box		
SM27 1360		58	10	4000/	22/Oct/19 A		0		Dranam & Culturate Designation 1 control Control Control	votom	
	Prepare & Submit Package - Local Sound System	15	0	100%	22/Oct/19 A	20/Nov/19 A	-	_	Prepare & Submit Package - Local Sound S	•	
SM27 1370	Review & Approve Package - Local Sound System	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Local Sou	•	
SM27 1380	Fabricate & Deliver Local Sound System	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Local Sound System	em	
Elevator Phone Li	ine Fault Monitor	58	10		22/Oct/19 A	14/Jan/20	8	_	<u> </u>		
SM27 1330	Prepare & Submit Package - Elevator Phone Line Fault	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - Elevator Phone	e Line Fault Monitor	
SM27 1340	Review & Approve Package - Elevator Phone Line Fault I	15	5	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package - Elevator F	Phone Line Fault Mon	nitor
SM27 1350	Fabricate & Deliver Elevator Phone Line Fault Monitor	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver Elevator Phone Lir	ne Fault Monitor	
CCTV System		58	10		22/Oct/19 A	14/Jan/20	8				
SM27 1390	Prepare & Submit Package - CCTV	15	0	100%	22/Oct/19 A	20/Nov/19 A		_	Prepare & Submit Package - CCTV		
SM27 1400	Review & Approve Package CCTV		-	66.67%	19/Dec/19 A	07/Jan/20	8		Review & Approve Package CCTV		
		15	5				-				
SM27 1410	Fabricate & Deliver CCTV	5	5	0%	08/Jan/20	14/Jan/20	8		Fabricate & Deliver CCTV		
Division 31 - Earth	work	45	0		30/May/19 A	01/Aug/19 A					
312100 Erosion &	Sediment Control	30	0		30/May/19 A	11/Jul/19 A					
Date: 08/Feb/18	Summon	Critical	l Remaining \	Mork			Man	chester Memorial Elementary School Note: The	projections are based upon activity earning	type and	
sh Date: 31/Jan/22	Culturally		il Kemaining \ il Milestone	, voir					ce to-date on in-progress activities. Every pr	* 1	
	Adual VVOIK	→ Addal	II IVIIIGOLUI IE						to ensure this report is accurate and up-to-d		W.T. RICH CO., INC.
Date: 31/Dec/19	Domoirie Medi	A 43_ 4	ono					joech taken	to ensure unis report is accurate and up-to-u	aic. No	
Date: 31/Dec/19 t Date: 30/Dec/19	Remaining vyork	♦ Milesto	one Il Milestone						assumed for errors or omissions. Rounding		.,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,


PROJECT SCHEDULE


December Update Schedule

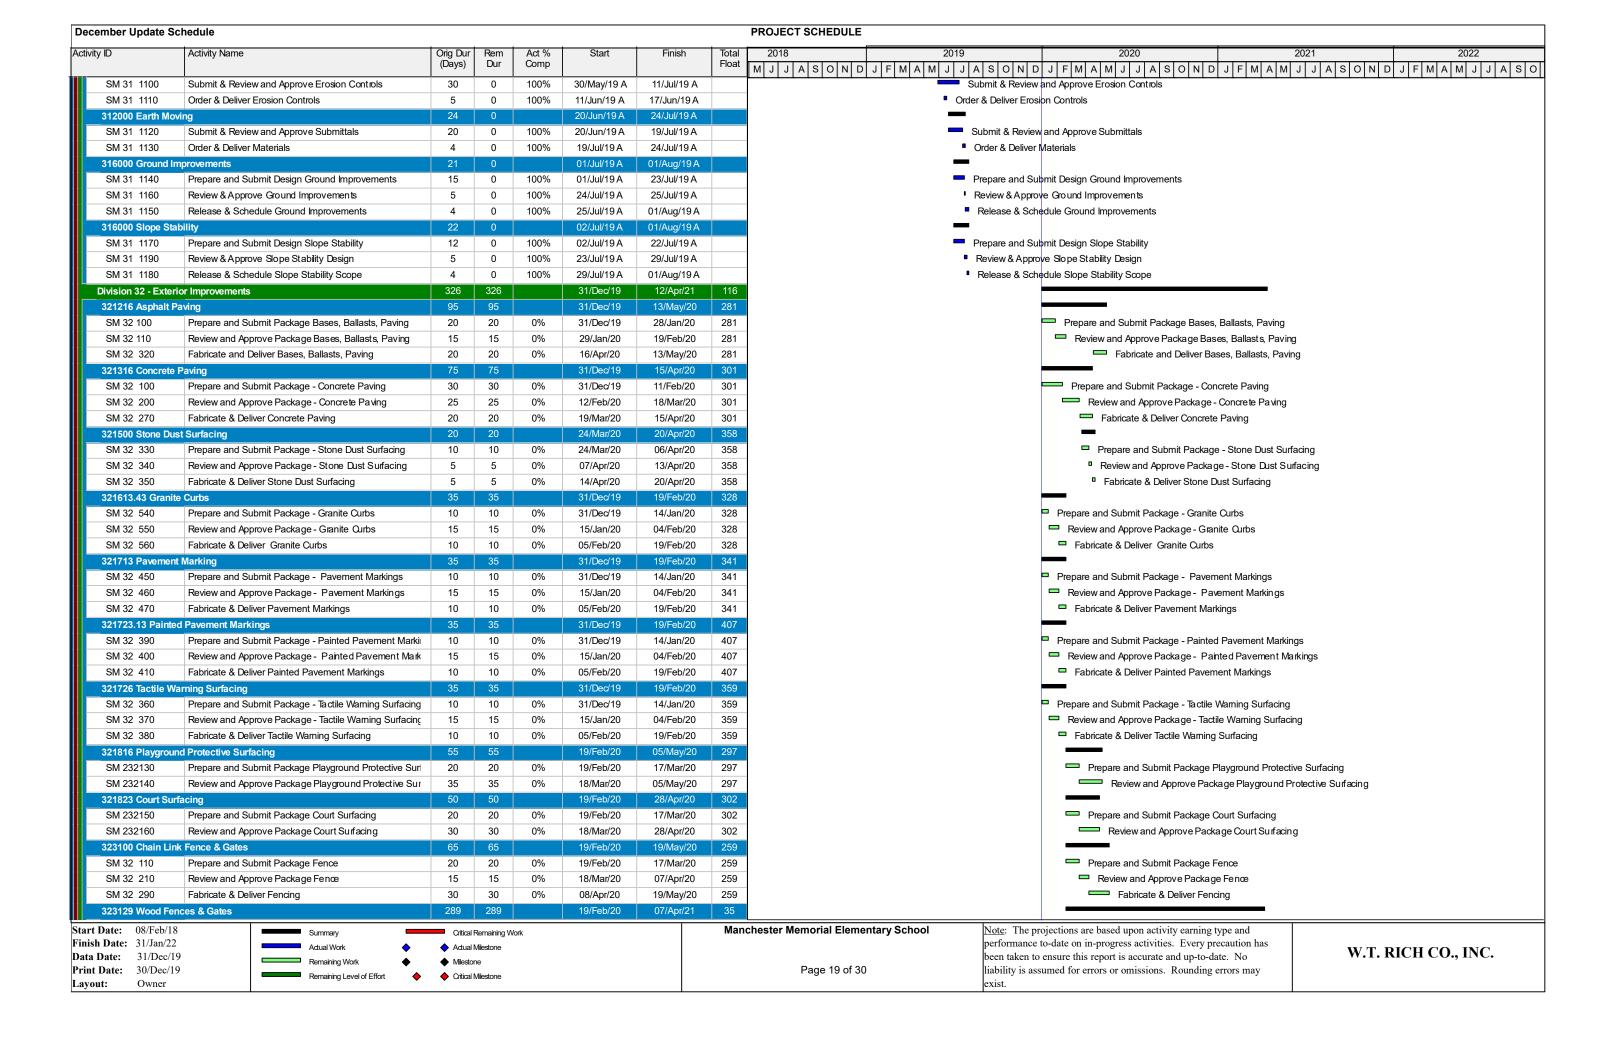


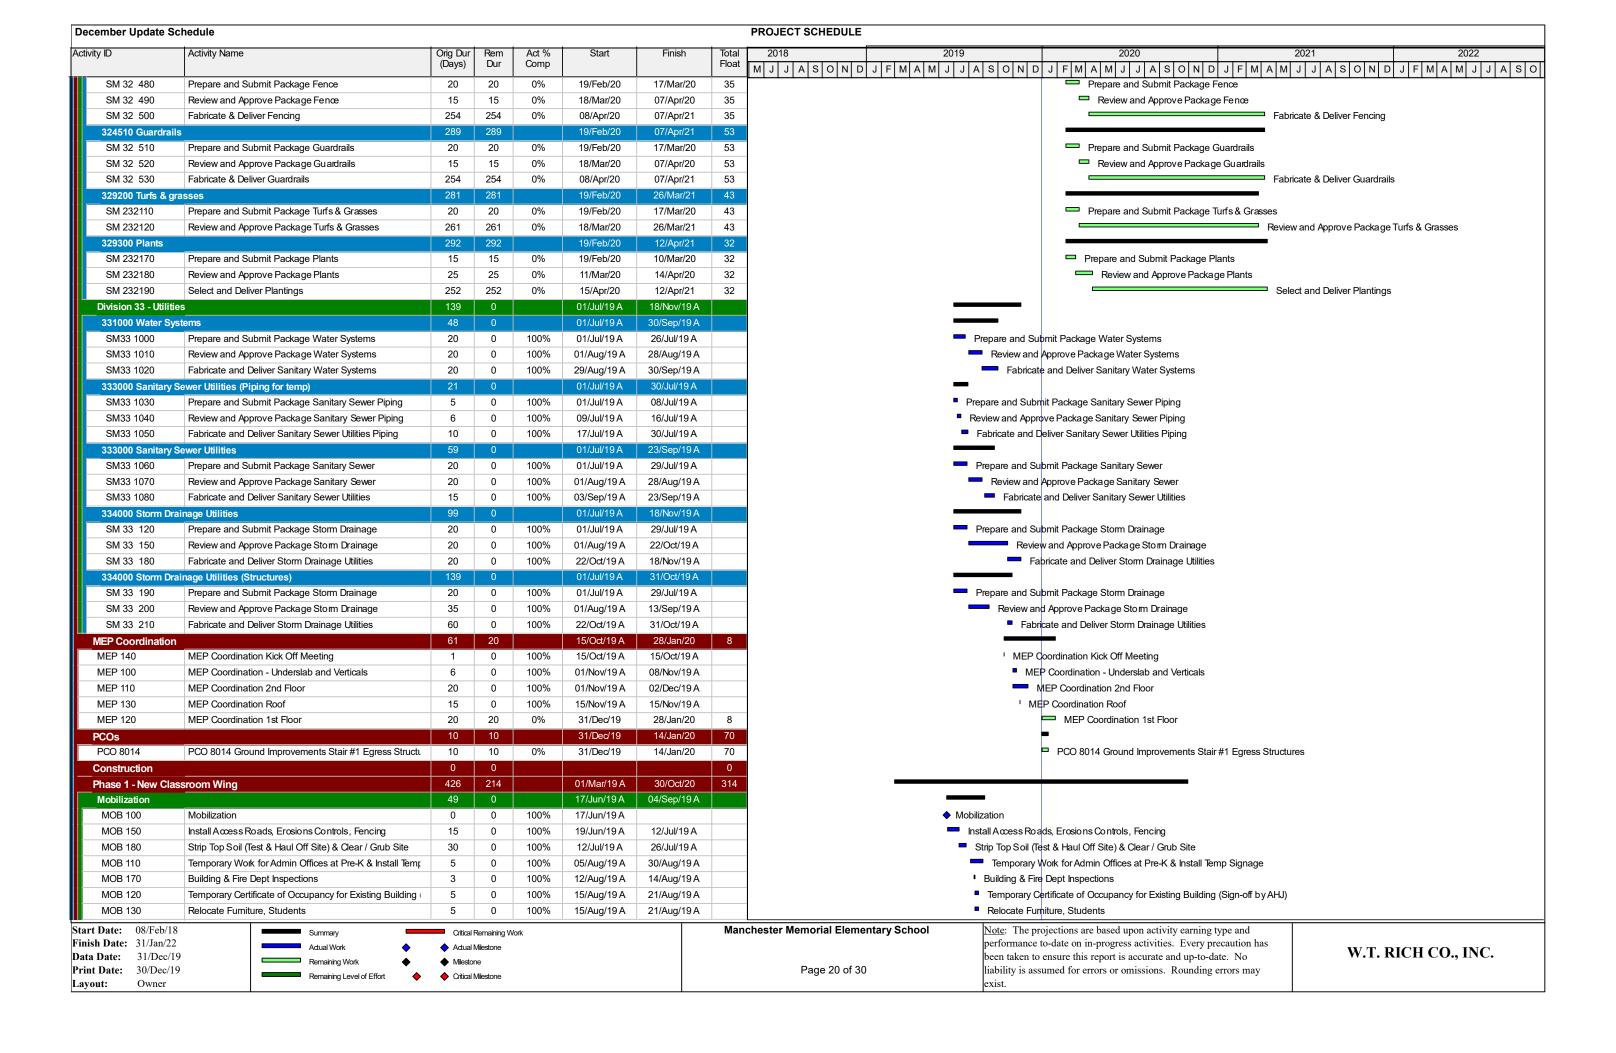


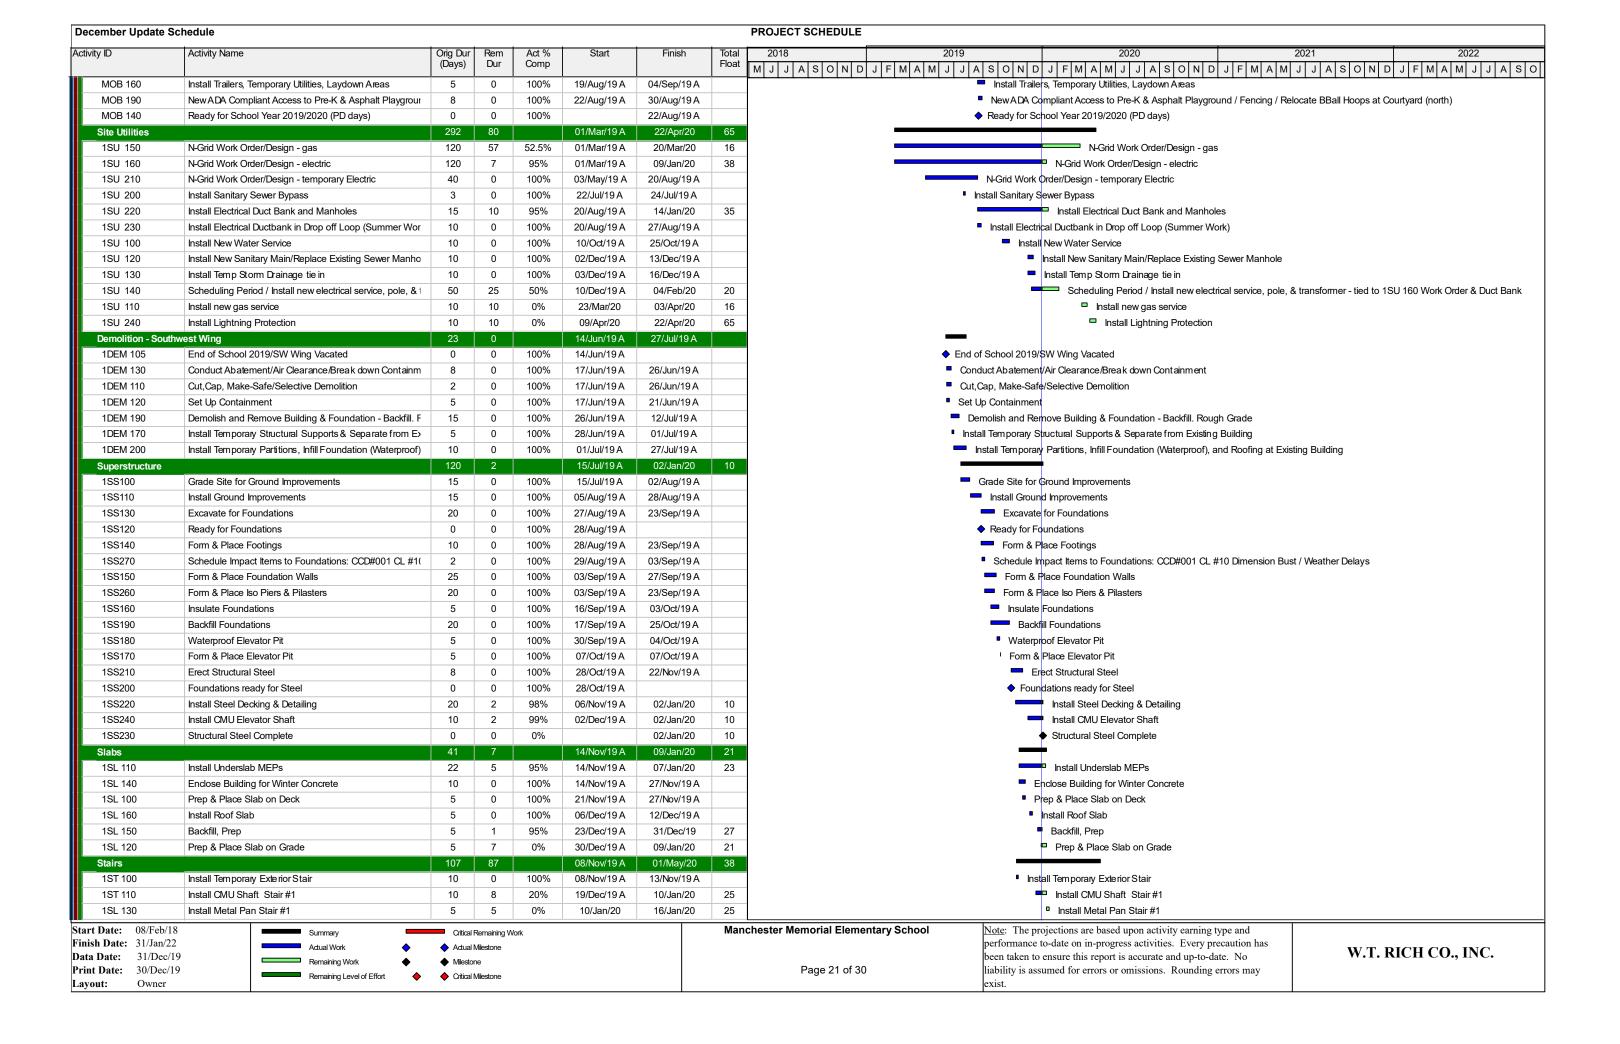


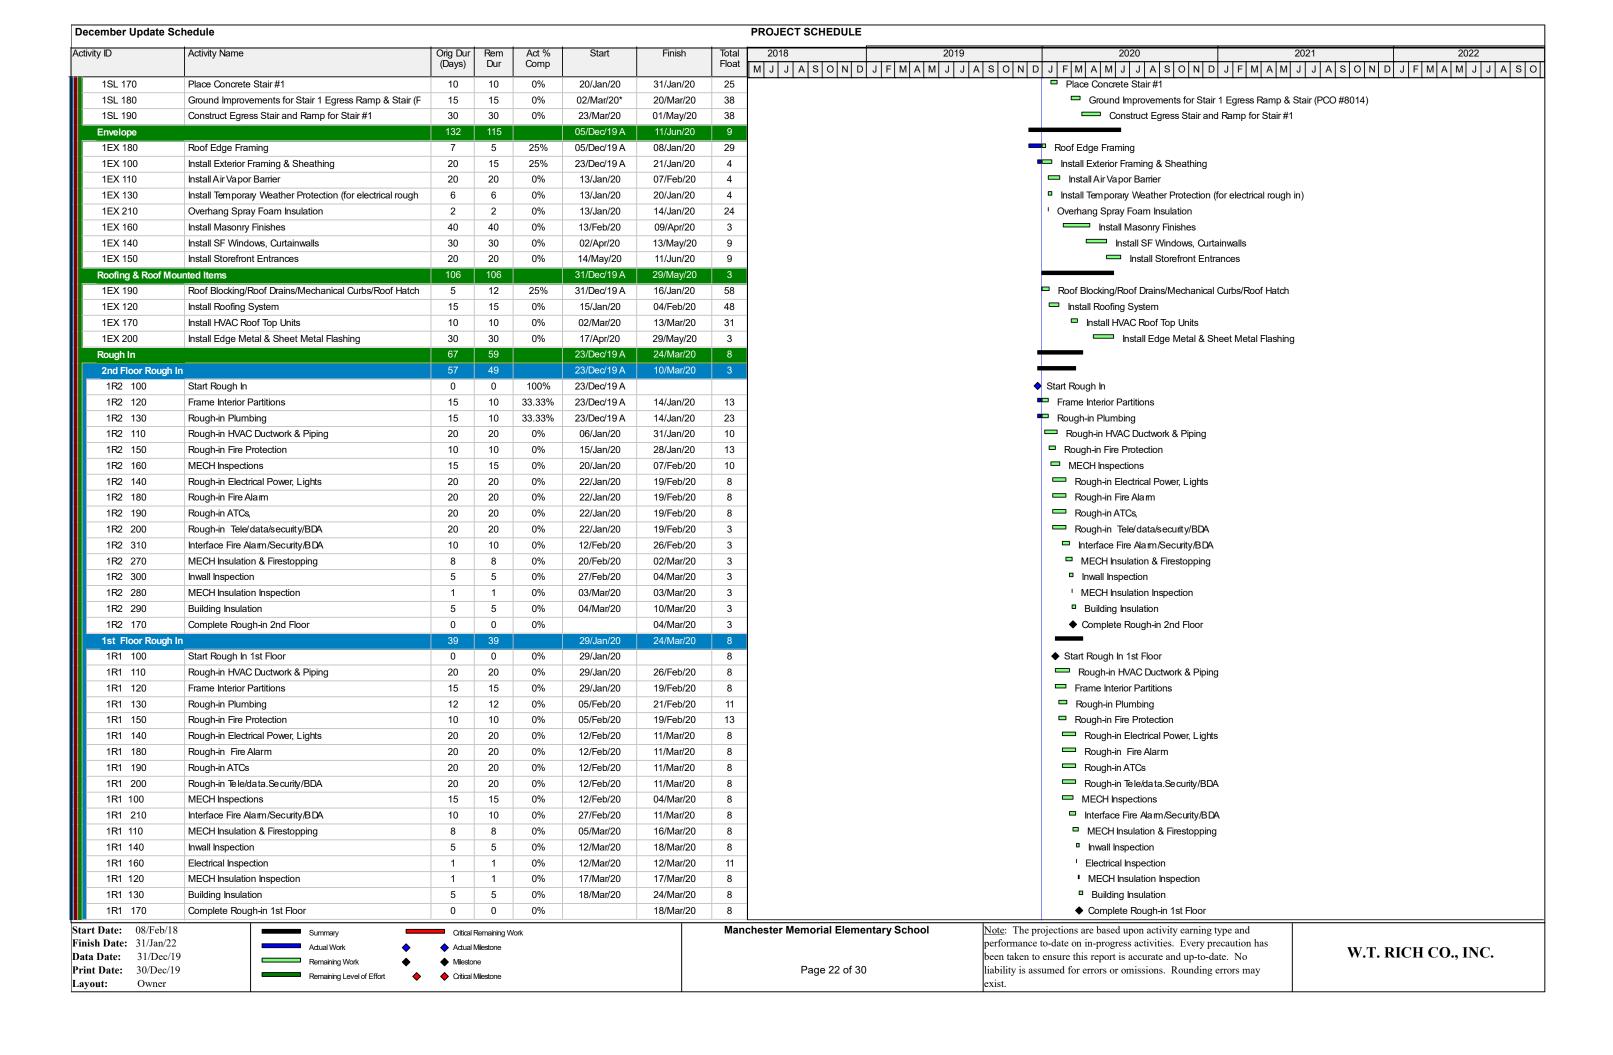


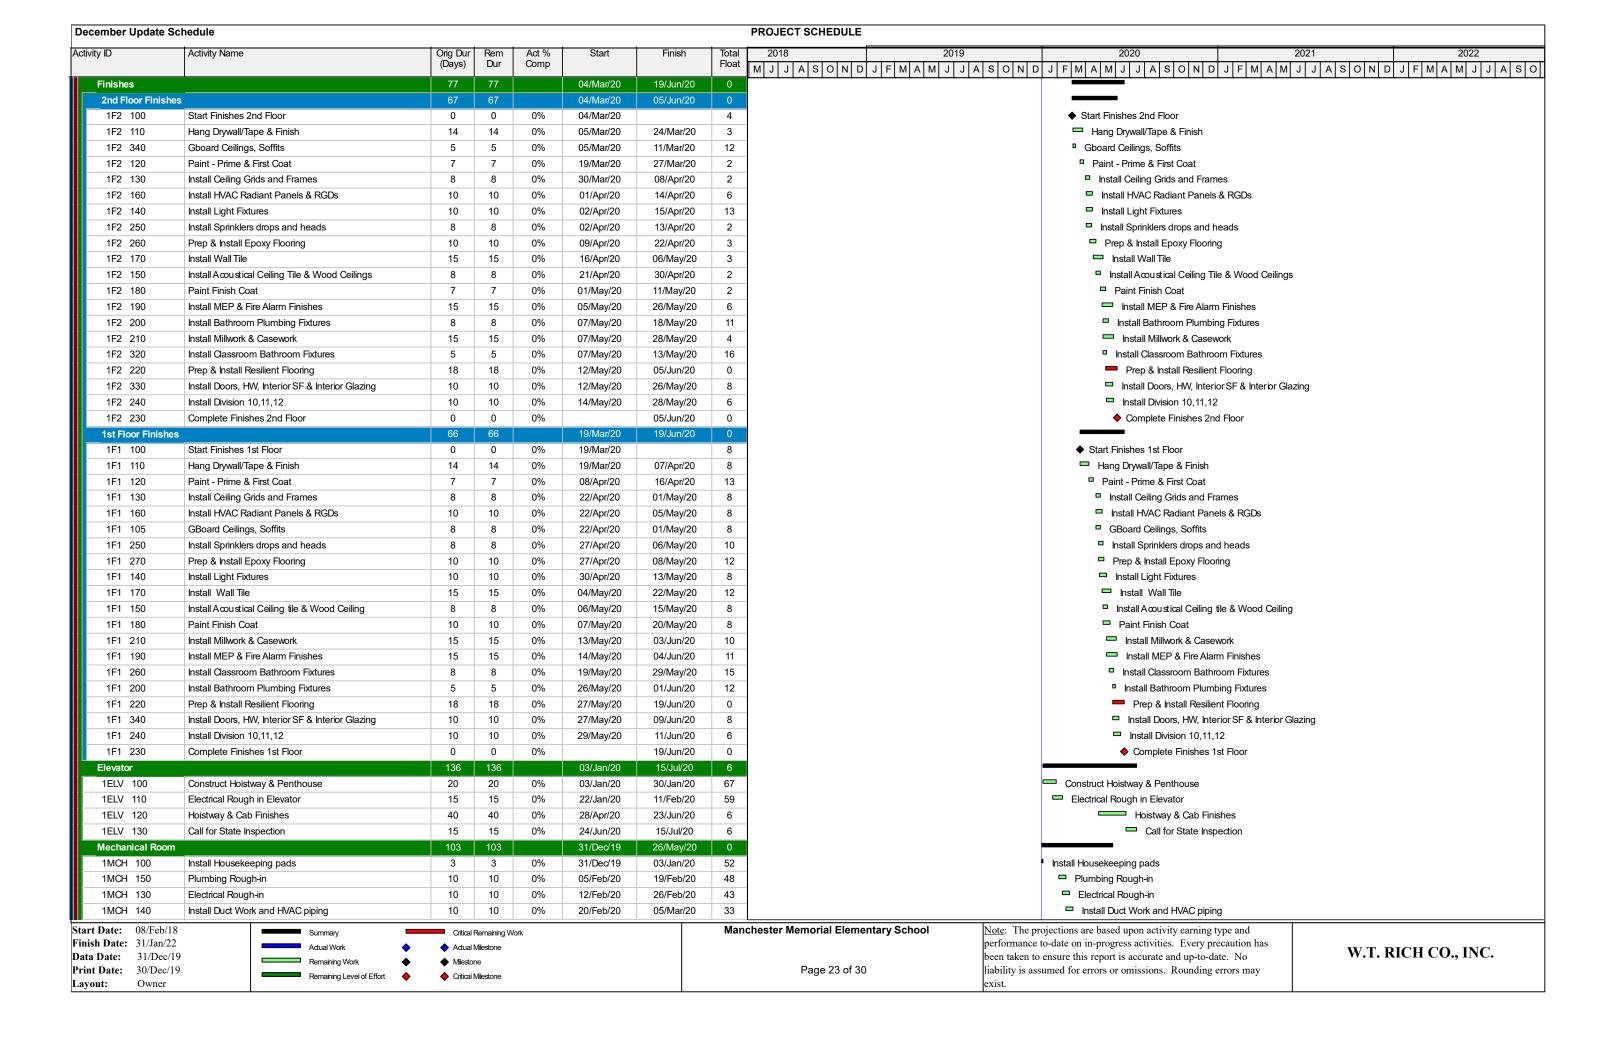


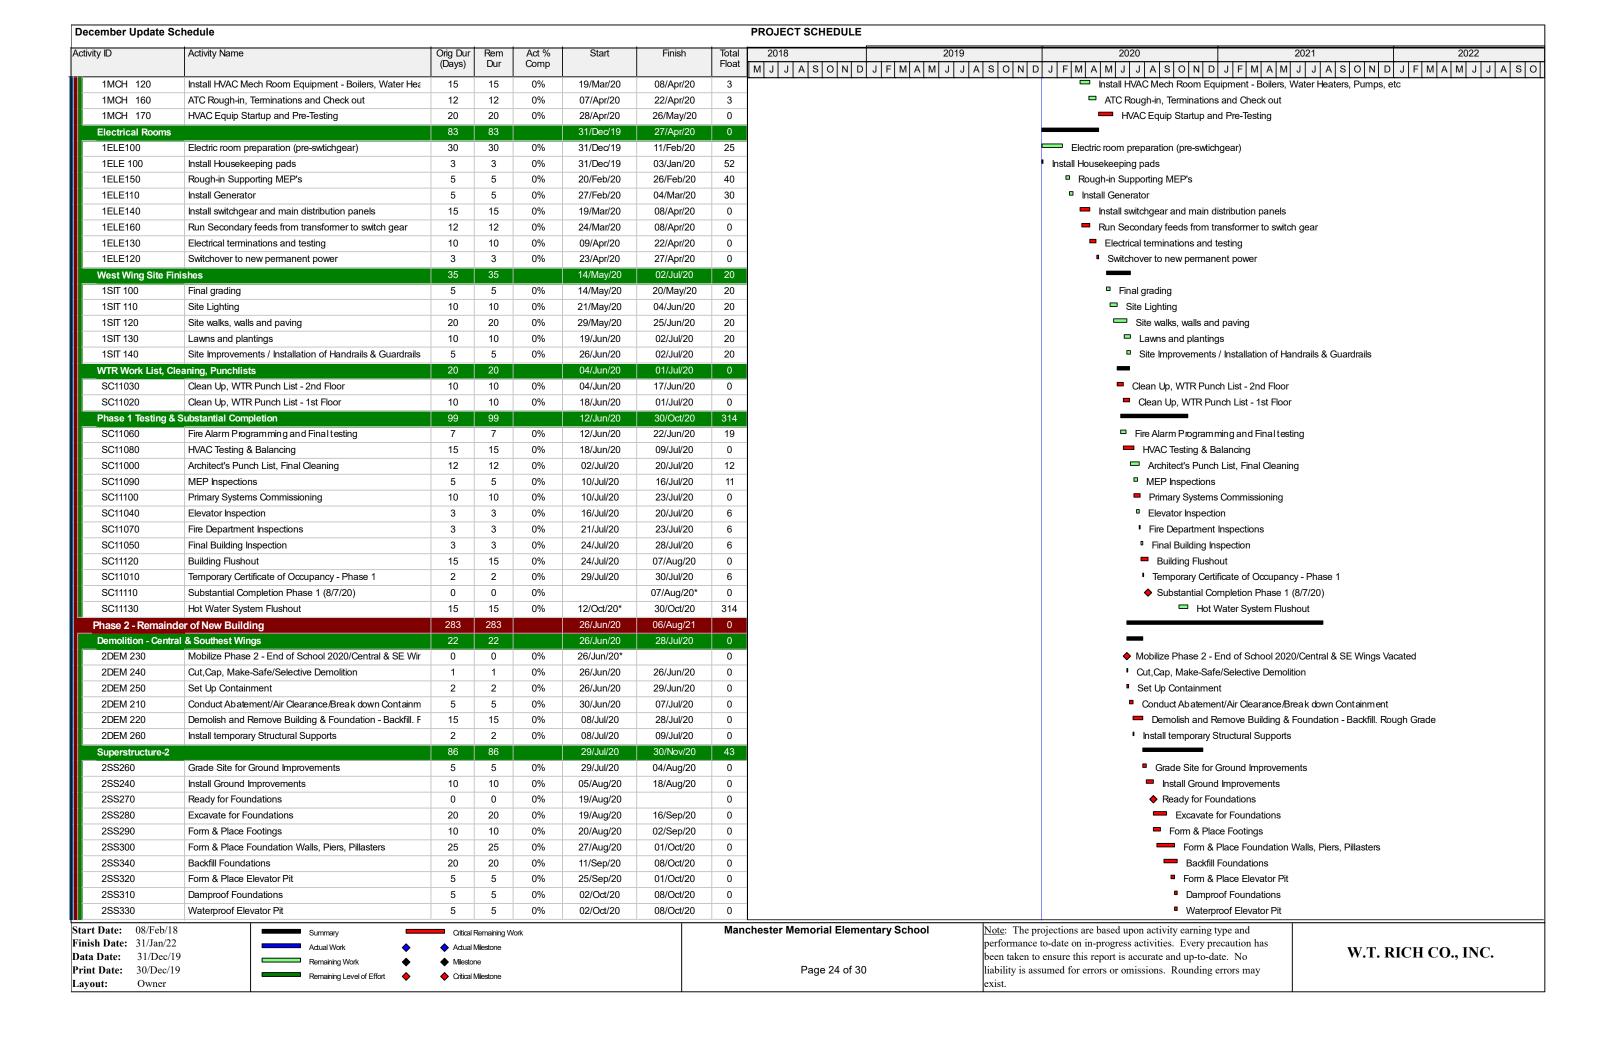


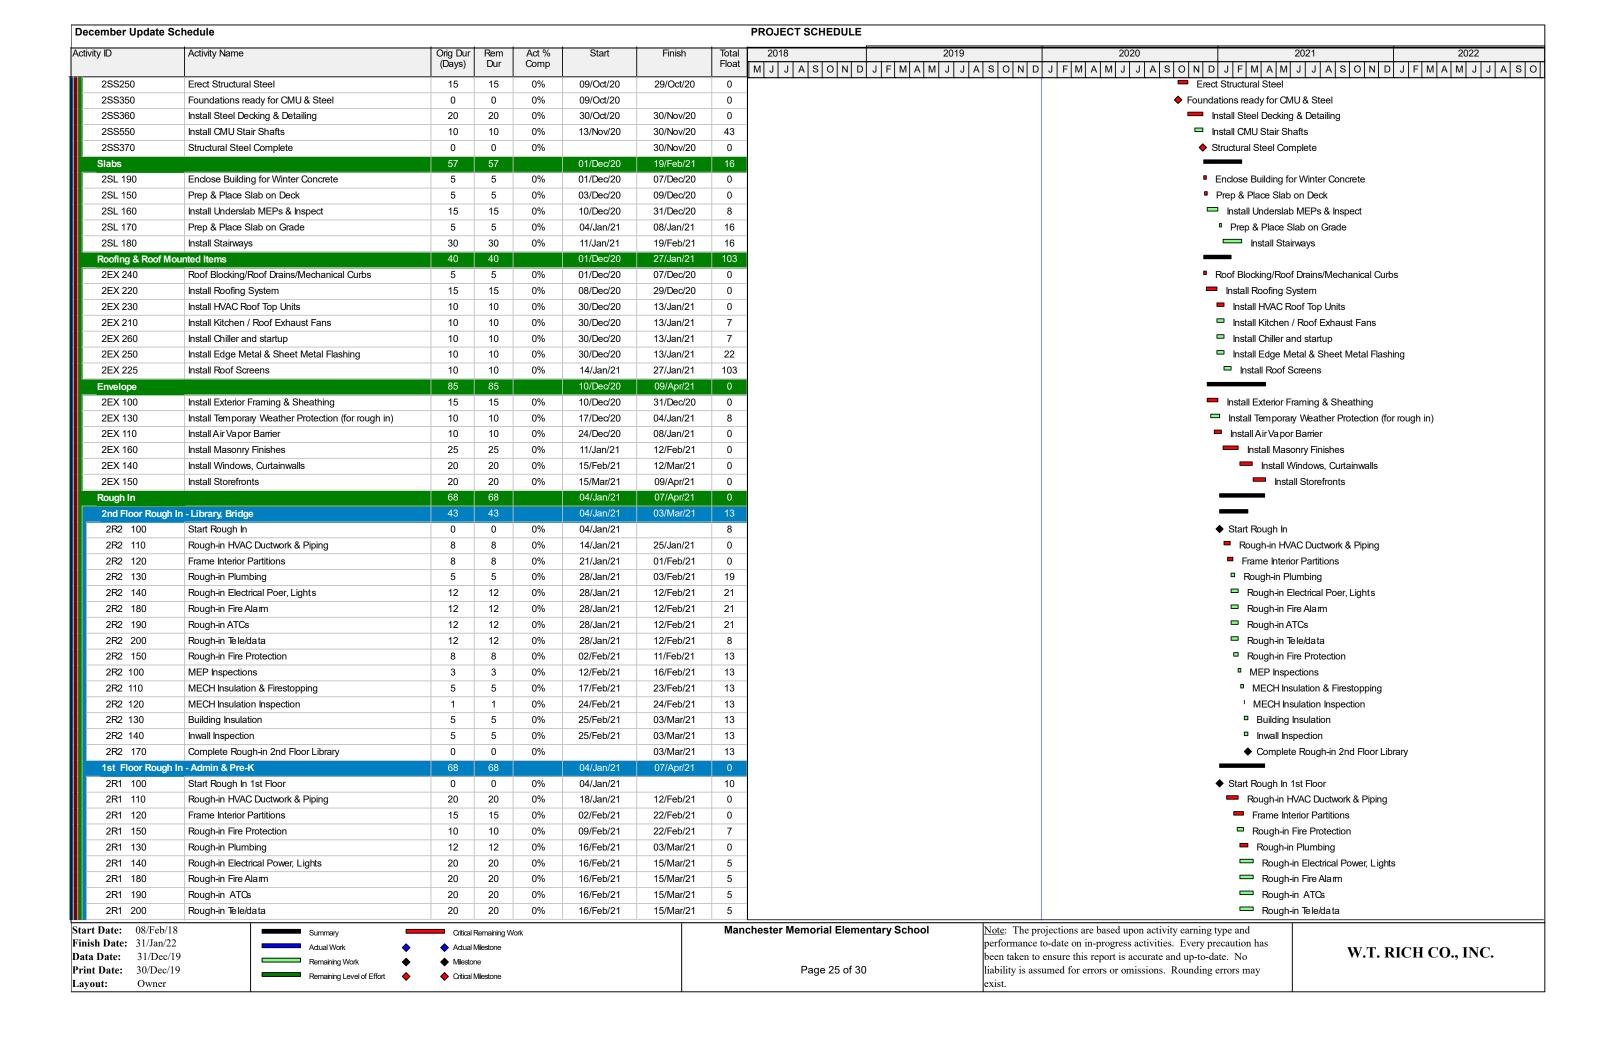

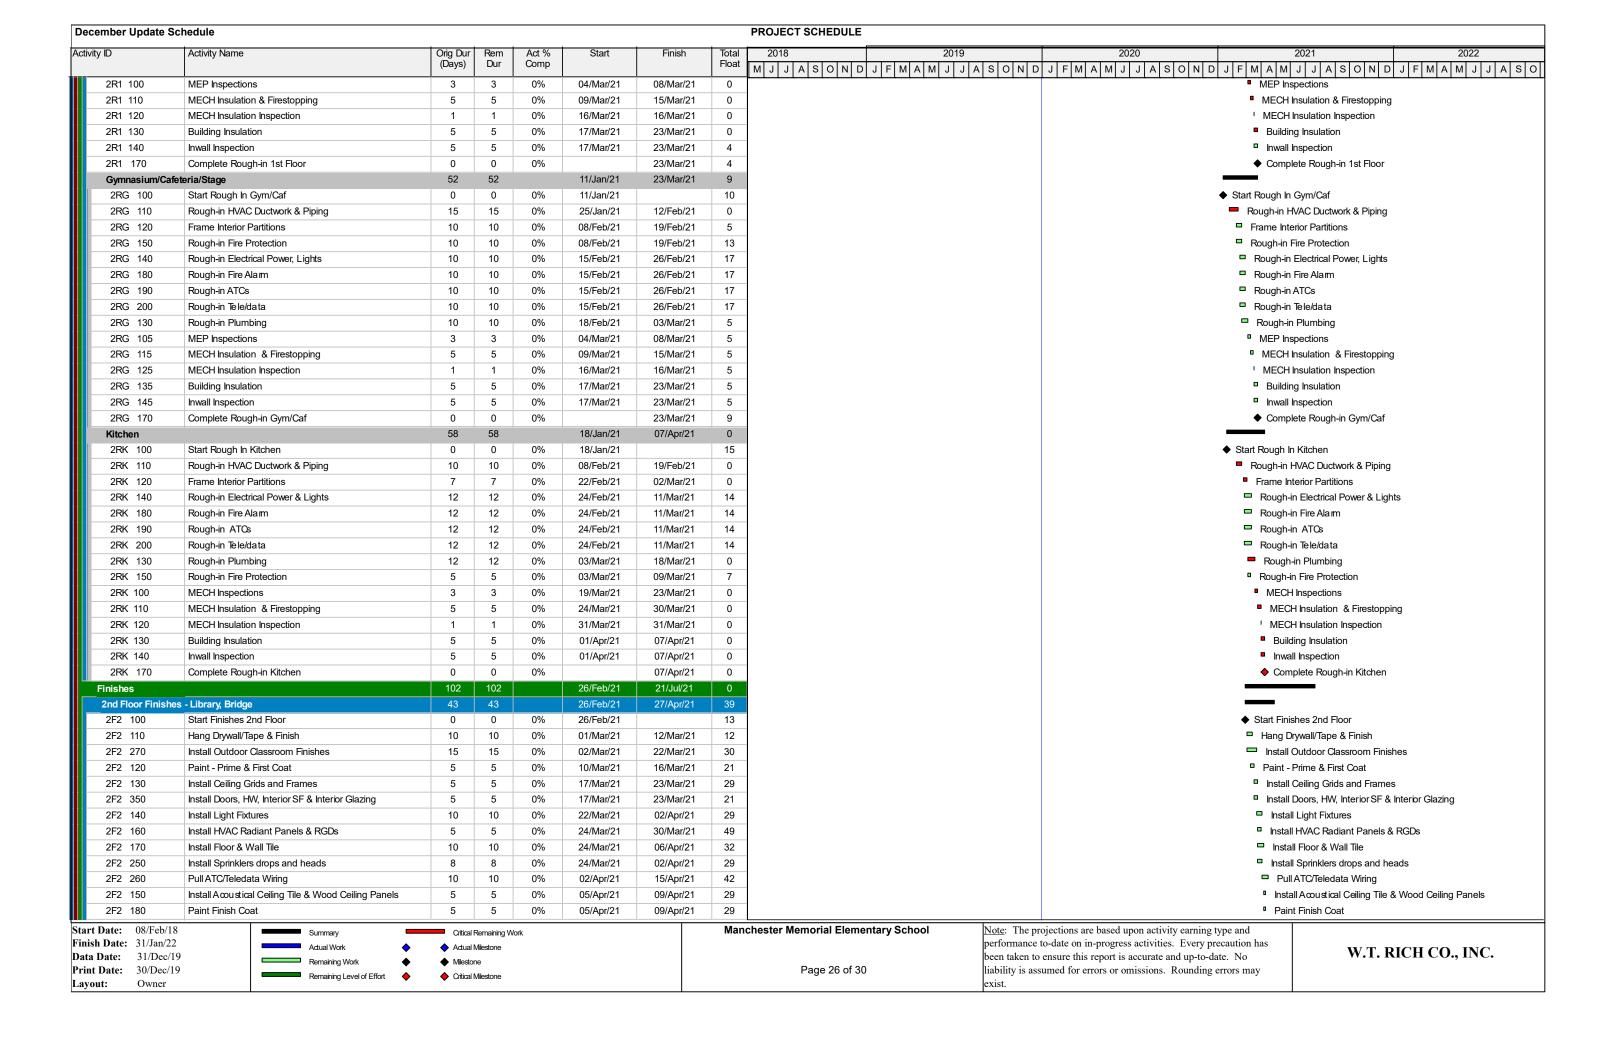


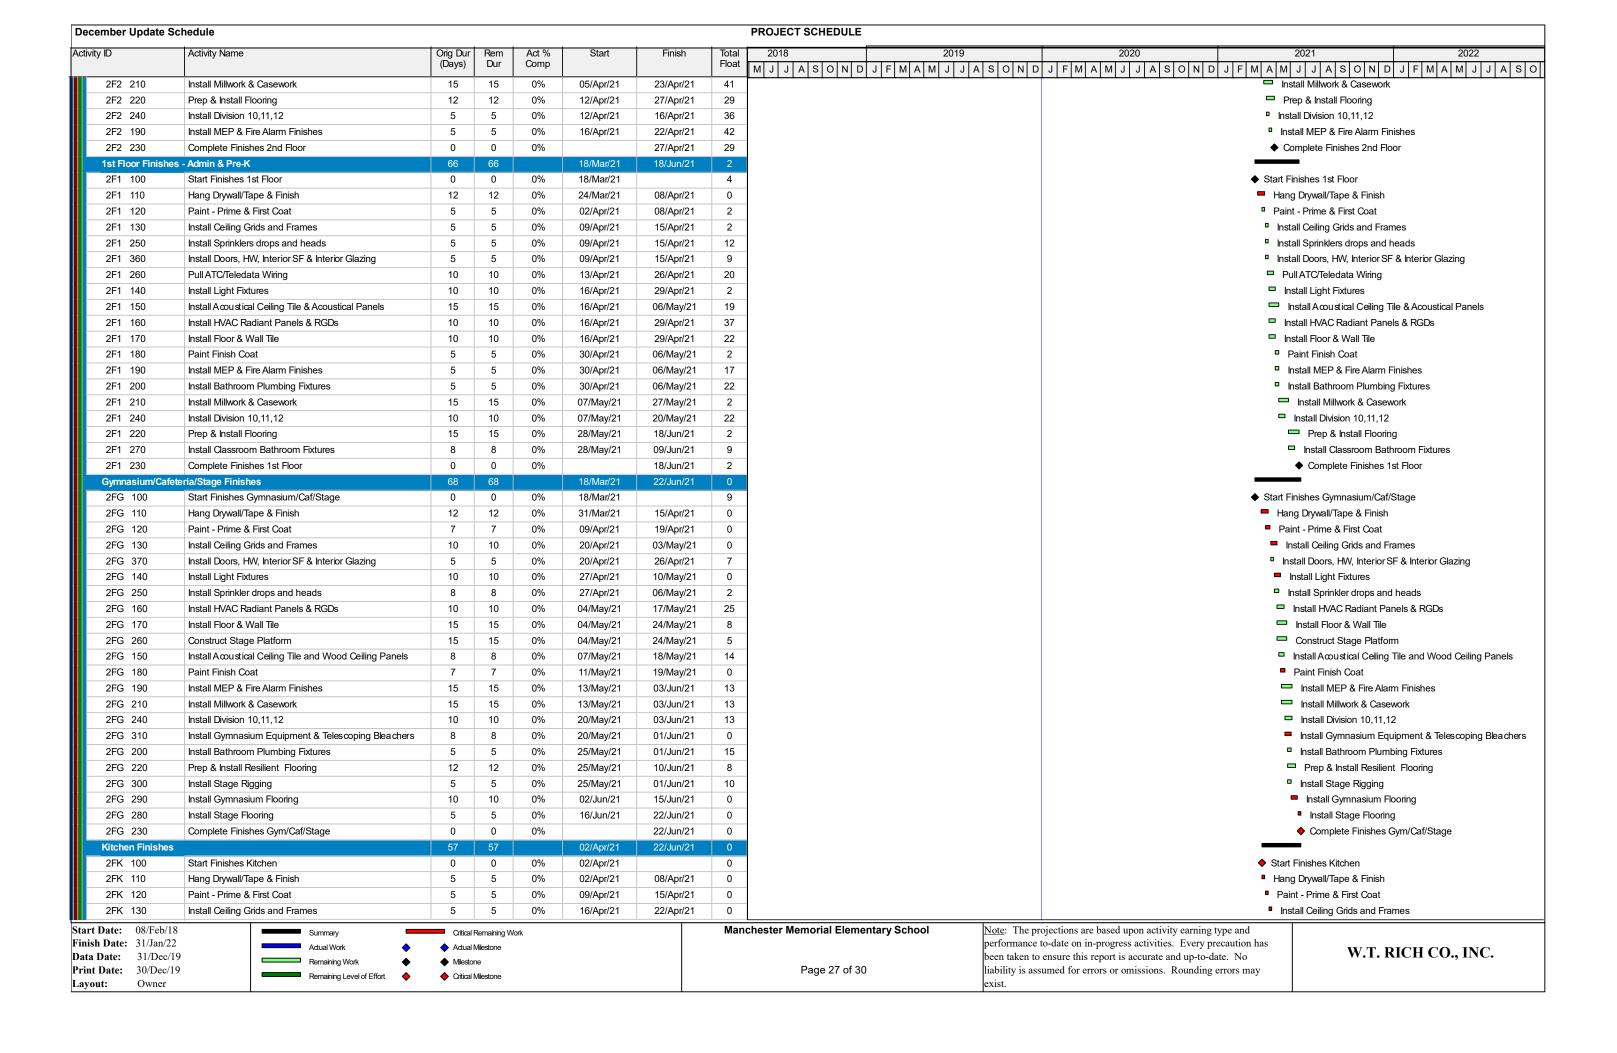

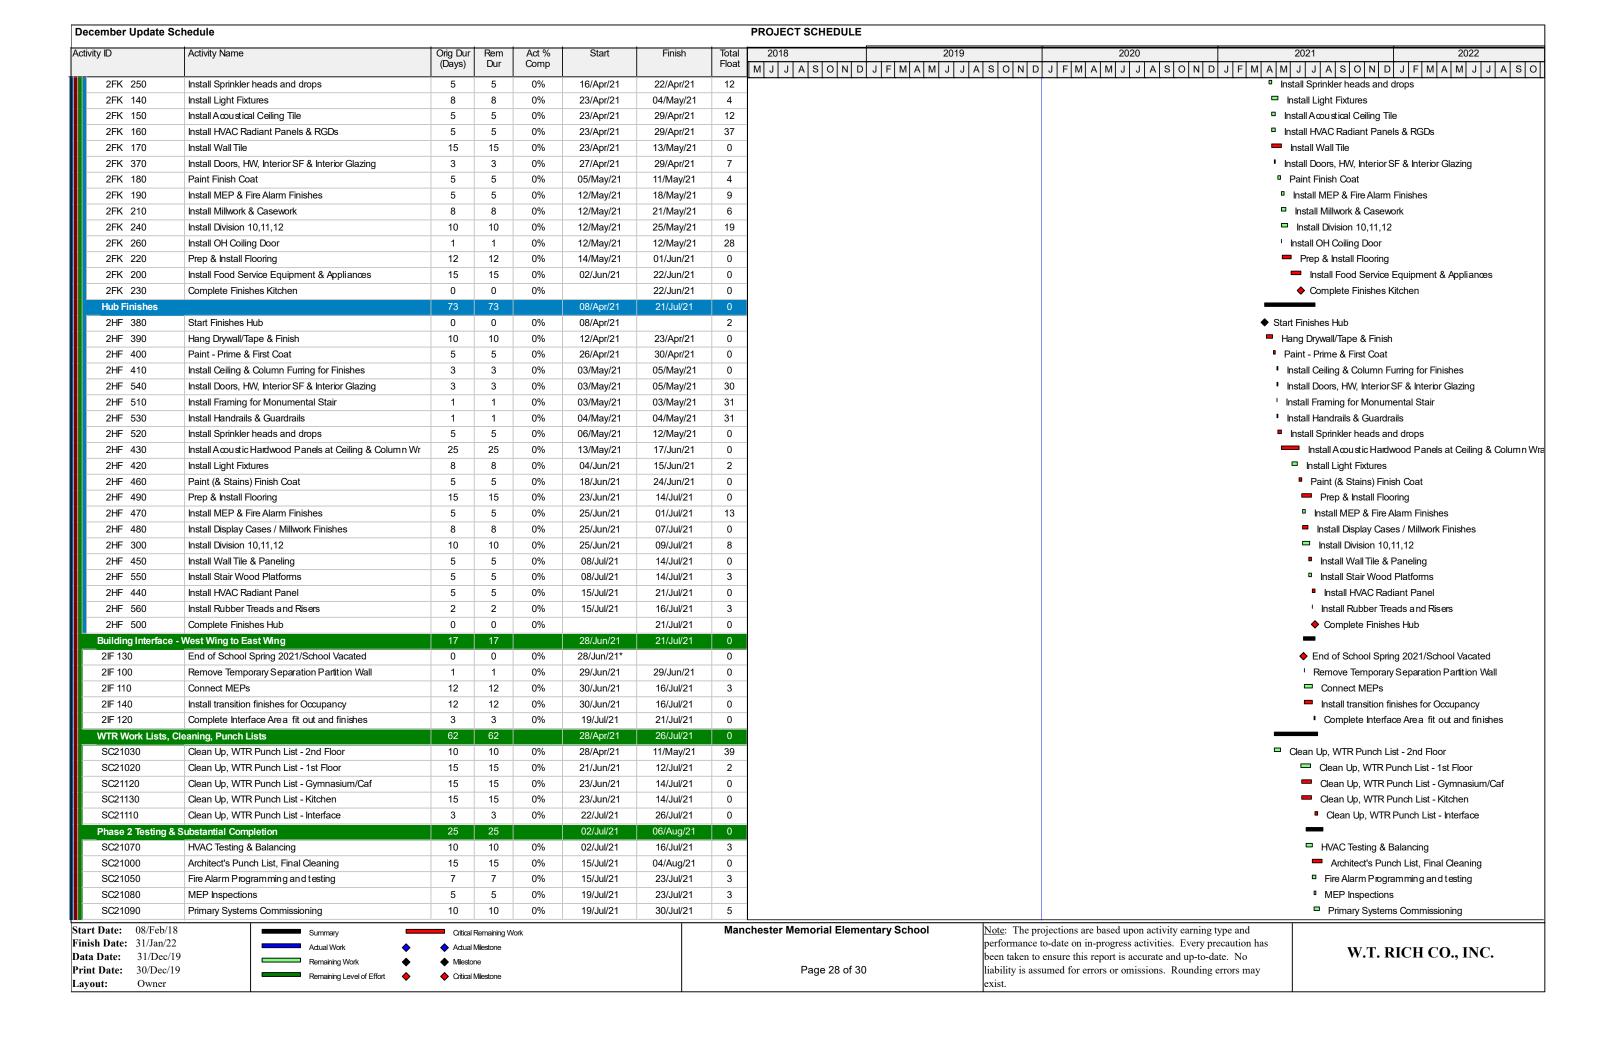

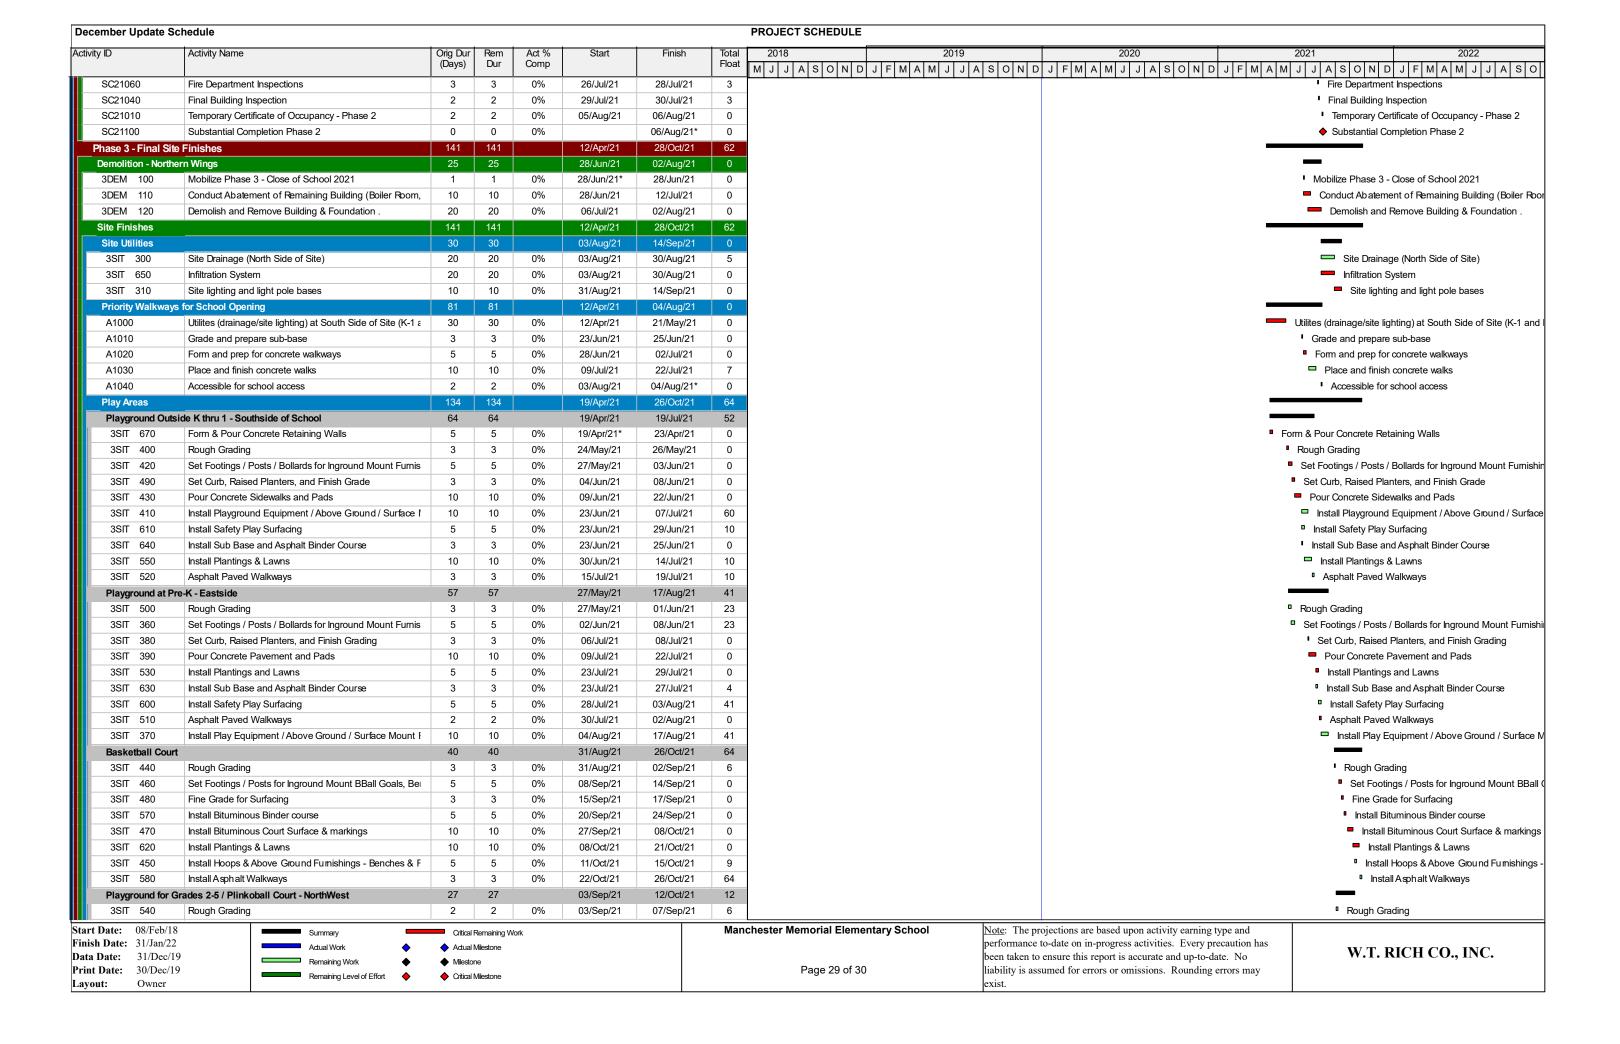

December Update Schedule PROJECT SCHEDULE											
ctivity ID	Activity Name	Orig Dur		Act %	Start	Finish	Total				
		(Days)	Dur	Comp			Float				
3SIT 320	Set Footings / Posts / Bollards for Inground Mount Furnis	5	5	0%	08/Sep/21	14/Sep/21	6	Set Footings / Posts / Bollards for Inground M			
3SIT 340	Set Flush Curb & Finish Grading	3	3	0%	08/Sep/21	10/Sep/21	6	Set Flush Curb & Finish Grading			
3SIT 350	Install Sub Base and Asphalt Binder Course	2	2	0%	13/Sep/21	14/Sep/21	16	<u> </u>			
3SIT 330	Install Safety Play Surfacing	5	5	0%	15/Sep/21	21/Sep/21	17	, , , ,			
3SIT 660	Install Plantings & Lawns	1	1	0%	15/Sep/21	15/Sep/21	16				
3SIT 700	Install Play Equipment / Above Ground / Surface Mount I	10	10	0%	22/Sep/21	05/Oct/21	17				
3SIT 560	Install Bituminous Court Surfacing and Markings	1	1	0%	11/Oct/21	11/Oct/21	12	· ·			
3SIT 590	Aphalt Paved Walkways	1	1	0%	12/Oct/21	12/Oct/21	12	¹ Aphalt Paved Walkways			
	sphalt Paving (at Demolished Bldg)	23	23		15/Sep/21	15/Oct/21	9				
3SIT 180	Final Prep for Sub-base	5	5	0%	15/Sep/21	21/Sep/21	16	·			
3SIT 190	Lay 8" Gravel Sub-base	5	5	0%	22/Sep/21	28/Sep/21	16	•			
3SIT 200	Install Curbs/Berms	5	5	0%	22/Sep/21	28/Sep/21	16	Install Curbs/Berms			
3SIT 210	Install Binder Course	5	5	0%	23/Sep/21	29/Sep/21	16				
3SIT 220	Install Top Course	5	5	0%	11/Oct/21	15/Oct/21	9	Install Top Course			
Main Entrance l	Plaza	28	28		13/Sep/21	20/Oct/21	68	<u> </u>			
3SIT 100	Grading Prep & Install Remaining Bases	5	5	0%	13/Sep/21	17/Sep/21	6	□ Grading Prep & Install Remaining Bases			
3SIT 110	Prep & Form Sidewalks	15	15	0%	20/Sep/21	08/Oct/21	6	Prep & Form Sidewalks			
3SIT 120	Pour Concrete Sidewalks	10	10	0%	23/Sep/21	06/Oct/21	6	□ Pour Concrete Sidewalks			
3SIT 130	Install Plantings & Lawn	10	10	0%	27/Sep/21	08/Oct/21	9	□ Install Plantings & Lawn			
3SIT 240	Install Bike Racks, Flag Poles, Planters, Site Furnishings	5	5	0%	30/Sep/21	06/Oct/21	78	Install Bike Racks, Flag Poles, Planters, Sit			
3SIT 690	Finish Exterior Canopy & Main Entrance Tie-ins	10	10	0%	07/Oct/21	20/Oct/21	6	□ Finish Exterior Canopy & Main Entrance			
General Site Finishes			29		20/Sep/21	28/Oct/21	0	<u> </u>			
3SIT 230	Install Traffic Signage	1	1	0%	20/Sep/21	20/Sep/21	23	¹ Install Traffic Signage			
3SIT 170	Landscape Work-to- Complete	5	5	0%	22/Oct/21	28/Oct/21	0	Landscape Work-to- Complete			
Completion and	Closeout - Phase 3	77	77		08/Oct/21	31/Jan/22	0				
3CO 100	Final Site As-Builts & Warrantees	20	20	0%	08/Oct/21	04/Nov/21	57	Final Site As-Builts & Warrantees			
3CO 110	Completion of site contract work	0	0	0%		28/Oct/21	0	◆ Completion of site contract work			
3CO 120	Landscape Architect's Punch List	5	5	0%	29/Oct/21	04/Nov/21	0	Landscape Architect's Punch List			
3CO 130	Design / Owner Affidavits / Final insp, Cert. of Occupancy	5	5	0%	04/Nov/21	10/Nov/21	12	Design / Owner Affidavits / Final insp, C			
3CO 180	Correction of all remaning punch list items	15	15	0%	05/Nov/21	29/Nov/21	0	Correction of all remaning punch list			
3CO 140	PROJECTED Substantial Completion - Phase 3	0	0	0%		29/Nov/21	0	◆ PROJECTED Substantial Completion			
3CO 150	REQUIRED Substantial Completion - Phase 3	0	0	0%		30/Nov/21*	0	♦ REQUIRED Substantial Completion			
3CO 190	Project Closeout documentation	40	40	0%	30/Nov/21	26/Jan/22	2	Project Closeout documentat			
3CO 160	PROJECTED Final Project Completion	0	0	0%		26/Jan/22	2	◆ PROJECTED Final Project Co			
3CO 170	REQUIRED Project Final Completion	0	0	0%		31/Jan/22*	0	♦ REQUIRED Project Final Con			






Upload Date

2019/12/31 07:53:14

2019/12/31 07:54:01

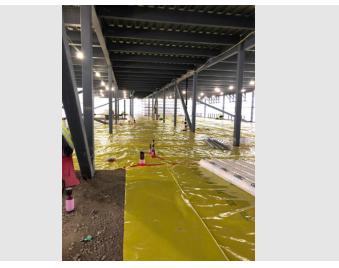

Description



File Name

29AE9FE0-23F1-4BF3-8E5C-C131...



Upload Date 2019/12/30 13:26:29

Description

Uploaded By Trishya Patel

> **File Name** 9BCE2CB5-C2C0-43F7-870E-F9A...



Description

Uploaded By Trishya Patel **File Name**

Taken Date 2019/12/30 12:57:29 **Upload Date**

Description

Uploaded By Trishya Patel **File Name**

2019/12/30 12:57:40 05D7A4BF-A221-4E7C-A2D1-627...

2019/12/30 12:59:35


2019/12/30 12:59:32

Taken Date


Upload Date

D6AB4085-4A66-4FF2-9DB1-53B...

Page 2 of 26





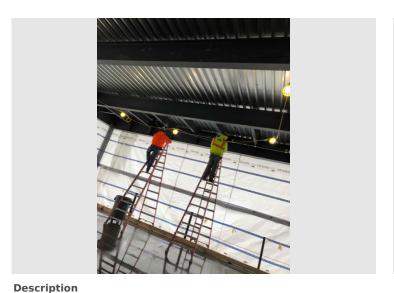

Description

Taken Date 2019/12/30 12:57:09

2019/12/30 12:57:12

Upload Date

Uploaded By Trishya Patel

File Name 9AD3402A-0038-4697-A977-A57...


Taken Date 2019/12/30 09:01:35

Upload Date 2019/12/30 09:01:39

Uploaded By Trishya Patel

File Name

7F68B9CF-CAA8-43D4-A3CB-993...

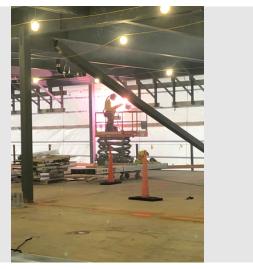

Description

Upload Date

Description

Taken Date 2019/12/30 08:19:42

2019/12/30 08:19:44

Uploaded By Trishya Patel


File Name 4963470E-75A9-45F9-980F-C4F3...

Taken Date 2019/12/30 08:03:35

Upload Date 2019/12/30 08:04:21 **Uploaded By** Trishya Patel

File Name

7167CD80-C83E-4E05-8601-959...









File Name

Taken Date Uploaded By 2019/12/30 06:56:19 Trishya Patel

Upload Date


Upload Date

2019/12/30 06:56:22 B66101E0-0AA8-458C-8EF5-7019... **Taken Date Uploaded By** 2019/12/28 12:20:36 Trishya Patel

Upload Date File Name

2019/12/28 12:20:40 DE31D007-4DA8-4739-AADF-18F...

File Name

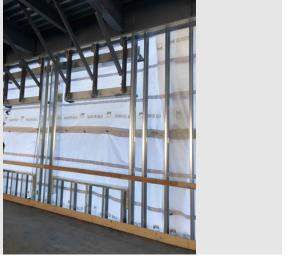


Description Description

File Name

Taken Date Uploaded By Taken Date Uploaded By 2019/12/28 12:20:30 Trishya Patel 2019/12/28 11:16:47 Trishya Patel

2019/12/28 12:20:38 2019/12/28 11:16:51 353CF94C-F04D-4791-96F8-8B18... 9A90A86C-1CE8-4E7E-ABE3-BB9...

Upload Date







Description

Taken Date 2019/12/28 09:55:46

2019/12/28 09:55:48

Upload Date

Uploaded By Trishya Patel

File Name 0753EC44-708B-499D-9E16-EDA...


Taken Date 2019/12/28 09:55:00

Upload Date 2019/12/28 09:55:02

Uploaded By Trishya Patel

File Name

F0B40A27-5119-452F-9944-7CBA...



Description

Description

Taken Date 2019/12/28 07:35:32

2019/12/28 07:38:49

Upload Date

Uploaded By Trishya Patel

File Name E22570F2-67BB-4F33-AF63-C1DB...


Taken Date 2019/12/28 07:35:13

Upload Date 2019/12/28 07:38:43

Uploaded By Trishya Patel

File Name

D4C32940-F9C6-4FE8-A8FC-C5B...







Description

2019/12/27 11:05:35

Uploaded ByRick Lawrence

 Upload Date
 File Name

 2019/12/28 12:04:11
 DSC03084.JPG



Description

Taken Date
Uploaded By
2019/12/27 08:49:09
Rick Lawrence
Upload Date
File Name

 Upload Date
 File Name

 2019/12/28 12:03:48
 DSC03070.JPG




Description

Taken DateUploaded By2019/12/27 11:04:50Rick Lawrence

 Upload Date
 File Name

 2019/12/28 12:04:11
 DSC03083.JPG

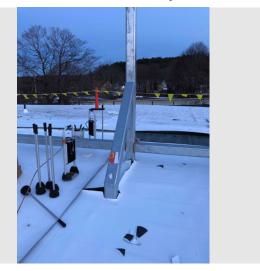


Description

2019/12/26 16:33:14

Taken DateUploaded By2019/12/26 16:33:08Trishya Patel


Upload Date File Name

B99F9F4E-CBFD-4AF2-88B0-79E9...







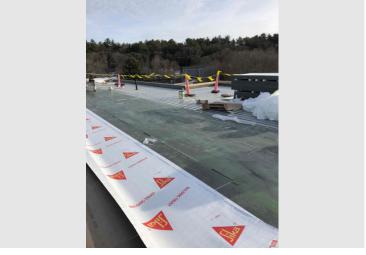

Description

Taken Date 2019/12/26 16:32:58

2019/12/26 16:33:08

Upload Date

Uploaded By Trishya Patel

File Name AC708436-1568-4852-9774-1BCF...


Taken Date 2019/12/26 14:15:18

Upload Date 2019/12/26 14:15:20

Uploaded By Trishya Patel

File Name

37BC3AA7-3C95-4B52-A103-310...

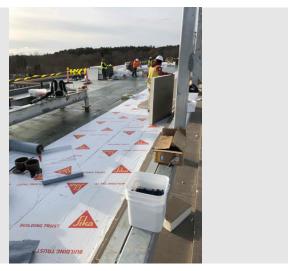

Description

Description

Taken Date2019/12/26 14:13:42 **Upload Date**

2019/12/26 14:13:45

Uploaded By Trishya Patel

File Name0DDC60D1-8EAC-4A10-8AC1-C82...


Taken Date 2019/12/26 14:13:40

Upload Date 2019/12/26 14:13:43

Uploaded By Trishya Patel

File Name

E5758D04-EB3B-4046-95AA-08B...







Description

2019/12/26 11:16:37

Uploaded ByRick Lawrence

 Upload Date
 File Name

 2019/12/27 07:17:23
 DSC03058.JPG




Description

Taken DateUploaded By2019/12/26 08:35:11Rick Lawrence

 Upload Date
 File Name

 2019/12/27 07:16:55
 DSC03039.JPG

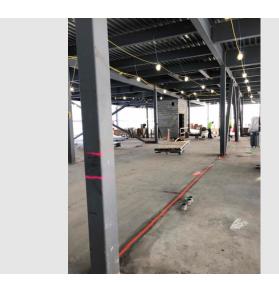

Description

Taken DateUploaded By2019/12/26 08:44:41Trishya Patel

Upload Date File Name

2019/12/26 08:44:47 399D1DB8-697B-4430-B3B7-97A...




Description


Taken DateUploaded By2019/12/24 10:39:09Rick Lawrence

 Upload Date
 File Name

 2019/12/26 09:51:11
 DSC03029.JPG





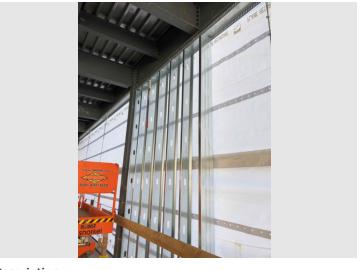



Uploaded By

Rick Lawrence

Description

Description

Taken Date 2019/12/24 09:34:03

Upload Date 2019/12/24 09:35:01

Uploaded By Trishya Patel

File Name

4FB0D1EB-EB14-4EB6-A239-312...

Taken Date 2019/12/24 09:27:28

Upload Date File Name 2019/12/26 09:51:09 DSC03022.JPG



Description

Description

Taken Date 2019/12/24 08:32:49 **Upload Date**


2019/12/24 08:32:54

Uploaded By Trishya Patel

File Name DF8157E4-FF3E-4E3D-B2DC-972... **Taken Date** 2019/12/23 12:11:32

Upload Date 2019/12/24 07:24:06 **Uploaded By** Rick Lawrence

File Name DSC03011.JPG







Description

2019/12/23 10:27:25

Uploaded ByRick Lawrence

 Upload Date
 File Name

 2019/12/24 07:23:59
 DSC03006.JPG




Description

Taken DateUploaded By2019/12/23 10:18:57Rick Lawrence

 Upload Date
 File Name

 2019/12/24 07:23:59
 DSC03001.JPG

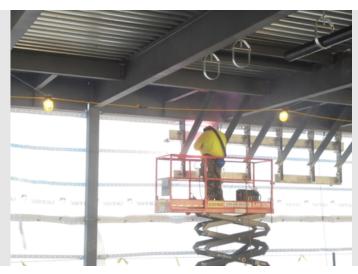

Description

Taken DateUploaded By2019/12/23 10:20:32Rick Lawrence

 Upload Date
 File Name

 2019/12/24 07:23:58
 DSC03002.JPG




Description


Taken DateUploaded By
2019/12/23 09:02:34
Rick Lawrence

 Upload Date
 File Name

 2019/12/24 07:23:48
 DSC02996.JPG






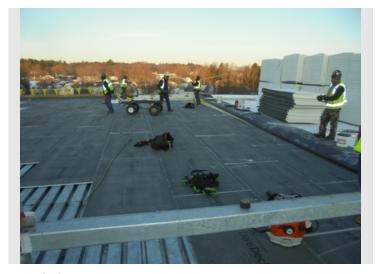



Uploaded By Rick Lawrence

File Name 2019/12/24 07:23:50 DSC02994.JPG



Description

Taken Date

Upload Date

2019/12/20 14:36:22

2019/12/20 14:36:25

Taken Date

Upload Date

2019/12/23 08:48:14

Uploaded By Trishya Patel **File Name**

18A7E334-ACDF-4F1A-A8CF-3151...



Description

Taken Date Uploaded By 2019/12/20 14:43:46 Trishya Patel

Upload Date File Name


2019/12/20 14:43:48 60C8CB62-62B3-45EF-80C3-4FE1...



Description

Taken Date

Uploaded By 2019/12/20 12:01:49 Rick Lawrence **Upload Date File Name** 2019/12/23 07:15:39 DSC02982.JPG









Description

Taken Date 2019/12/20 08:53:54

Upload Date 2019/12/20 08:53:57

Uploaded By Trishya Patel

File Name

DDE0CFA5-1B1E-4484-B6BB-D51...

Taken Date Uploaded By 2019/12/20 08:42:37 Trishya Patel

Upload Date File Name

2019/12/20 08:42:40 F6FE9A52-0D04-4E47-ADF7-DC3...







Description

Taken Date 2019/12/19 09:44:53


Upload Date 2019/12/19 09:44:58

Uploaded By Trishya Patel

File Name 23F39098-DBCC-4C5C-911A-145... **Taken Date** 2019/12/18 09:02:48

Upload Date 2019/12/19 07:18:19 **Uploaded By** Rick Lawrence

File Name DSC02924.JPG







Description

Taken DateUploaded By2019/12/18 08:55:40Rick Lawrence

 Upload Date
 File Name

 2019/12/19 07:18:16
 DSC02922.JPG



DSC02913.JPG

Description

2019/12/18 07:20:10

Taken Date
Uploaded By
2019/12/17 15:11:04
Rick Lawrence
Upload Date
File Name



Description

Taken DateUploaded By2019/12/18 07:20:25Trishya Patel

Upload Date File Name

2019/12/18 07:20:28 A17601D0-786B-4121-ABD6-CD4...




Description

 Taken Date
 Uploaded By

 2019/12/17 15:10:55
 Rick Lawrence

 Upload Date
 File Name

 2019/12/18 07:20:11
 DSC02912.JPG









2019/12/17 11:04:30

Taken Date

Uploaded By Rick Lawrence

Upload Date File Name 2019/12/18 07:20:06 DSC02907.JPG



Description

Taken Date

Upload Date

2019/12/16 13:49:04

2019/12/16 13:49:09

Uploaded By Trishya Patel

File Name



Taken Date Uploaded By 2019/12/17 10:55:55 Rick Lawrence

Upload Date File Name 2019/12/18 07:20:03 DSC02903.JPG



Description


C686657A-E6C6-4D89-947D-B33...

Taken Date 2019/12/16 13:34:53

Upload Date 2019/12/16 13:35:03 **Uploaded By** Trishya Patel

File Name

46C9504A-9675-4363-A67B-6DF...







Description

Taken DateUploaded By2019/12/16 10:39:33Rick Lawrence

 Upload Date
 File Name


 2019/12/17 12:26:47
 DSC02868.JPG



Description

Taken Date
Uploaded By
2019/12/16 08:50:59
Rick Lawrence
Upload Date
File Name

Upload Date File Name
2019/12/17 12:26:36 DSC02842.JPG

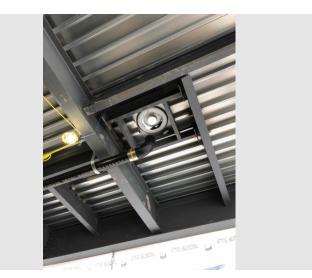


Description

Taken DateUploaded By2019/12/16 09:34:28Trishya Patel

Upload Date File Name

2019/12/16 09:34:34 CCAF98CB-E6CE-4809-AC15-192...




Description

Taken DateUploaded By2019/12/16 08:24:53Trishya Patel

Upload Date File Name

2019/12/16 08:24:59 4C6CFFF2-D8F7-4F94-93A6-C3DF...









Description

Taken Date 2019/12/13 11:18:18

Description

Upload Date 2019/12/17 12:25:09

Uploaded By Rick Lawrence

File Name DSC02840.JPG **Taken Date** 2019/12/13 10:36:02

Upload Date 2019/12/17 12:25:10 **Uploaded By** Rick Lawrence

File Name DSC02839.JPG





Taken Date

File Name FE4CC757-0D05-47CD-B78A-790...

Uploaded By

Trishya Patel


Taken Date 2019/12/13 09:09:10

Description

Upload Date 2019/12/17 12:25:07 **Uploaded By** Rick Lawrence

File Name DSC02833.JPG


2019/12/13 10:13:50









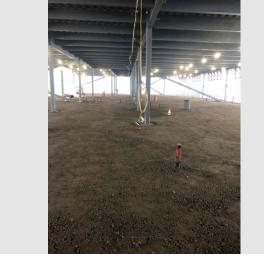

Description

Taken Date 2019/12/13 08:36:09

Upload Date 2019/12/17 12:25:02

Uploaded By Rick Lawrence

File Name DSC02825.JPG **Taken Date** 2019/12/13 07:34:53

Upload Date 2019/12/13 07:34:57 **Uploaded By** Trishya Patel

File Name

8C9330E2-F7B1-4393-9F1C-8FE8...



4D6EB686-44EC-4F70-A362-D5E...

Description

2019/12/13 07:33:41


Taken Date Uploaded By 2019/12/13 07:33:37 Trishya Patel **Upload Date File Name**



Uploaded By

Taken Date

2019/12/12 14:09:51 Rick Lawrence **Upload Date File Name** 2019/12/13 07:13:38 DSC02820.JPG







Description

Taken Date Uploaded By 2019/12/12 13:21:22 Rick Lawrence

Upload Date File Name 2019/12/13 07:13:38 DSC02817.JPG



DSC02794.JPG

Description

2019/12/13 07:13:14

Taken Date Uploaded By 2019/12/12 09:41:16 Rick Lawrence **Upload Date File Name**

Description

Taken Date Uploaded By 2019/12/12 13:18:26 Rick Lawrence


Upload Date File Name 2019/12/13 07:13:37 DSC02816.JPG



Description

Taken Date

Uploaded By 2019/12/12 09:36:30 Rick Lawrence **Upload Date File Name** 2019/12/13 07:13:18 DSC02791.JPG







Description

Taken DateUploaded By2019/12/12 09:16:20Rick Lawrence

 Upload Date
 File Name

 2019/12/13 07:13:22
 DSC02787.JPG



Description

Taken DateUploaded By2019/12/11 15:24:56Rick Lawrence

 Upload Date
 File Name

 2019/12/12 07:30:32
 DSC02782.JPG



Description

Taken DateUploaded By2019/12/12 09:00:32Rick Lawrence

 Upload Date
 File Name

 2019/12/13 07:13:11
 DSC02785.JPG




Description

Taken DateUploaded By2019/12/11 14:24:30Rick Lawrence

 Upload Date
 File Name

 2019/12/12 07:30:32
 DSC02780.JPG







Description

2019/12/11 14:09:06

Uploaded By
Rick Lawrence

 Upload Date
 File Name

 2019/12/12 07:30:27
 DSC02774.JPG



Description

Taken DateUploaded By2019/12/11 13:05:24Rick Lawrence

 Upload Date
 File Name

 2019/12/12 07:30:25
 DSC02769.JPG




Description

Taken DateUploaded By2019/12/11 14:08:20Rick Lawrence

 Upload Date
 File Name


 2019/12/12 07:30:26
 DSC02772.JPG




Description

Taken DateUploaded By2019/12/09 10:05:20Trishya Patel

Upload Date File Name









Upload Date

2019/12/09 10:05:18

2019/12/09 10:08:39

Uploaded By

File Name

Trishya Patel

DFA819EC-5A7B-4E0E-8991-0157...



Description

Taken Date Uploaded By 2019/12/09 06:54:17 Trishya Patel

Upload Date 2019/12/09 06:54:21

B9BEB61A-922C-4B5B-8702-904...

File Name



Description

Upload Date

Description

Taken Date 2019/12/06 15:38:24

2019/12/06 15:38:28


Uploaded By Trishya Patel

File Name 909FB33F-FFEE-4A65-85F5-2E26... **Taken Date** 2019/12/06 14:06:25


Upload Date 2019/12/06 14:06:29 **Uploaded By** Trishya Patel

File Name

031AB2BE-4A36-467B-889D-674...





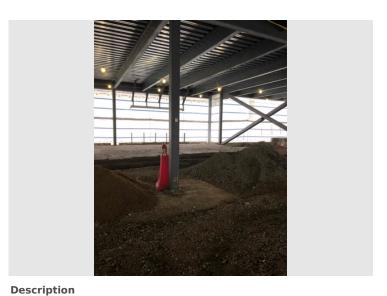



Description

Taken Date 2019/12/06 13:43:03

Upload Date 2019/12/06 13:43:09


Uploaded By Trishya Patel

File Name1A56F61A-0737-4CF4-B48F-DDE...

Taken Date 2019/12/06 12:01:05

Upload Date 2019/12/09 07:34:38 Uploaded By
Rick Lawrence

File Name DSC02707.JPG



Description

Uploaded By Trishya Patel

File Name

93567ED2-8393-474E-A6C5-7CA...

Description

Taken Date

Upload Date 2019/12/05 14:09:37

2019/12/05 14:09:27

Uploaded By Trishya Patel


File Name

D537CA9C-1396-4249-A80D-4B5...


2019/12/05 14:09:39 **Upload Date**2019/12/05 14:10:18


Taken Date

Page 22 of 26





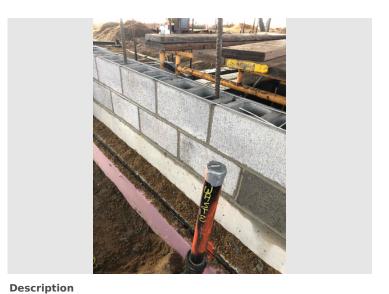

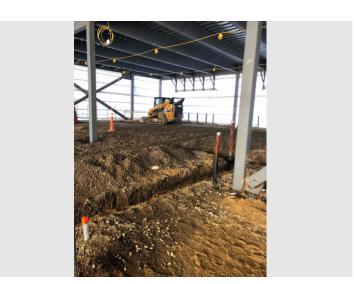

Description

Taken Date 2019/12/05 13:42:14

Upload Date 2019/12/05 13:42:17

Uploaded By Trishya Patel

File Name 5720E222-9577-42DC-BC6D-3E2... **Taken Date** 2019/12/05 12:08:46

Upload Date 2019/12/05 12:22:54 **Uploaded By** Trishya Patel

File Name

4B565B42-A00A-4C95-BE46-4D4...







Description

Taken Date 2019/12/05 11:09:48

Upload Date 2019/12/05 11:09:50


Uploaded By Trishya Patel

File Name 4DB4523C-20ED-4E6F-945D-572... **Taken Date** 2019/12/04 13:58:58

Upload Date 2019/12/04 14:00:31 **Uploaded By** Trishya Patel

File Name

6203BD7F-2020-48D9-91E7-DFC...









Description

Taken	Date	2	
2019/1	2/04	09:06:10)

Upload Date 2019/12/05 07:19:11

Uploaded By Rick Lawrence

File Name DSC02648.JPG

Taken Date 2019/12/04 08:42:11

Upload Date 2019/12/04 08:42:24

Uploaded By Trishya Patel

File Name

DED068AB-8ED0-48AA-9831-C37...





Taken Date Uploaded By 2019/12/04 08:29:31 Trishya Patel **Upload Date File Name**


2019/12/04 08:29:36 3CD86A30-E9A8-485D-BA71-B3E... **Taken Date** 2019/12/04 08:29:20

Description

Upload Date 2019/12/04 08:29:26 **Uploaded By** Trishya Patel

File Name

8E25765F-4EA2-455E-959B-BD2F...











Description

Taken Date 2019/12/03 09:11:22

Upload Date 2019/12/04 07:38:04

Uploaded By Rick Lawrence

File NameDSC02633.JPG

Taken Date 2019/12/02 10:26:27

Upload Date 2019/12/03 07:37:10

Uploaded By
Rick Lawrence

File Name
DSC02624.JPG



Description

Upload Date

Description

Taken Date 2019/12/02 07:56:12

2019/12/02 07:56:16

Uploaded By Trishya Patel

File Name E188A440-87F9-4335-BB5E-563A...

Taken Date 2019/12/02 07:55:52

Upload Date 2019/12/02 07:55:56


Uploaded By Trishya Patel

File Name

15A1ED18-F4D3-4B0D-8EBA-A35...



Job #: 201802 Manchester Memorial Elementary School 43 Lincoln Street Manchester by the Sea, Massachusetts 01944

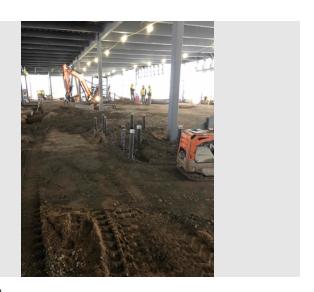

Description

Taken DateUploaded By2019/12/02 07:55:48Trishya Patel

Upload Date File Name

2019/12/02 07:55:53 823D909C-F397-4DC4-9A17-0A0...

Manchester Memorial Elementary School Monthly Construction Report Summary – December 2019

SECTION 3 - ATTACHMENTS
